PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

FRAC. SEC. 2, T 16N, R 29 W COUNTY WASHINGTON

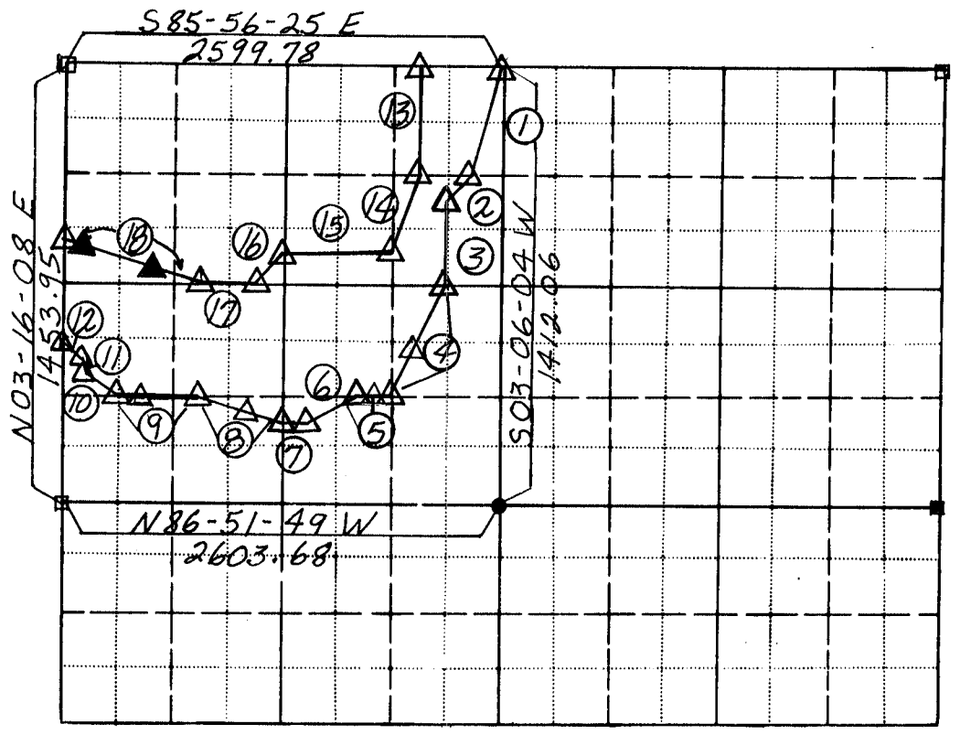

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		2310-1-12		1135.40	646,425.87	1,402,130.08	yielded to mahaffey survey
	1		S16-15-36 W	724.94			
		2310-1-13		1141.44	645,729.93	1,401,927.10	yielded to mahaffey survey
	2		S46-11-29 E	241.13			
		2310-1-14		1139.42	645,563.01	1,401,753.09	yielded to mahaffey survey
	3		S03-05-49 E	529.90			
		2310-1-15 2311-1		1210.61	645,033.68	1,401,729.030	yielded to mahaffey 28" ROD
	4		S29-01-38 W	402.97			

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____

COUNTY, ARKANSAS

Field Book No. 68-B-6 TRANSIT Date: _____
68-B-5 CHAIN
68-B-7 TRANSIT
68-B-8 CHAIN
68-B-4 LEVEL

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET _____ of _____

GN MN
1°10' 7°04'E

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 2, T 16 N, R 29 W COUNTY WASHINGTON

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		2311-1B			644,681.21	1,401,533.43	
	4		S29-01-38W	327.91			
		2311-2		1155.26	644,394.40	1,401,374.26	△ with 24" rod
	5		N86-59-38W	73.95			
		2311-2A		1167.24	644,398.27	1,401,300.49	△ "
	5		N86-59-38W	89.45			
		2311-3		1164.59	644,402.96	1,401,211.25	△ "
	6		S66-12-31W	365.35			
		2311-4		1156.20	644,255.64	1,400,877.11	△ "
	7		N87-00-57W	163.56			
		2311-5		1139.79	644,264.15	1,400,713.93	△ "
	8		N68-25-03W	195.14			
		2311-5A		1147.52	644,335.84	1,400,532.69	△ "
	8		N68-25-03W	322.49			
		2311-6		1136.74	644,454.33	1,400,233.17	△ "
	9		N86-58-56W	337.00			
		2311-6A		1144.82	644,472.04	1,399,896.97	△ "
	9		N86-58-56W	153.19			
		2311-7		1145.42	644,480.11	1,399,744.14	△ "
	10		N25-49-32W	138.75			
		2311-8		1135.43	644,604.84	1,399,683.77	△ "
	11		N13-09-01E	66.00			
		2311-9			644,669.07	1,399,698.78	△ "
	12		N59-20-03W	158.40			
		2311-10			644,749.76	1,399,562.70	△ "
		2310-1-4		1137.17	646,460.77	1,401,644.79	△ type in book not indicated
	13		S02-12-39W	766.65			
		2310-1-5		1138.24	645,695.37	1,401,615.24	△ "
	14		S21-51-20W	514.35			
		2310-1-6		1137.83	645,218.22	1,401,423.86	△ "
	15		N87-02-06W	660.00			
		2310-1-7		1143.81	645,252.40	1,400,764.10	△ "

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 2, T 16N, R 29W COUNTY WASHINGTON

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	16		S48-05-58W	233.44			
		2310-1-8		1136.57	645,096.49	1,400,590.33	△ type in book not indicated
	17		N86-55-58W	311.85			
		2310-2-1		1138.37	645,113.19	1,400,278.63	△ "
	18		N70-13-49W	301.61			
		2310-2-1A		1145.09	645,215.34	1,399,994.46	▲Conc. Mon.
	18		N70-13-49W	529.50			
		2310-2-1B		1144.30	645,394.65	1,399,495.58	▲ Conc. Mon.
	18		N70-13-49W	29.67			
		2310-2-2			645,404.70	1,399,467.62	
