PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 18, T 17N, R 28W COUNTY WASHINGTON

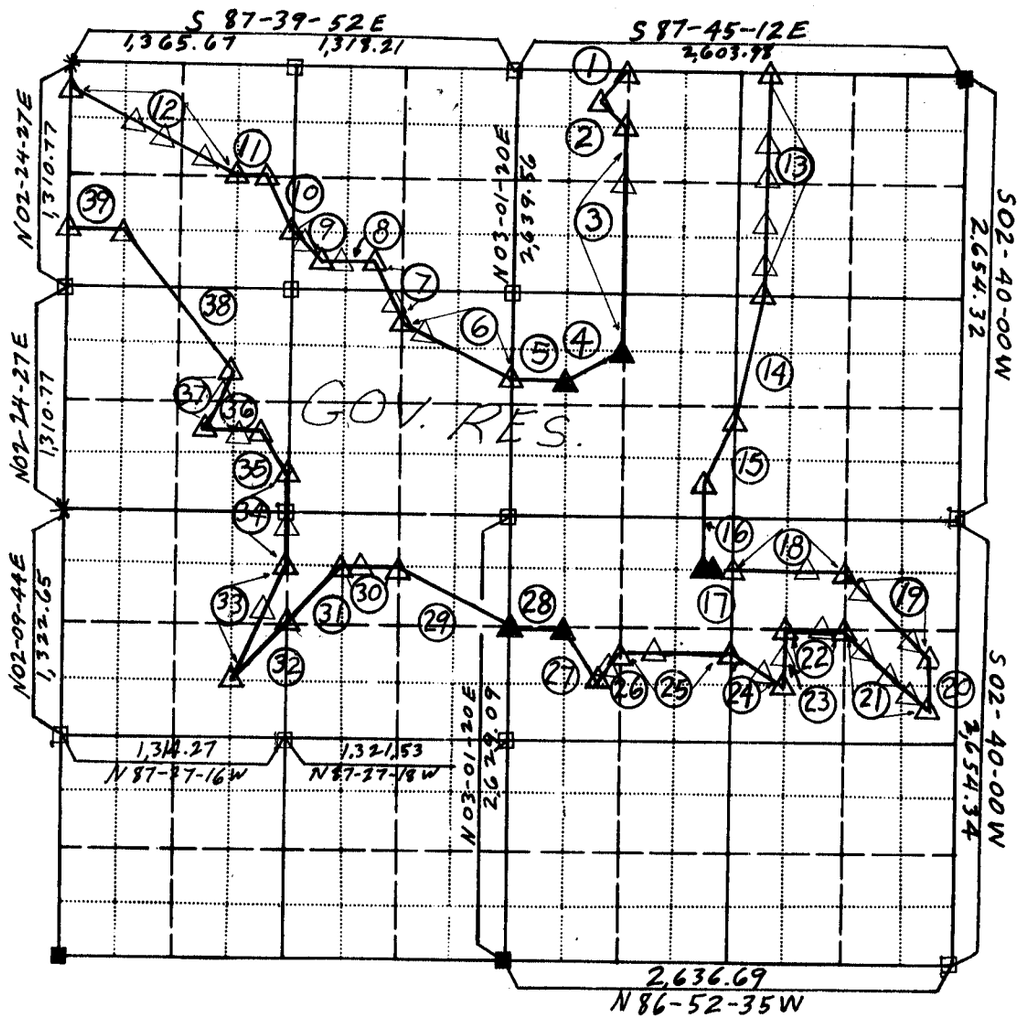

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		2119-3		1128.30	667,329.51	1,408687.11	
	1		S47-06-56W	233.34			
		2119-4		1134.76	667,170.71	1,408,516.12	
	2		S41-58-36E	230.65			
		2119-5		1126.64	666,999.52	1,408,670.54	
	3		S02-51-06W	324.49			
		2119-5A		1131.57	666,675.53	1,408,654.39	
	3		S02-51-06W	997.36			

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____

COUNTY, ARKANSAS

Field Book No. 67-B-116 TRANSIT Date: JAN 1968
67-B-117 CHAIN
67-B-119 TRANSIT
67-B-120 CHAIN
67-B-121 LEVEL
67-B-118 LEVEL

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 5

GN MN 1°10' 7°04'E

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 18, T 17N, R 28W COUNTY WASHINGTON

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		2119-6		1132.75	665,679.71	1,408,604.81	CONC MON
	4		S65-16-16W	372.97			
		2119-7		1138.86	665,523.59	1,408,265.72	CONC MON
	5		N87-33-18W	326.97			
		2119-8		1140.99	665,537.83	1,407,939.33	
	6		N60-50-19W	598.55			
		2119-8A		1160.34	665,829.49	1,407,416.65	
	6		N60-50-19W	137.15			
		2119-9		1161.65	665,895.96	1,407,296.69	
	7		N23-42-08W	100.04			
		2119-9A		1159.07	665,987.56	1,407,256.48	
	7		N23-42-08W	267.00			
		2119-10		1160.89	666,231.80	1,407,149.25	RESET MARCH 8
	8		N87-33-18W	237.84			
		2119-10A		1179.10	666,241.95	1,406,911.63	
	8		N87-33-18W	92.19			
		2119-11		1171.08	666,245.89	1,406,819.46	
	9		N42-22-08W	140.70			
		2119-11A		1190.99	666,349.84	1,406,724.64	
	9		N42-22-08W	91.01			
		2119-12 = 2118-1		1187.15	666,417.00	1,406,663.39	
	10		N24-24-46W	368.32			
		2118-2		1167.50	666,752.15	1,406,511.27	
	11		N87-38-52W	169.73			
		2118-3		1211.06	666,759.12	1,406,341.65	
	12		N61-53-40W	202.73			
		2118-3A		1228.59	666,855.63	1,406,163.83	
	12		N61-53-46W	250.18			
		2118-3B		1231.33	666,973.49	1,405,943.15	
	12		N61-53-40W	269.21			
		2118-3C		1213.07	667,100.31	1,405,705.41	
	12		N61-53-40W	408.79			
		2118-4		1227.28	667,295.77	1,405,346.48	

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 18, T - 17-N, R - 28-W COUNTY WASHINGTON

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		2125-1 = 2126-3		1181.87	667,295.73	1,409,497.70	
	13		S02-49-07 W	462.8.0			
		2125-1A		1184.15	666,833.75	1,409,474.97	
	13		S02-49-07W	175.77			
		2125-1B		1205.62	666,658.29	1,409,466.33	
	13		S02-49-07W	258.25			
		2125-1C		1221.17	666,400.50	1,409,453.63	
	13		S02-49-07W	246.98			
		2125-1D		1212.49	666,153.96	1,409,441.49	
	13		S02-49-07W	180.36			
		2125-2 = 2124-1		1211.32	665,973.92	1,409,432.62	
	14		S15-11-34 W	763.35			
		2124-2 = 2119-16			665,233.59	1,409,233.39	POINT NOT SET SEE PG.34 BK.67-B-116
	15		S24-23-56 W	445.57			
		2119-17		1180.26	664,827.81	1,409,049.33	
	16		S02-51-08 W	86.97			
		2119-17A		1195.03	664,740.93	1,409,045.00	
	16		S02-51-08 W	408.44			
		2119-18		1137.27	664,332.88	1,409,024.68	CONC MON
	17		S87-21-41E	83.77			
		2119-18A		1153.67	664,329.03	1,409,108.34	CONC MON
	17		S87-21-41 E	80.14			
		2119-19 = 2121-1		1154.79	664,325.34	1,409,188.38	
	18		S87-21-52 E	471.74			
		2121-1A		1147.59	664,303.64	1,409,659.53	
	18		S87-21-52 E	184.14			
		2121-2 = 2122-1		1169.72	664,295.18	1,409,843.44	
	19		S42-01-13E	188.82			
		2122-1A		1132.69	664,154.90	1,409,969.83	
	19		S42-01-13E	407.27			
		2122-1B		1145.02	663,852.32	1,410,242.47	
	19		S42-01-13E	103.02			
		2122-2		1147.00	663,775.78	1,410,311.44	
	20		S02-39-51W	331.64			

SWL FORM 136
REVISED FEB 66

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 18, T 17 N, R 28 W COUNTY WASHINGTON

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		2122-3		1139.40	663,444.42	1,410,296.02	
	21		N42-01-53W	154.87			
		2122-3A		1128.88	663,559.45	1,410,192.34	
	21		N42-01-53W	208.01			
		2122-3B		1146.51	663,713.95	1,410,053.08	
	21		N42-01-53W	157.20			
		2122-3C		1158.67	663,830.71	1,409,947.83	
	21		N42-01-53W	179.75			
		2122-4= 2121-3		1139.38	663,964.21	1,409,827.48	
	22		N87-19-10W	109.87			
		2121-3A		1164.25	663,969.35	1,409,717.71	
	22		N87-19-10W	218.20			
		2121-4		1162.18	663,979.56	1,409,499.70	
	23		S02-45-18W	143.32			
		2121-4A		1155.53	663,836.36	1,409,492.81	
	23		S02-45-18W	187.31			
		2121-5		1133.40	663,649.22	1,409,483.81	
	24		N60-33-15W	115.60			
		2121-5A		1145.85	663,706.06	1,409,383.13	
	24		N60-33-15W	251.76			
		2121-6= 2119-20		1153.77	663,829.86	1,409,163.88	
	25		N87-17-25W	456.91			
		2119-20A		1126.07	663,851.43	1,408,707.39	
	25		N87-17-25W	199.47			
		2119-21		1122.10	663,860.86	1,408,508.11	
	26		S47-43-24W	109.50			
		2119-21A		1138.48	663,787.18	1,408,427.06	
	26		S47-43-24W	123.35			
		2119-22		1129.20	663,704.17	1,408,335.77	
	27		N23-36-56W	242.23			
		2119-22A		1145.47	663,926.08	1,408,238.75	
	27		N23-36-56W	124.96			
		2119-23		1127.36	664,040.56	1,408,188.69	CONC MON
	28		N86-58-42W	327.93			

SHEET 4 of 5

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 18, T - 17-N, R - 28-W COUNTY WASHINGTON

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		2119-24		1146.26	664,057.73	1,407,861.12	CONC MON
	29		N60-49-25W	736.42			
		2119-25		1136.73	664,416.66	1,407,218.25	
	30		N87-18-15W	200.04			
		2119-25A		1141.07	664,426.07	1,407,018.44	
	30		N87-18-15W	130.44			
		2119-26		1129.27	664,432.20	1,406,888.16	
	31		S47-56-19W	468.08			
		2119-27 = 2120-1		1119.92	664,118.60	1,406,540.62	
	32		S47-50-18W	467.92			
		2120-2		1130.01	663,804.50	1,406,193.74	
	33		N29-31-15E	484.37			
		2120-2A		1140.14	664,225.93	1,406,432.37	
	33		N29-31-15E	254.86			
		2130-3 = 2119-28		1142.78	664,447.67	1,406,557.93	
	34		N03-04-33E	277.16			
		2119-28A		1160.53	664,724.37	1,406,572.79	
	34		N03-04-33E	216.90			
		2119-29		1145.52	664,940.91	1,406,584.42	
	35		N23-58-20W	367.82			
		2119-30		1140.77	665,277.06	1,406,435.34	
	36		N87-17-54W	125.74			
		2119-30A		1147.40	665,282.99	1,406,309.74	
	36		N87-17-54W	209.11			
		2119-31		1134.96	665,292.85	1,406,100.89	
	37		N29-54-29E	258.22			
		2119-31A		1138.05	665,516.65	1,406,229.62	
	37		N29-54-29E	111.26			
		2119-32		1129.70	665,613.08	1,406,285.09	
	38		N36-41-35W	1060.09			
		2119-33		1123.30	666,462.91	1,405,651.80	
	39		N87-31-19W	338.37			
		2119-34		1132.81	666,477.84	1,405,313.80	

SWL FORM 136
REVISED FEB 66
