BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SECTION 24, T 19N, R 28W COUNTY BENTON

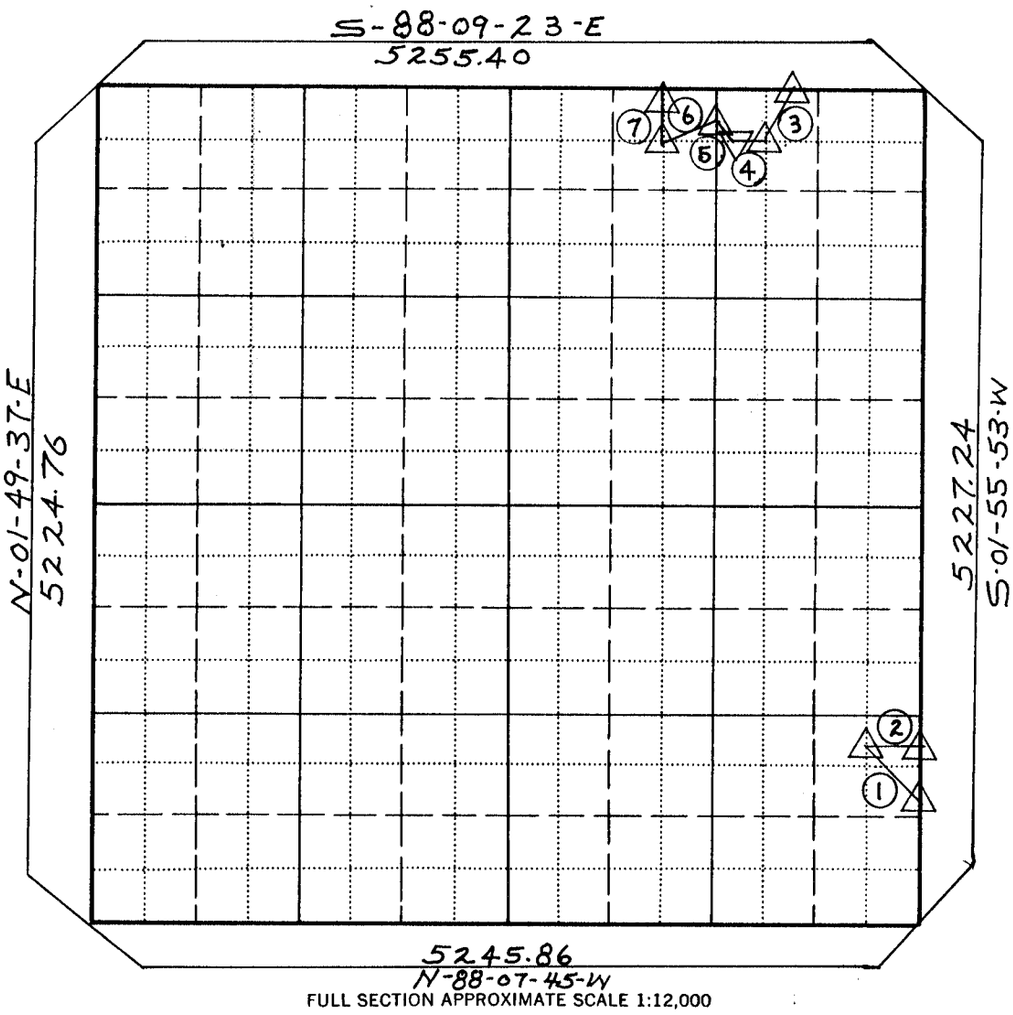

FULL SECTION APPROXIMATE SCALE 1:12,000

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	1109-1-3 = 1111-1		1184.73	719,605.58	1,439,170.31	
1		N-43-04-03-W	174.78			
	1111-1A			719,733.23	1,439,051.00	
1		N-43-04-03-W	112.45			
	1111-1B			719,815.35	1,438,974.23	
1		N-43-04-03 W	179.18			
	1111-2			719,946.22	1,438,851.92	
2		S-88-06-20-E	104.04			

Field Book No. 70B-9, 70B-10, 70B-12, 70B-13, 70B-14 Date: AUG 1970 OCT 1970

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION 24, T 19, R 28.

COUNTY, ARKANSAS

SURVEYOR REG. NO.

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 OF 2

GN MN 01-07-22 02-17-30

LEGEND
- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 2
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✳ OTHER

BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SEC. 24, T 19N, R 28W COUNTY BENTON

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1111-2A			719,942.78	1,438,955.94	
	2		S-88-06-20-E	225.96			
		1109-1-4 1111-3=		1182.45	719,935.30	1,439,181.85	
		1108-4			724,081.60	1,438,490.17	YIELD TO PREVIOUS SURVEY
	3		S-28-05-06W	351.97			
		1108-5			723,769.83	1,438,324.00	
	4		S-88-08-43-E	164.21			
		1108-6			723,775.14	1,438,160.00	
	5		N-44-00-40W	130.19			
		1108-6A			723,868.43	1,438,069.16	
	5		N-44-00-40W	113.17			
		835-8-1= 1108-7=			723,950.17	1,437,990.91	YIELD TO PREVIOUS SURVEY
	6		S-65-24-20W	132.42			
		835-8-1A			723,887.61	1,437,881.35	
	6		S-65-24-20W	315.31			
		835-8-2			723,789.90	1,437,667.92	
	7		N-01-48-21-E	315.31			
		835-8-2A			724,104.89	1,437,677.88	
	7		N-01-48-21-E	102.03			
		835-8-2B			724,206.82	1,437,681.09	
	7		N-01-48-21-E	83.19			
		835-8-3			724,289.92	1,437,683.70	IN SEC. 30

SHEET 2 of 2

SWL FORM 136
REVISED FEB. 66
