PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 5, T-20-N, R-27-W COUNTY BENTON

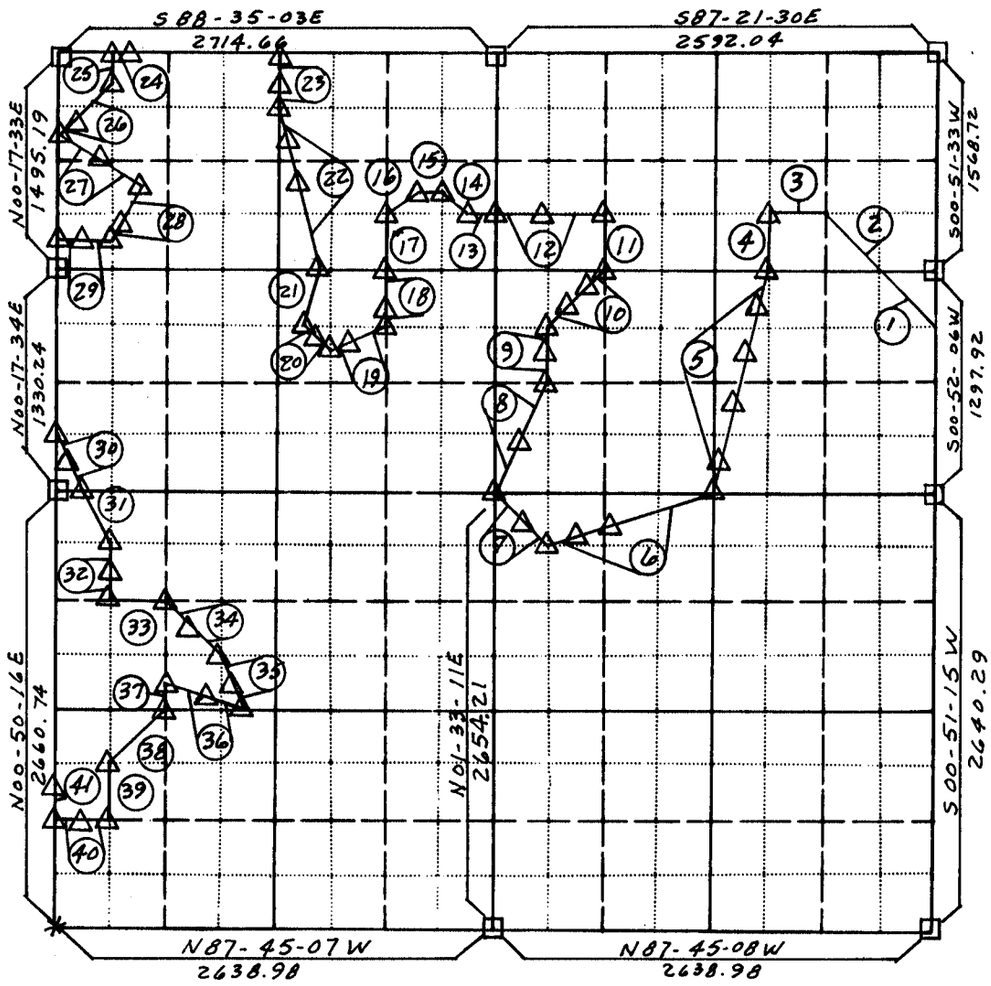

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		123-4= 126-1			769,651.73	1,450,853.85	NOT SET POINT IN LAKE
	1		N42-59-02W	468.92			
		126-2= 127-2-1			769,994.77	1,450,534.14	NOT SET POINT IN LAKE
	2		N37-53-41W	518.16			
		127-2-2			770,403.67	1,450,215.88	NOT SET POINT IN LAKE
	3		N86-52-49W	324.87			
		127-2-3			770,421.35	1,449,891.49	
	4		S00-58-21W	389.45			

Field Book No. ⅞ Bk. 67B-90, ch. Bk. 67B-91, Level Bk. 67B-94 Date: March 1967, June 1967

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____

COUNTY, ARKANSAS

_____

GN MN 07-17-30 01-05-30

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 6

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 5, T-20-N, R-27-W COUNTY BENTON

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		127-2-4= 126-3		1143.70	770,031.96	1,449,884.88	
	5		S15-02-16W	269.90			
		126-3A		1132.24	769,771.30	1,449,814.85	
	5		S15-02-16W	285.39			
		126-3B		1157.50	769,495.68	1,449,740.80	
	5		S15-02-16W	290.39			
		126-3C		1150.87	769,215.23	1,449,665.46	
	5		S15-02-16W	385.40			
		126-3D		1143.93	768,843.03	1,449,565.47	
	5		S15-02-16W	110.04			
		126-4= 127-1-1		1130.34	768,736.77	1,449,536.92	
	6		S73-43-18W	661.97			
		127-1-1A		1132.52	768,551.22	1,448,901.49	
	6		S73-43-18W	210.09			
		127-1-1B		1158.18	768,492.33	1,448,699.82	
	6		S73-43-18W	154.21			
		127-1-2		1152.75	768,449.10	1,448,551.79	
	7		N42-29-51W	174.67			
		127-1-2A		1153.99	768,577.89	1,448,433.79	
	7		N42-29-51W	294.66			
		127-1-3		1119.92	768,795.14	1,448,234.73	
	8		N27-34-35E	311.43			
		127-1-3A		1146.15	769,071.19	1,448,378.90	
	8		N27-34-35E	419.97			
		127-1-4		1163.02	769,443.45	1,448,573.32	
	9		N01-07-37E	198.02			
		127-1-4A		1153.10	769,641.43	1,448,577.21	
	9		N01-07-37E	133.49			
		127-1-5		1137.39	769,774.90	1,448,579.84	
	10		N46-37-40E	225.05			
		127-1-5A		1133.22	769,929.45	1,448,743.43	
	10		N46-37-40E	146.99			
		127-1-5B		1141.99	770,030.39	1,448,850.28	
	10		N46-37-40E	83.52			

SHEET 2 of 6

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 5, T-20-N, R-27-W COUNTY BENTON

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		127-1-6		1145.83	770,087.75	1,448,910.99	
	11		N01-05-10E	386.71			
		127-1-7		1179.31	770,474.39	1,448,918.32	
	12		N86-52-49W	380.48			
		127-1-7A		1144.67	770,495.10	1,448,538.40	
	12		N86-52-49W	269.25			
		127-1-8= 128-1-1		1170.13	770,509.75	1,448,269.55	
	13		N87-52-21W	168.63			
		128-1-2		1156.53	770,516.01	1,448,101.04	
	14		N39-48-10W	257.69			
		128-1-3		1157.17	770,713.98	1,447,936.08	
	15		N87-59-25W	168.80			
		128-1-4		1169.48	770,719.90	1,447,767.38	
	16		S42-52-23W	252.60			
		128-1-5		1162.69	770,534.78	1,447,595.52	
	17		S00-57-03W	382.10			
		128-1-6= 127-1-9		1137.17	770,152.73	1,447,589.18	
	18		S00-56-40W	267.31			
		127-1-9A		1131.47	769,885.46	1,447,584.77	
	18		S00-56-40W	65.22			
		127-1-10		1122.81	769,820.25	1,447,583.70	
	19		S65-44-19W	284.77			
		127-1-10A		1148.61	769,703.24	1,447,324.08	
	19		S65-44-19W	86.05			
		127-1-11		1147.15	769,667.88	1,447,245.63	
	20		N43-40-55W	82.47			
		127-1-11A		1149.82	769,727.52	1,447,188.67	
	20		N43-40-55W	157.01			
		127-1-12		1140.78	769,841.07	1,447,080.23	
	21		N15-04-22E	340.74			
		127-1-13= 128-2-1		1155.80	770,170.09	1,447,168.84	
	22		N11-41-28W	568.19			
		128-2-1A		1153.49	770,726.49	1,447,053.70	
	22		N11-41-28W	396.81			

SHEET 3 of 6

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 5, T-20-N, R-27-W COUNTY BENTON

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		128-2-1B		1173.71	771,115.07	1,446,973.29	
	22		N11-41-27W	207.65			
		128-2-2		1159.83	771,318.41	1,446,931.22	
	23		N00-44-08E	188.72			
		128-2-2A			771,507.11	1,446,933.64	
	23		N00-44-08E	190.61			
		128-2-3		1149.79	771,697.71	1,446,936.09	
		128-2-9		1164.69	771,721.59	1,445,975.71	
	24		N88-43-13W	57.32			
		128-2-10		1179.36	771,722.87	1,445,918.40	
	25		S00-24-22W	176.45			
		128-2-10A		1177.36	771,546.42	1,445,917.15	
	25		S00-24-22W	11.14			
		128-2-11		1177.18	771,535.28	1,445,917.07	
	26		S43-03-17W	409.21			
		128-2-11A		1175.08	771,236.27	1,445,637.70	
	26		S43-03-17W	89.93			
		128-2-12		1189.77	771,170.56	1,445,576.31	
	27		S52-10-02E	281.50			
		128-2-12A		1168.33	770,997.90	1,445,798.64	
	27		S52-10-02E	356.84			
		128-2-13		1144.94	770,779.03	1,446,080.47	
	28		S24-53-26W	296.35			
		128-2-13A		1163.48	770,510.21	1,445,955.74	
	28		S24-53-26W	110.72			
		128-2-14		1153.36	770,409.77	1,445,909.14	
	29		N87-45-10W	218.42			
		128-2-14A		1149.12	770,418.33	1,445,690.89	
	29		N87-45-10W	118.49			
		128-2-15 = 129-1		1138.74	770,422.98	1,445,572.49	

SHEET 4 of 6

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 5, T 20-N, R 27-W COUNTY BENTON

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		131-6		1152.61	769,238.42	1,445,566.44	
	30		S25-56-41E	178.41			
		131-6A		1177.77	769,077.99	1,445,644.50	
	30		S25-56-41E	199.11			
		131-7= 132-1		1181.00	768,898.94	1,445,731.61	
	31		S25-26-58E	375.83			
		132-2		1153.94	768,559.58	1,445,893.11	
	32		S00-55-37W	162.39			
		132-2A		1171.02	768,397.21	1,445,890.48	
	32		S00-55-37W	170.10			
		132-3		1173.04	768,227.13	1,445,887.73	
	33		S87-39-27E	333.00			
		132-4		1148.75	768,213.52	1,446,220.45	
	34		S43-20-09E	200.79			
		132-4A		1153.90	768,067.48	1,446,358.25	
	34		S43-20-09E	274.68			
		132-5		1143.31	767,867.69	1,446,546.75	
	35		S25-11-33E	265.56			
		132-5A		1141.58	767,627.39	1,446,659.79	
	35		S25-11-33E	108.99			
		132-6		1135.41	767,528.77	1,446,706.18	
	36		N69-21-51W	263.38			
		132-6A		1146.19	767,621.59	1,446,459.67	
	36		N69-21-51W	265.10			
		132-7		1170.17	767,715.02	1,446,211.61	
	37		S01-01-01W	166.19			
		132-8		1143.73	767,548.86	1,446,208.66	
	38		S46-34-17W	464.12			
		132-9		1158.76	767,229.80	1,445,871.60	
	39		S00-41-12W	340.40			
		132-10		1131.31	766,889.42	1,445,867.52	
	40		N87-40-36W	234.56			
		132-10A		1134.37	766,898.93	1,445,633.15	
	40		N87-40-36W	96.00			

SHEET 5 of 6

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 5, T-20-N, R-27-W COUNTY BENTON

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		132-11		1127.93	766,902.82	1,445,537.23	
	41		N00-54-09E	164.43			
		132-12		1146.40	767,067.23	1,445,539.82	

SHEET 6 of 6

SWL FORM 136
REVISED FEB. 66
