BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SECTION 14 , T 20N , R 27W COUNTY Carroll

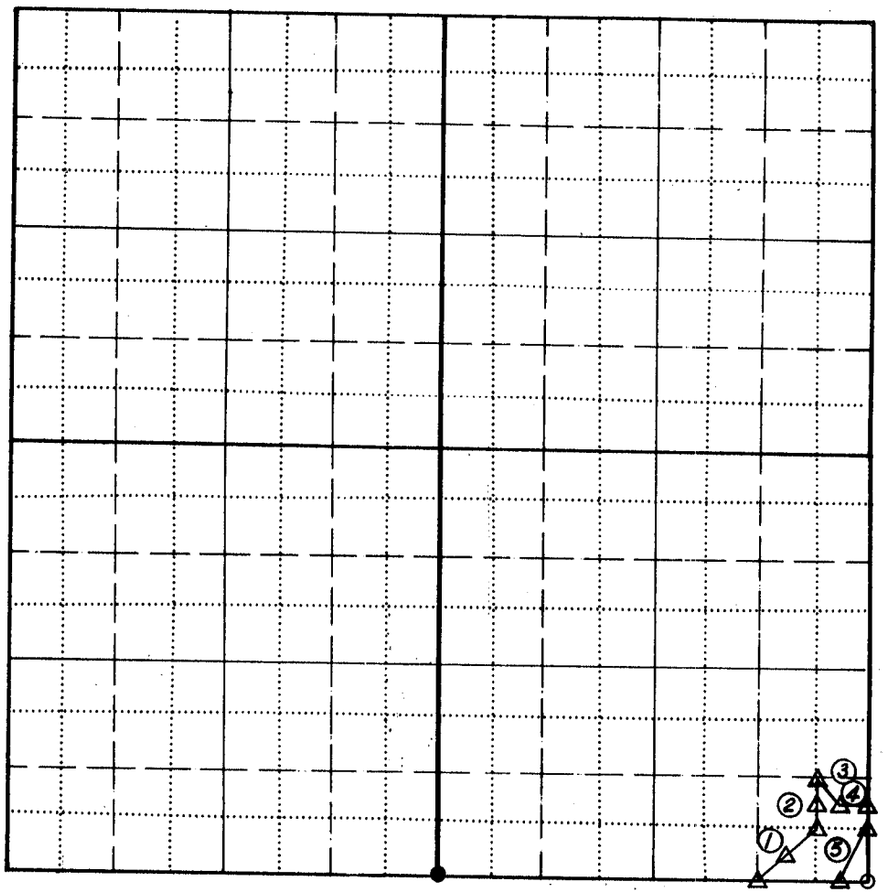

FULL SECTION APPROXIMATE SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		320-3 = 317-1		1,168.84	754,738.86	1,465,626.58	
	1		N45-08-05E	368.25			
		317-1-A		1,172.81	754,998.66	1,465,887.60	
	1		N45-08-05E	90.98			
		317-2		1,163.35	755,062.84	1,465,952.09	
	2		N00-13-12 W	212.31			
		317-2A		1,168.54	755,274.99	1,465,951.28	

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____,

T _____, R _____

COUNTY, ARKANSAS

Field Book Number 71-B-3 & 71-B-4 Date Aug. 1971

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK

CORPS OF ENGINEERS

SHEET 1 OF 2

GN MN

LEGEND
- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 3
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✱ OTHER

SWL FORM 1
REVISED JUNE 1971

BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SEC. 14, T 20N, R 27W COUNTY Carroll

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		317-2-A		1,168.54	755,274.99	1,465,951.28	
	2		N 00-13-12 W	117.25			
		317-3		1,161.65	755,392.15	1,465,950.83	
	3		S 44-48-43 E	236.24			
		317-4		1,130.00	755,224.36	1,466,117.52	
	3		S 89-01-29 E	159.98			
		317-4-A		1,156.70	755,221.63	1,466,277.62	
	4		S 89-01-29 E	5.39			
		317-5 = 319-1			755,222.11	1,466,283.01	
		319-6 = 317-6			755,056.74	1,466,284.74	
			S 26-56-25 W	365.87			
		317-7 = 320-4			754,730.48	1,466,119.20	

SHEET 2 of 2

SWL FORM 136
REVISED FEB. 66
