PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

CONTRACT NO. DACW03-67-C-0101

SEC. 13, T 20-N, R 28-W COUNTY BENTON

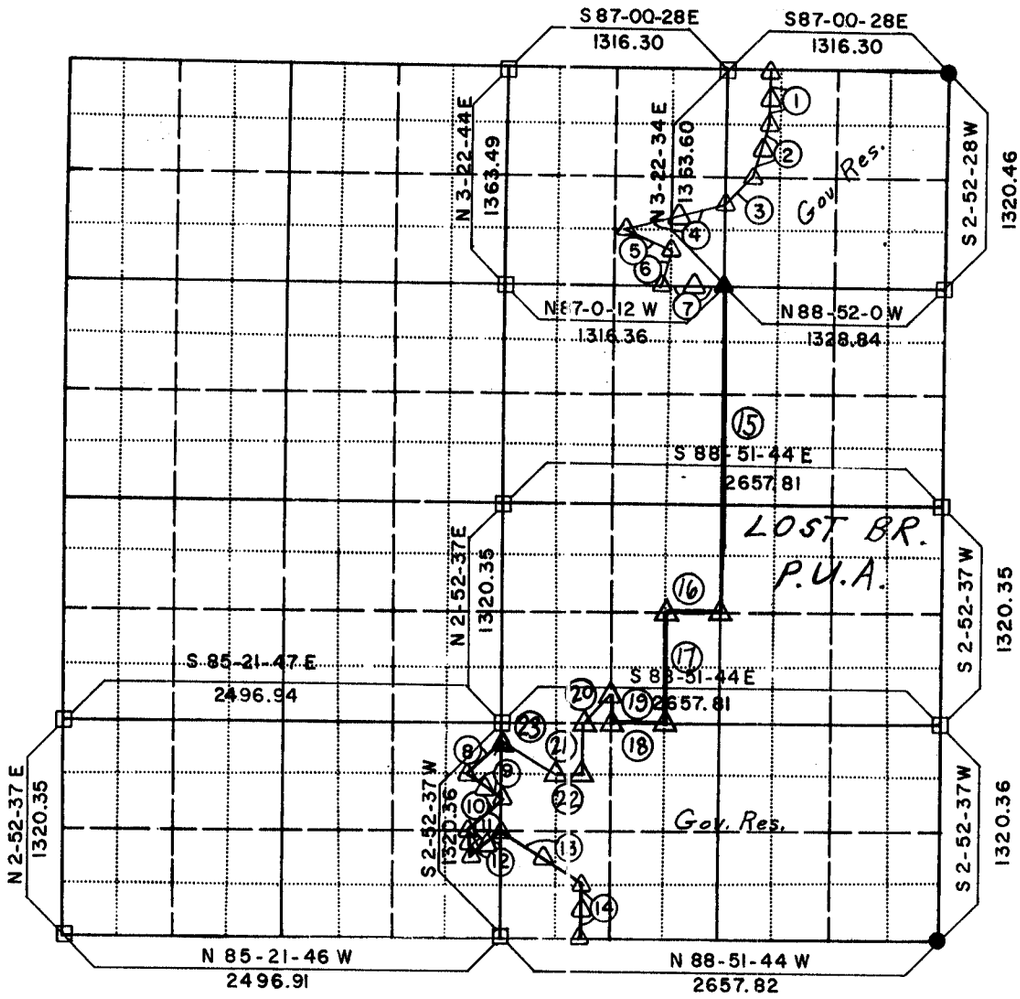

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		221-5			761,145.38	1,439,273.05	
			S87-0-27E	246.80			
		221-6 222-1		1136.08	761,132.50	1,439,519.52	
	1		S3-17-07W	101.80			
		222-1A		1138.43			
	1		S3-17-07W	137.08			
		222-2		1133.75	760,794.18	1,439,500.10	
	2		S16-55-09W	221.83			

Field Book No. Angles 867-34 Dist. 867-35 Levels 867-37+ 867-40 Date: '67

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION 13, T 20-N, R 28-W.

BENTON COUNTY, ARKANSAS

Lemuel H Tull

LEMUEL H. TULL P.E. REG. NO. 1786

CRAFTON AND TULL CONSULTING ENGINEERS, INC.
UNDER THE SUPERVISION OF
U.S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 4

GN MN 1°11'35" 7°30' JAN-67

LEGEND
- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS
CONTRACT NO. DACW03-67-C-0101

SEC. 13, T 20-N, R 28-W COUNTY BENTON

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		222-2A		1147.51			
	2		S16-55-09W	128.69			
		222-3		1146.30	760,458.83	1,439,398.09	
	3		S46-51-28W	120.54			
		222-3A		1156.79			
	3		S46-51-28W	119.61			
		222-4 226-1		1156.67	760,294.61	1,439,222.86	
	4		S76-32-20W	212.13			
		226-1A		1167.75			
	4		S76-32-20W	389.55			
		226-2		1150.37	760,154.55	1,438,637.71	
	5		S52-15-17E	299.01			
		226-3		1148.08	759,971.51	1,438,874.15	
	6		S29-04-16W	189.76			
		226-4		1155.12	759,805.66	1,438,781.95	
	7		S87-14-44E S87-0-10E	135.62			Field survey Section Breakdown
		226-4A		1134.42			
	7		S87-14-44E S87-0-10E	273.50 275.74			Field Survey Section Breakdown
		226-5 401-1		1131.71	759,784.15	1,439,192.75	Conc. Mk. stamped 401-2 by USCE
		400-9 414-5-1			757,008.31	1,437,723.28	Yield to brass cap Stamped 400-1 by USCE
	8		S47-40-38W S47-06-57W	231.54 223.68			Field Survey Section Breakdown
		414-5-2		1167.32	756,856.09	1,437,559.38	
	9		S39-41-17E	116.68			
		414-5-2A		1162.44			
	9		S39-41-17E	113.91			
		414-5-3 414-6-1		1146.32	756,678.64	1,437,706.64	
	10		S47-06-20W	223.64			
		414-6-2		1143.77	756,526.42	1,437,542.80	
	11		S2-52-34W	75.56			

SHEET 2 of 4

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

CONTRACT NO. DACW03-67-C-0101

SEC. 13, T 20-N, R 28-W COUNTY BENTON

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION / NORTH	POSITION / EAST	REMARKS
		414-6-2A		1175.68			
	11		S2-52-34W	89.48			
		414-6-3		1197.56	756,361.58	1,437,534.52	
	12		N47-06-14E	109.78			
		414-6-3A		1178.81			
	12		N47-06-14E	113.85			
		414-6-4 400-10		1155.09	756,513.80	1,437,698.35	
	13		S54-49-17E	183.32			
		400-10A		1174.73			
	13		S54-49-17E	406.08			
		400-11		1153.91	756,174.23	1,438,180.10	
*	14		S 0·40·11 E S 0·38·30 E	166.60			FIELD SURVEY OFFICE CALCULATION
		400-11A		1155.37			
*	14		S 0·40 11 E S 0·38·30 E	130.38 130.24			FIELD SURVEY OFFICE CALCULATION
		400-12 414-1-1		1146.16	755,876.97	1,438,183.43	YIELD TO PREVIOUS SURVEY
							IN Sec. 24
		400-11			756,174.23	1,438,180.10	SECTION BREAKDOWN
*	14		S2·52·39W	330.10			
		400-12 414-1-1			755,844.55	1,438,163.53	SECTION BREAKDOWN
		401-2			759,784.15	1,439,192.75	
	15		S02-52-37W	1,980.54			
		400-9= 401-1			757,806.11	1,439,083.34	
	16		N88-51-44W	332.23			
		400-8			757,812.70	1,438,761.18	
	17		S02-52-37W	660.18			
		400-7			757,153.35	1,438,728.04	
	18		N88-51-44W	332.23			
		400-6			757,159.95	1,438,395.88	
	19		N02-52-36E	165.04			
		400-5			757,324.79	1,438,404.17	

BY C. of E.
LOST BRIDGE
P.U.A.

SHEET 3 of 4

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

CONTRACT NO. DACW03-67-C-0101

SEC. 13, T 20-N, R 28-W COUNTY BENTON

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		400-5			757,324.79	1,438,404.17	
	20		S47-11-12W	237.69			
		400-4			757,163.25	1,438,229.80	
	21		S02-52-38W	330.09			
		400-3			756,833.58	1,438,213.24	
	22		N88-51-44W	166.11			
		400-2			756,836.88	1,438,047.15	
	23		N62-06-26W	366.45			
		400-1			757,008.31	1,437,723.28	

BY C of E
LOST BRIDGE
P.U.A.

SHEET 4 of 4

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

CONTRACT NO. DACW03-67-C-0101

SEC. 13, T 20-N, R 28-W COUNTY BENTON

EASEMENTS

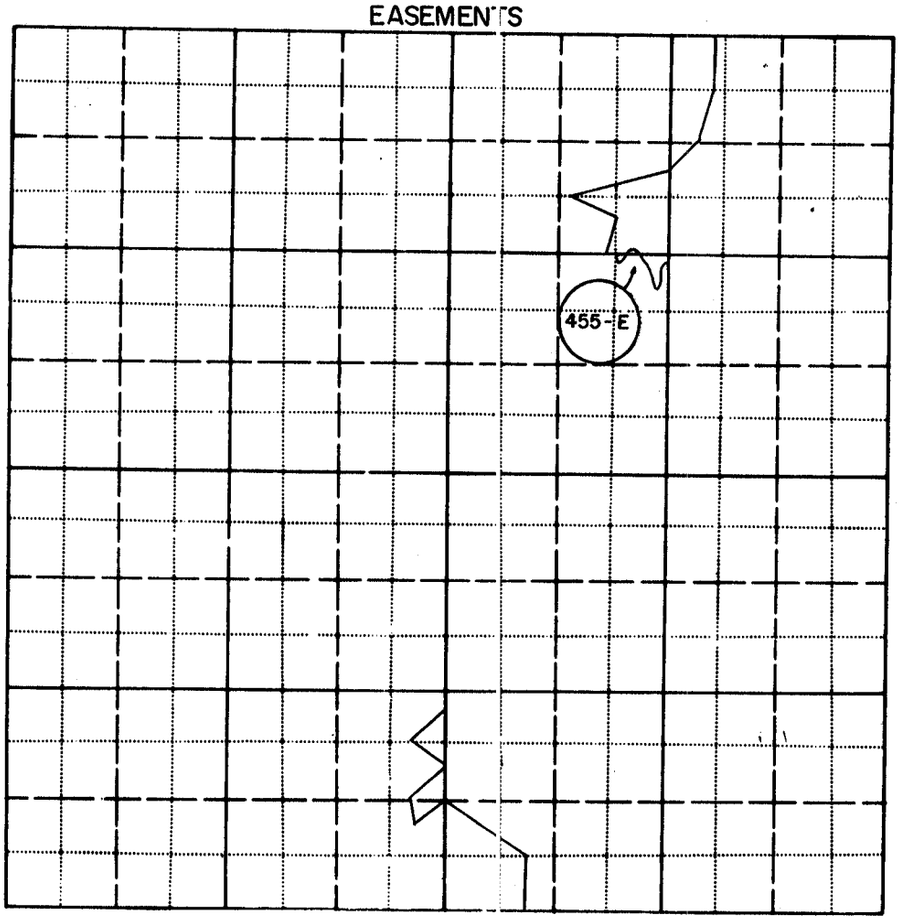

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE	ELEVATION	POSITION		REMARKS
			GRID BEARING	DISTANCE	NORTH	EAST	

Field Book No. _____ Date: _____

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION 13, T 20-N, R 28-W.

BENTON COUNTY, ARKANSAS

Lemuel H. Tull

LEMUEL H. TULL P.E. REG. NO. 1786

CRAFTON AND TULL CONSULTING ENGINEERS, INC.
UNDER THE SUPERVISION OF
U.S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of _____

GN MN 1°11'35" 7°30' JAN-67

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER
