BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SECTION 14, T 20N, R 28W. COUNTY BENTON

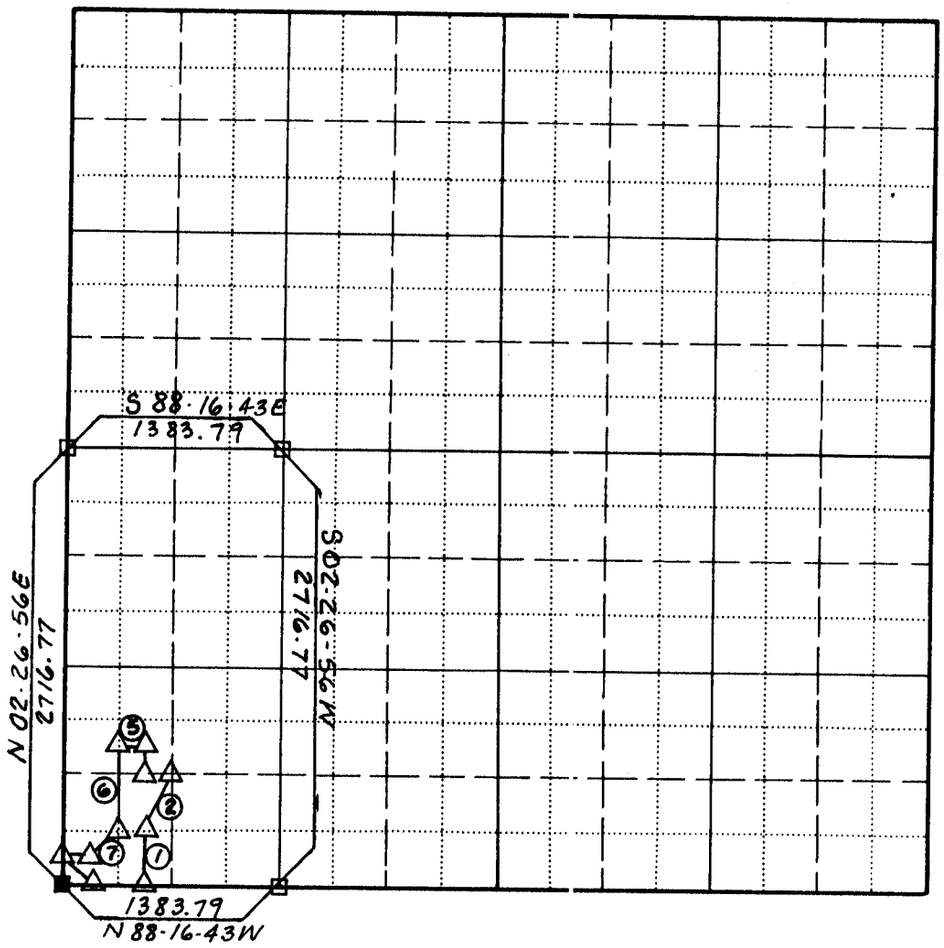

FULL SECTION APPROXIMATE SCALE 1:12,000

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	501-8 500-1		1181.04	756,375.03	1,430,338.45	
1		N02.27.01E	143.50			
	500-1A		1172.32	756,538.40	1,430,344.59	
1		N02.26.57E	196.10			
	500-2		1144.30	756,734.32	1,430,352.96	
2		N 29.16.53E	383.06			
	500-3		1194.87	757,068.44	1,430,540.32	
3		N88.17.12W	81.90			

Field Book No. 71B-5, 6 / 71B-8 Date: 1972 / 1972

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

COUNTY, ARKANSAS

SURVEYOR REG. NO.

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 OF 2

GN MN

LEGEND
- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 2
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✳ OTHER

BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SECTION 14 , T 20N , R 28W COUNTY BENTON

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	500-3A		1181.65	757,070.88	1,430,458.45	
3		N91-17-16W	91.07			
	500-4		1144.65	757,073.60	1,430,367.42	
4		N02-26-25E	169.80			
	500-5		1150.87	757,243.25	1,430,374.65	
5.		N88-17-55W	172.97			
	500-6		1145.00	757,248.39	1,430,201.76	
6		S02-26-16W	110.71			
	500-6A		1147.68	757,137.78	1,430,197.05	
6		S02-26-12W	398.69			
	500-7		1142.37	756,739.45	1,430,180.10	
7		S47-35-23W	243.91			
	500-8		1170.99	756,574.95	1,430,000.02	
8		N88-18-42W	172.97			
	500-9		1200.04	756,580.04	1,429,827.12	
9		S43-28-46E	240.84			
	500-10 = 501-9		1143.95	756,405.28	1,429,992.84	

SHEET 2 OF 2

SWL FORM 136
REVISED OCT. 1971
