PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 30, T -8-N, R -20-W COUNTY POPE

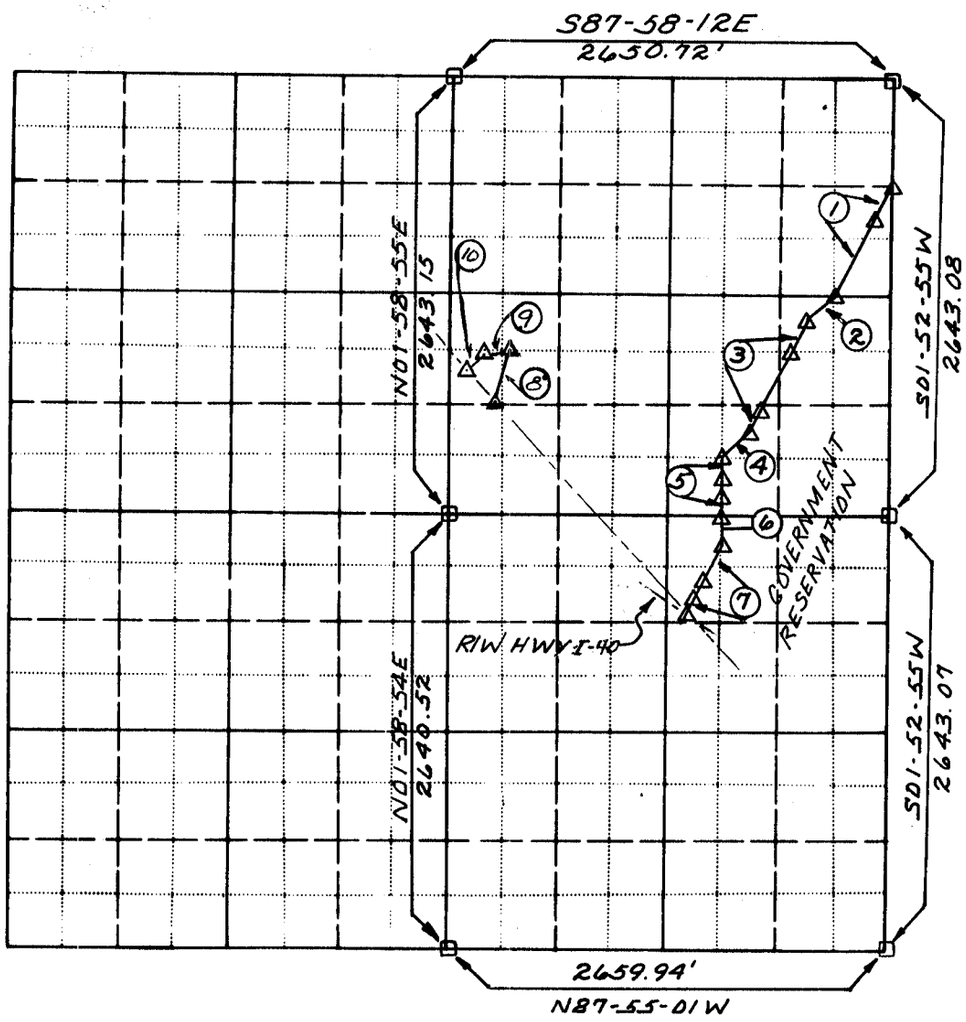

FULL SEC APPROX SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION / NORTH	POSITION / EAST	REMARKS
		215-1		371.73	361,426.61	1,655,534.88	
	1		S28-33-46W	226.63'			
		215-1A		359.65	361,227.56	1,655,426.52	
	1		S28-33-46W	511.93'			
		215-2= 217-1		341.45	360,777.94	1,655,181.76	
	2		S47-04-22W	233.79'			
		217-2		356.77	360,618.71	1,655,010.57	
	3		S26-26-49W	191.66'			

Field Book No. 67D 11&12 Date: Sept. 1967
73D-8 Nov. 1973

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____
COUNTY, ARKANSAS

GN MN 0°43'-04" 6°05E

LEGEND

- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 3
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✱ OTHER

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 2

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 30, T 8-N, R 20-W COUNTY POPE

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		217-2A		357.70	360,447.11	1,655,002.21	
	3		S26-26-49W	424.21'			
		217-2B		371.37	360,067.29	1,654,813.28	
	3		S26-26-49W	110.45'			
		217-3= 216-1		369.60	359,968.40	1,654,687.09	
	4		S51-57-13W	255.70'			
		216-2		369.61	359,810.81	1,654,485.72	
	5		S01-55-11W	78.76'			
		216-2A		380.23	359,732.09	1,654,483.08	
	5		S01-55-11W	71.55'			
		216-2B		387.30	359,660.58	1,654,480.68	
	5		S01-53-11W S01-54-37W	180.08' 180.18'			Comp. Bearing & DIST. Field Bearing & DIST.
		219-1= 250-2		387.35	359,480.61	1,654,474.65	Tie Point
	6		S01-55-11W	165.13'			
		219-2		366.11	359,315.57	1,654,469.12	
	7		S28-38-11W	220.29'			
		219-2A		376.50	359,122.23	1,654,363.55	
	7		S28-38-11W	152.55'			
		219-2B		380.88	358,988.34	1,654,290.44	
	7		S28-38-11W	53.29'			
		219-2C		376.93	358,941.57	1,654,264.90	I-40 R/W Fence
		211-1			360,267.81	1,653,088.64	Type III I-40 R/W Fence
	8		N20-30-13E	267.36			
		211-2			360,518.23	1,653,182.29	Type III
	9		N87-59-09W	166.06			
		211-3			360,524.07	1,653,016.33	Type III
	10		S47-08-43W	134.56			
		211-4			360,432.55	1,652,917.69	Type III I-40 R/W Fence

SHEET 2 of 2

SWL FORM 136
REVISED FEB. 66
