PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 20, T -8-N, R -21-W COUNTY POPE

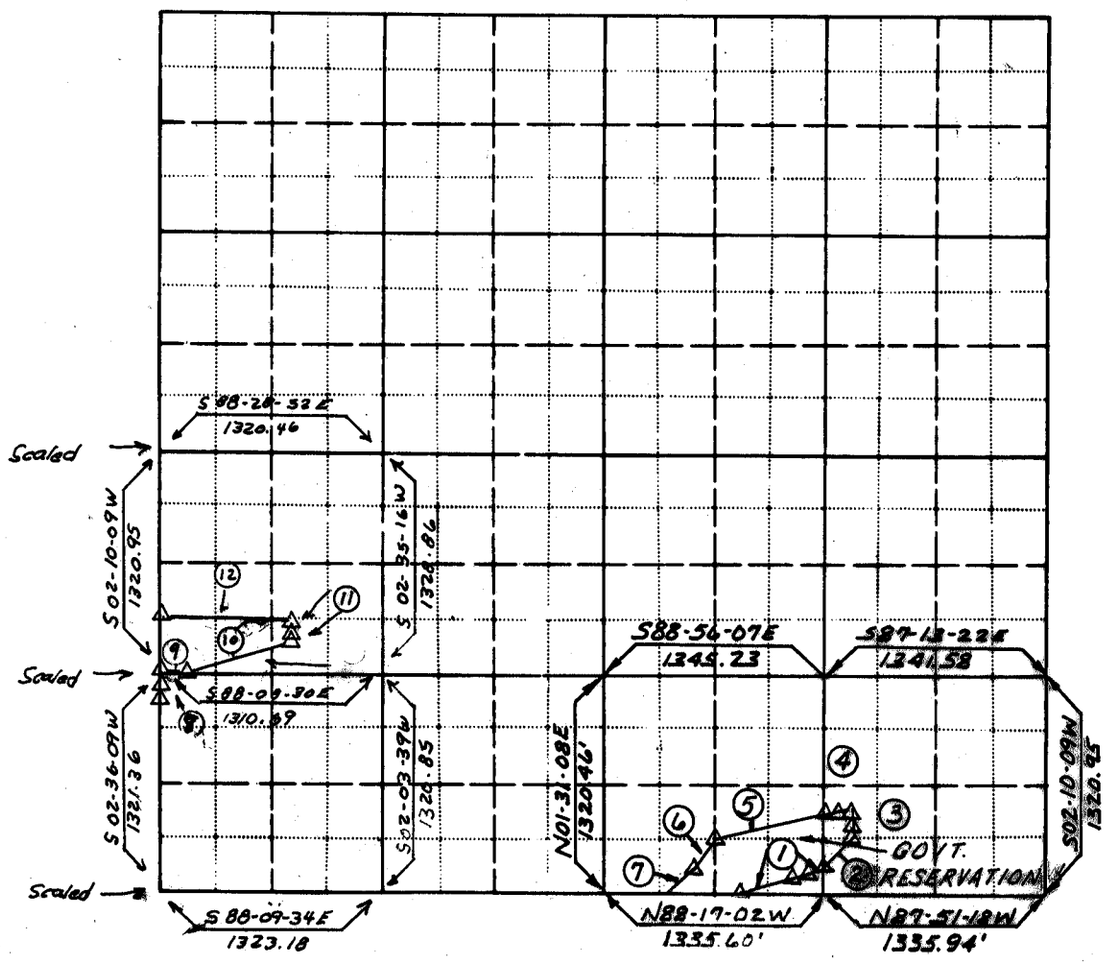

FULL SEC. APPROX. SCALE 1:12,000

COURSE 3 REVISED MAY '05

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION / NORTH	POSITION / EAST	REMARKS
		520-2= 522-1		341.27	362,965.06	1,626,812.44	
	1		N73-22-03E	394.65'			
		522-1A		349.37	363,078.02	1,627,190.58	
	1		N73-22-03E	66.65'			
		522-1B		352.98	363,097.10	1,627,254.44	
	1		N73-22-03E	69.07'			
		522-2= 521-1		357.18	363,116.87	1,627,320.62	
	2		N47-09-04E	235.51'			

Field Book No. 67D23 & 24 / 67D-25 / 73 D-17 & 18 Date: Nov. 67 AUG 73

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____

COUNTY, ARKANSAS

GN MN 0°43'04" 6°05'E

LEGEND

- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 3
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✱ OTHER

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 2

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 20, T -8-N, R -21-W COUNTY POPE

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		521-2		349.83	363,277.03	1,627,493.28	
	3		N01-57-34E	100.74'			
		521-2A-1		347.91	363,377.71	1,627,496.72	REPLACED 2 008 NEW COORD & ELEV. *
	3		N01-57-34E	66.00'			
		521-3			363,443.67	1,627,498.98	Fell in Creek Not set
	4		N87-37-06W	35.00'			
		521-3A		348.06	363,445.12	1,627,464.01	
	4		N87-37-06W	132.26'			
		521-4= 522-3		347.34	363,450.62	1,627,331.87	
	5		S77-33-43W	690.58'			
		522-4= 523-1		347.66	363,301.88	1,626,657.50	
	6		S41-14-23W	259.32'			
		523-2= 519-4		341.22	363,106.88	1,626,486.55	
	7		S50-10-05W	246.69'			
		519-4A		343.75	362,948.87	1,626,297.11	
	7		S50-10-05W	201.54'			
		519-5		340.37	362,819.77	1,626,142.34	This point in Sec. 29
		528-1-6		389.763	364,228.66	1,623,388.01	
	8		N 02-38-32 E	65.57			
		528-1-6A		368.084	364,294.12	1,623,391.03	
	8		N 02-38-32 E	99.60			
		525-1 = 528-1-7		341.287	364,393.56	1,623,395.62	
	9		S 87-33-42 E	155.16			
		℄ R.R. 525-2		353.817	364,386.93	1,623,550.65	
	10		N 35-01-15 E	715.12			
		525-3		357.096	364,571.63	1,624,241.50	
	11		N 01-50-31 W	51.12			
		525-3 A		347.971	364,622.72	1,624,239.85	
	11		N 01-50-31 W	74.67			
		525-4		346.883	364,697.34	1,624,237.45	CONCRETE MONUMENT
	12		N 88-11-32 W	829.54			
		525-5= 527-2-1		344.105	364,723.36	1,623,408.36	CONCRETE MONUMENT

* 521-2A COULD NOT BE RESET AT ORIGINAL LOCATION
REPLACED BY 521-2A-1

SHEET 2 of 2

SWL FORM 136
REVISED FEB. 66
