PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 8, T-8-N, R-22-W COUNTY JOHNSON

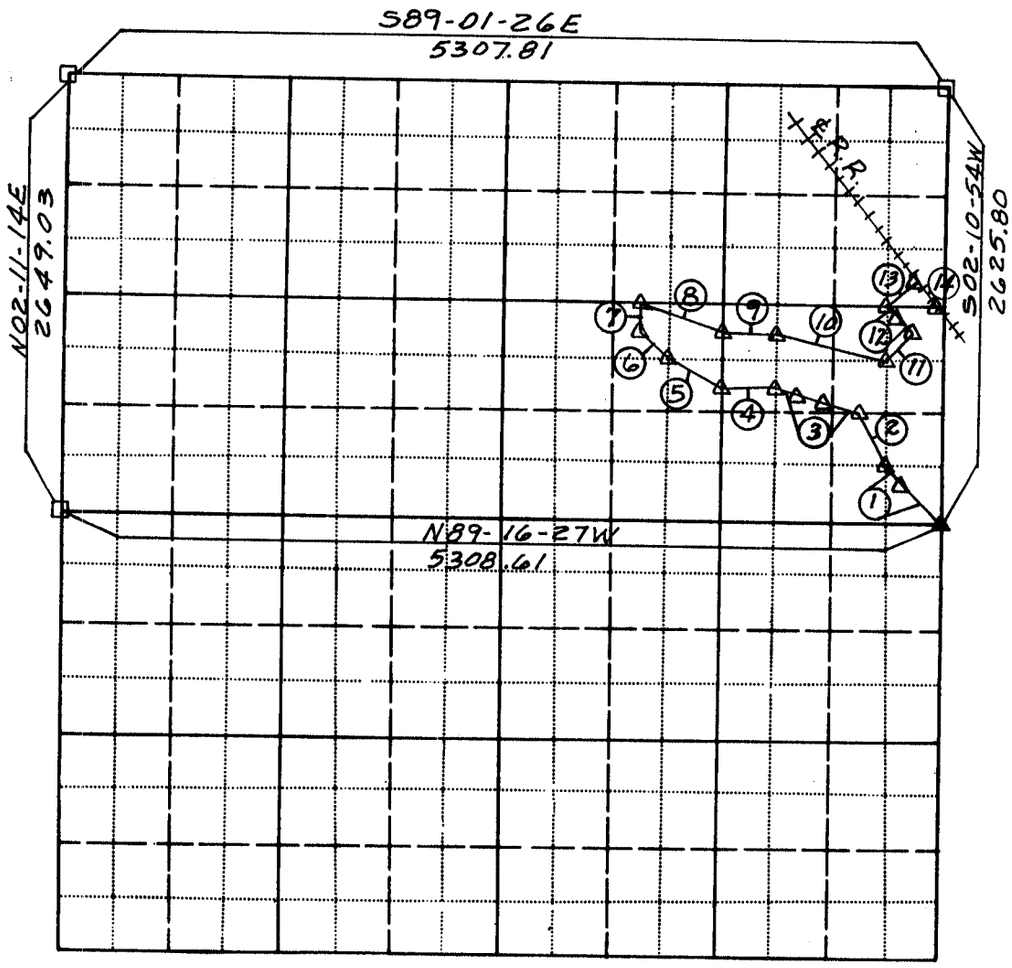

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		827-3		—	376,866.98	1,597,090.51	
	1		N43-52-10W	326.33			
		828-9A		349.84	377,102.28	1,596,864.55	
	1		N43-52-10W	134.54			
		828-9		344.55	377,199.15	1,596,771.42	
	2		N24-56-44W	364.30			
		828-8		345.27	377,528.87	1,596,618.04	
	3		N70-53-05W	225.44			

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION 8, T 8N, R 22W.

COUNTY, ARKANSAS

Field Book No. 69-D-26&27 Date: Oct. 1969
Level Book No. 690-33

GN MN 0°48'23" 06°39'

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 2

BOUNDARY SURVEYS
LAKE DARDANELLE
ARKANSAS RIVER, ARKANSAS

SECTION 8 , T-8-N , R-22-W COUNTY JOHNSON

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	828-7B		345.04	377,602.75	1,596,405.09	
3		N70-53-05W	142.49			
	828-7A		343.28	377,649.41	1,596,270.46	
3		N70-53-05W	152.16			
	828-7		343.47	377,699.19	1,596,126.70	
4		N89-19-18W	331.77			
	828-6= 829-5		346.22	377,703.12	1,595,794.76	
5		N62-41-01W	366.78			
	829-4		344.99	377,871.36	1,595,469.04	
6		N43-52-44W	230.90			
	829-3		347.53	378,037.59	1,595,309.18	
7		N02-01-03E	164.61			
	829-2		344.62	378,201.73	1,595,314.96	
8		S70-54-25E	520.47			
	829-1= 828-5		342.80	378,031.45	1,595,806.88	
9		S89-21-22E	331.76			
	828-4		343.89	378,027.73	1,596,138.42	
10		S75-23-05E	679.79			
	828-3		339.72	377,856.20	1,596,796.19	
11		N46-35-12E	236.14			
	828-2		343.21	378,018.17	1,596,967.38	
12		N44-00-31W	230.65			
	828-1= 830-3		354.36	378,183.86	1,596,807.33	
13		N34-04-21E	188.46			
	830-2A		346.83	378,339.61	1,596,912.70	
13		N34-04-21E	53.56			
	830-2		—	378,383.84	1,596,942.61	Tack in tie ℄ R/R Track
14		S36-59-39E	251.71			
	830-1		—	378,182.52	1,597,094.29	1"x2" Stake ℄ R/R Track

SHEET 2 OF 2

SWL FORM 136
REVISED OCT. 1971
