BOUNDARY SURVEYS
LAKE DARDANELLE
ARKANSAS RIVER, ARKANSAS

SECTION 24 ,T 8N ,R 22W COUNTY POPE

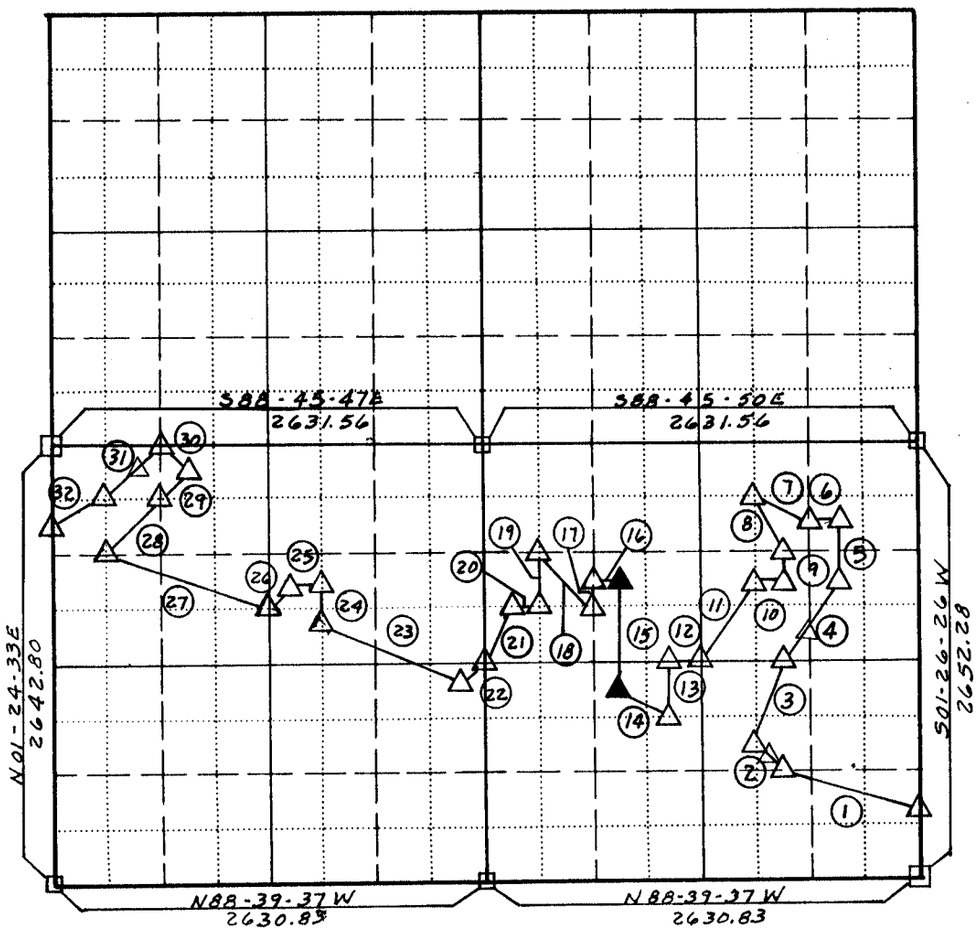

FULL SECTION APPROXIMATE SCALE 1:12,000

(DELEWARE QUAD)

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	711-1		344.36	363,593.17	1,617,882.60	
1		N71-27-17W	859.42			
	711-2		338.81	363,866.51	1,617,067.81	
2		N43-25-35W	85.16			
	711-2A		342.49	363,928.33	1,617,009.27	
2		N43-25-35W	48.00			
	711-2B		341.52	363,963.18	1,616,976.28	
2		N43-25-35W	100.00			

Field Book No. 73D-11, 73D-19, 73D-20 Date: 1973

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION 24, T 8N, R 22W.

COUNTY, ARKANSAS

SURVEYOR REG. NO.

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 OF 3

GN MN

LEGEND
- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 2
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✱ OTHER

BOUNDARY SURVEYS
LAKE DARDANELLE
ARKANSAS RIVER, ARKANSAS

SECTION 24 , T 8N , R 22W COUNTY POPE

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	711-3		—	364,036.08	1,616,906.67	Under Water
3		N 19-40-27E	349.30			
	711-3A		347.71	364,365.12	1,617,025.45	
3		N19-40-27E	174.57			
	711-4		340.60	364,529.63	1,617,084.27	
4		N34-49-10E	350.34			
	711-4A		351.07	364,817.51	1,617,284.51	
4		N34-49-10E	246.47			
	711-5		351.56	365,020.05	1,617,425.37	TYPE III FOUND 1/99
5		N01-22-33E	331.41			
	711-6		359.~~26~~ 40	365,351.53	1,617,433.33	TYPE III RESET 1/99
6		N88-48-38W	164.47			
	711-7		354.62	365,354.95	1,617,269.04	TYPE III FOUND 1/99
7		N 62-03-09 W	367.82			
	711-8		346.10	365,527.23	1,616,944.31	TYPE III FOUND 1/99 (LOCATED IN FENCE ROW)
8		S25-04-40E	369.44			
	711-9		338.41	365,192.64	1,617,100.88	
9		S01-21-09W	165.67			
	711-10		—	365,027.11	1,617,096.97	NOT MONUMENTED
10		N88-48-38W	164.45			
	711-11		—	365,030.52	1,616,932.71	NOT MONUMENTED
11		S34-53-11W	596.66			
	711-12		—	364,540.28	1,616,590.30	UNDER WATER
12		N88-42-39W	164.45			
	711-13		342.43	364,542.89	1,616,423.81	
13		S01-27-06W	331.20			
	711-14		344.32	364,211.97	1,616,415.43	
14		N54-46-25W	296.77			
	711-15		342.01	364,383.07	1,616,173.11	TYPE-I
15		N05-38-16W	667.15			
	711-16		342.85	365,047.27	1,616,107.55	TYPE-I
16		N88-43-28W	164.46			
	711-17		349.28	365,050.93	1,615,943.28	
17		S01-26-01W	165.55			
	711-18		338.65	364,885.52	1,615,939.14	
18		N43-27-51W	465.90			
	711-19		348.72	365,223.67	1,615,618.64	
19		S01-25-39W	331.01			

SHEET 2 OF 3

SWL FORM 136
REVISED OCT. 1971

BOUNDARY SURVEYS
LAKE DARDANELLE
ARKANSAS RIVER, ARKANSAS

SECTION 24 , T 8 N , R 22 W COUNTY POPE

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	711-20		338.24	364,892.94	1,615,610.40	
20		N88-43-32W	164.46			
	711-21		340.82	364,896.60	1,615,446.13	
21		S27-48-57W	369.93			
	711-22		344.04	364,569.70	1,615,273.66	
22		N72-47-16E	173.47			
	711-23		342.45	364,518.46	1,615,108.04	
23		N66-29-20W	886.96			
	711-24		346.68	364,872.29	1,614,294.71	
24		N01-24-19E	215.29			
	711-25		357.36	365,087.52	1,614,299.99	
25		N88-44-52W	164.31			
	711-26		362.27	365,091.11	1,614,135.72	
26		S72-58-28W	173.19			
	711-27		352.27	365,040.40	1,613,970.12	
27						
	711-28					NOT SET
28						
	711-29		361.30	365,609.76	1,613,325.98	
29		N46-09-02E	233.49			
	711-30		370.08	365,771.67	1,613,494.54	
30		N43-34-54W	123.18			
	711-30A		364.66	365,860.88	1,613,409.64	
30		N43-34-54W	109.62			
	711-31		386.06	365,940.27	1,613,334.10	
31		S46-08-42W	211.79			
	711-31A		373.42	365,793.68	1,613,181.52	
31		S46-08-42W	259.26			
	711-32		340.81	365,614.24	1,612,994.76	
32		S84-06-35W	328.58			
	711-33=712-1		354.191	365,580.52	1,612,667.91	

SHEET 3 OF 3

SWL FORM 136
REVISED OCT. 1971
