PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 10, T -8-N, R -23-W COUNTY LOGAN

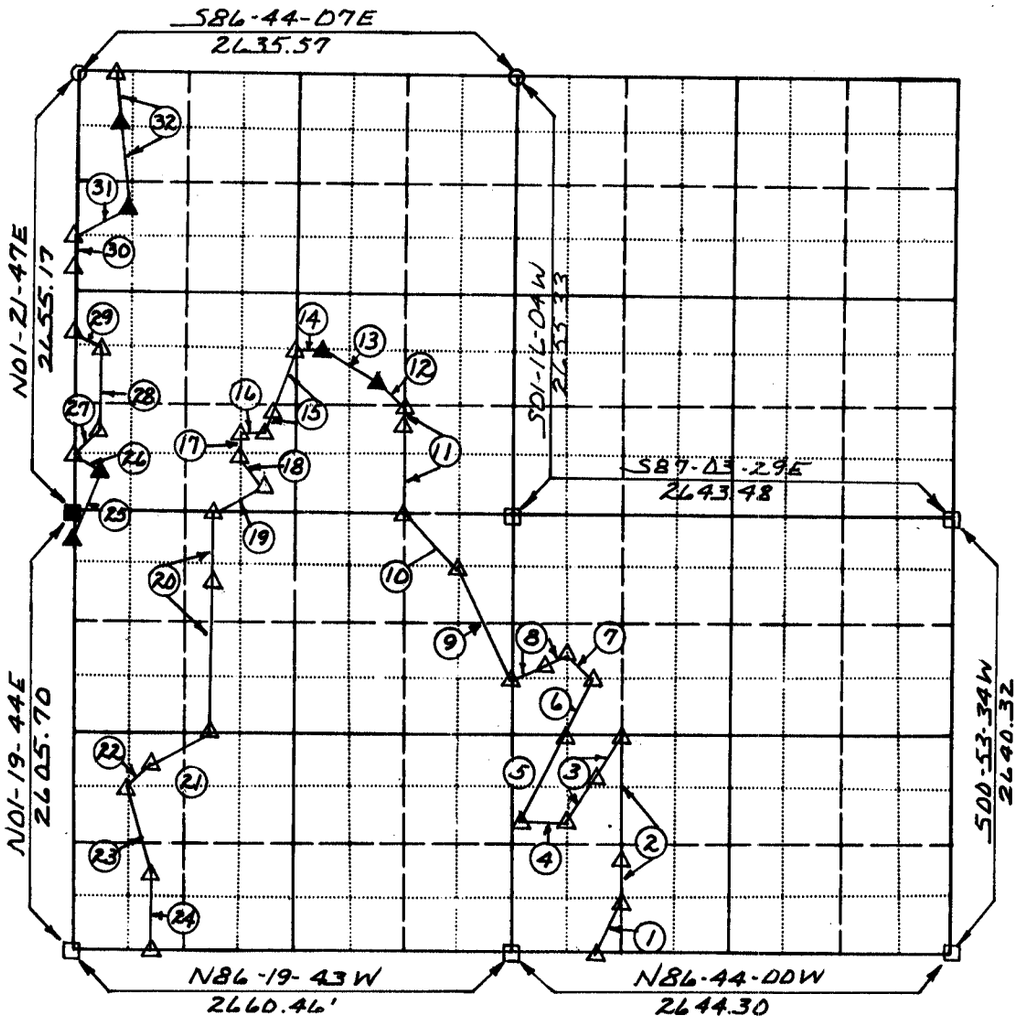

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1502-1-18		348.78	376.792.59	1.574.960.33	
	1		N28-05-44E	361.69'			
		1502-1-19		346.31	377.111.62	1.575.130.64	
	2		N00-55-44E	239.03'			
		1502-1-19A		352.49	377.350.57	1.575.134.51	
	2		N00-55-44E	746.87'			
		1502-1-20		——	378.097.22	1.575.146.62	Native Post in 1½' of Lake Water
	3		S35-28-15W	295.75'			

Field Book No. 68D1&2 / 66D15&16 Date: April 1968 / Oct. 1966

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____

COUNTY, ARKANSAS

_____

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 4

GN MN
0°34'21"
6°37'

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 10, T 8 N, R 23 W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1502-1-20A		352.50	377,856.32	1,574,974.98	
	3		S35-28-15W	286.77'			
		1502-1-21		348.21	377,622.75	1,574,808.55	
	4		N86-47-15W	247.88'			
		1502-1-22		347.62	377,636.64	1,574,561.07	
	5		N28-06-01E	542.61'			
		1502-1-23		342.37	378,115.22	1,574,816.61	
	6		N28-05-01E	362.00'			
		1502-1-24		338.22	378,434.56	1,574,987.00	
	7		N43-08-59W	237.31'			
		1502-1-25		340.21	378,607.67	1,574,824.73	
	8		S66-16-02W	129.35'			
		1502-1-25A		354.07	378,555.60	1,574,706.31	
	8		S66-16-02W	234.06'			
		1502-1-26= 1507-1		350.90	378,461.40	1,574,492.04	
	9		N25-15-28W	747.11'			
		1507-2		350.32	379,136.97	1,574,173.30	
	10		N43-00-43W	474.48'			
		1507-3		349.30	379,483.86	1,573,849.69	
	11		N01-21-33E	565.83'			
		1507-3A		350.44	380,049.44	1,573,863.10	
	11		N01-21-33E	97.99'			
		1507-4		342.55	380,147.38	1,573,865.43	
	12		N42-28-27W	237.96'			
		1507-5		342.56	380,322.87	1,573,704.77	
	13		N60-20-56W	374.24'			
		1507-6		354.10	380,507.99	1,573,379.57	
	14		N86-38-26W	164.90'			
		1507-7= 1506-1		342.09	380,517.66	1,573,214.96	
	15		S19-55-04W	401.55'			
		1506-1A		349.60	380,140.07	1,573,078.14	
	15		S19-55-04W	117.58'			
		1506-2		349.36	380,029.51	1,573,038.08	
	16		N86-38-55W	164.94			

SHEET 2 of 4

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 10, T 8-N, R 23-W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1506-3		338.58	380.039.15	1.572.873.42	
	17		S01-24-50W	165.95'			
		1506-4		339.34	379.873.22	1.572.869.33	
	18		S42-27-25E	237.93'			
		1506-5		349.06	379.697.65	1.573.029.96	
	19		S65-58-51W	364.29			
		1506-6		339.51	379.549.36	1.572.697.20	
	20		S01-14-36W	398.88'			
		1506-6A		342.02	379.150.51	1.572.688.55	
	20		S01-14-36W	907.02'			
		1506-7		344.83	378.243.55	1.572.668.86	
	21		S66-53-07W	363.53'			
		1506-8		346.24	378.100.83	1.572.334.50	
	22		S28-42-37W	359.95'			
		1506-9		350.18	377.785.09	1.572.161.56	
	23		S25-10-23E	371.80'			
		1506-10		351.68	377.448.54	1.572.319.73	
	24		S01-17-23W	489.26'			
		1506-11= 1502-2-1		352.44	376.959.32	1.572.308.72	
		1506-20		350.27	379.431.71	1.571.866.50	
	25		N23-20-51E	440.47			
		1506-21		347.62	379.836.11	1.572.041.06	
	26		N60-25-36W	187.11			
		1506-22		347.78	379.928.46	1.571.878.33	
	27		N28-09-21E	182.84			
		1506-23		347.13	380.089.66	1.571.964.61	
	28		N01-21-30E	497.85			
		1506-24		345.03	380.587.37	1.571.976.42	
	29		N24-40-27W	187.74			
		1506-25		343.38	380.757.96	1.571.898.06	

SHEET 3 of 4

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 10, T -8-N, R -23-W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1506-33		343.09	381,089.77	1,571,905.95	
	30		N01-21-47E	165.95			
		1506-34		344.71	381,255.67	1,571,909.91	
	31		N66-09-52E	364.08			
		1506-35		342.56	381,402.80	1,572,242.94	
	32		N04-16-37W N04-17-48W	800.00			As Surveyed As Calculated
		1506-35A		346.92			
	32		N04-16-37W N04-17-48W	35.35 36.56			As Surveyed As Calculated
		1506-36= 1500-2-1		347.27	382,237.00	1,572,180.27	Tie Point

SHEET 4 of 4

SWL FORM 136
REVISED FEB. 66
