PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

FRAC SEC. 31, T -8-N, R -25-W COUNTY LOGAN

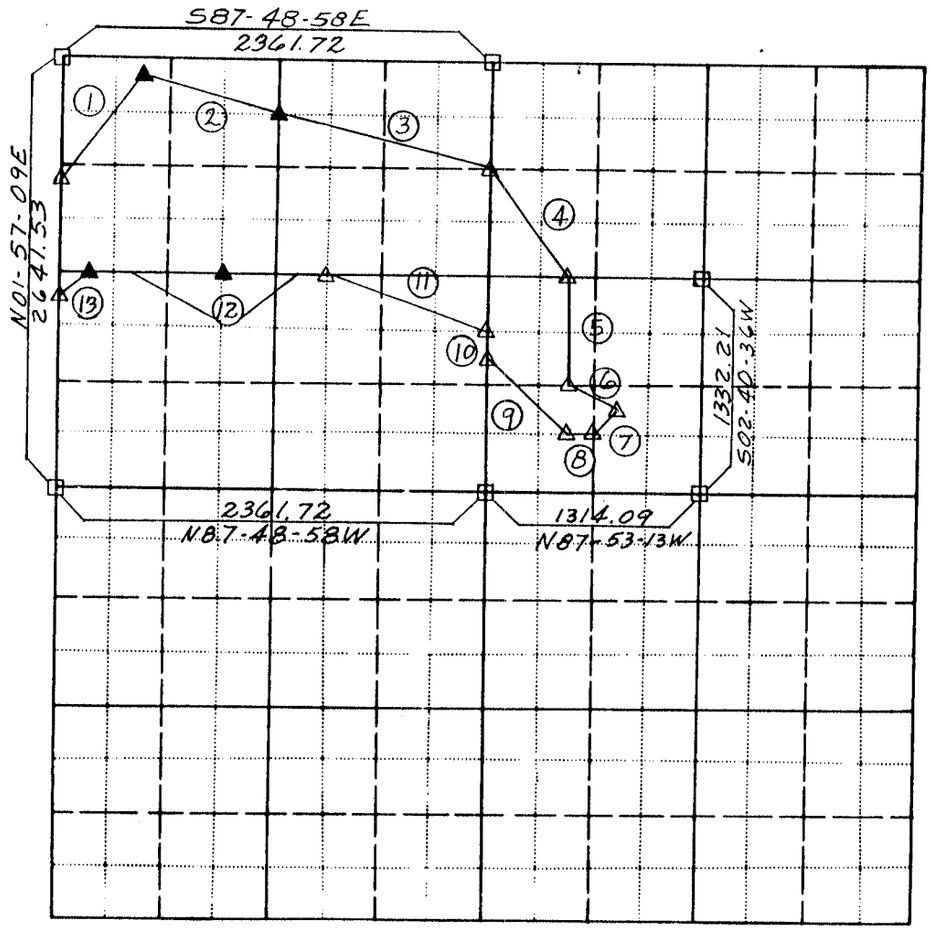

FULL SEC APPROX SCALE 1:12,000

TRACT NO	COURSE NO	MONUMENT NO	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		3207-3 = 3206-1		365.76	364,421.44	1,492,164.15	
	1		N41-54-06E	856.65			
		3206-2		361.31	365,059.07	1,492,736.29	
	2		S62-46-49E	543.70			
		3206-3 = 3205-1		358.22	364,810.35	1,493,219.84	
	3		S73-45-43E	1362.01			
		3205-2 = 3204-1		361.77	364,429.45	1,494,527.68	
	4		S33-40-38E	827.97			

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION 31, T-8-N, R-25-W.

COUNTY, ARKANSAS

Field Book No. 71D-20, 21 Date: 1971
Level Book No. 71D-22

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 2

LEGEND

- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 3
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✱ OTHER

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 31, T -8-N, R-25-W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		3204-2= 3203-1		360.36	363,740.37	1,494,986.84	
	5		S02-15-28W	661.40			
		3203-2		358.29	363,079.47	1,494,960.78	
	6		S61-24-56E	368.45			
		3203-3		362.23	362,903.16	1,495,284.36	
	7		S47-00-09W	234.89			
		3203-4		360.79	362,742.99	1,495,112.58	
	8		N88-02-15W	164.82			
		3203-5		355.62	362,748.63	1,494,947.87	
	9		N43-01-39W	699.66			
		3203-6		362.29	363,260.05	1,494,470.51	
	10		N07-19-26E	181.51			
		3205-3		360.68	363,440.08	1,494,493.65	
	11		N69-25-28W	1044.82			
		3205-4		356.89	363,807.22	1,493,515.60	
	12		N87-47-20W	633.45			
		3205-4A		359.70	363,831.65	1,492,882.69	
	12		N87-47-20W	538.27			
		3219-2		357.85	363,852.42	1,492,344.89	
	13		S58-39-49W	239.23			
		3219-3= 3208-1			363,728.02	1,492,140.58	

SHEET 2 of 2

SWL FORM 136
REVISED FEB. 66
