# PARTIAL BOUNDARY SURVEYS
# BEAVER RESERVOIR
# WHITE RIVER, ARKANSAS

SEC. 11, T 19N, R 28W COUNTY BENTON

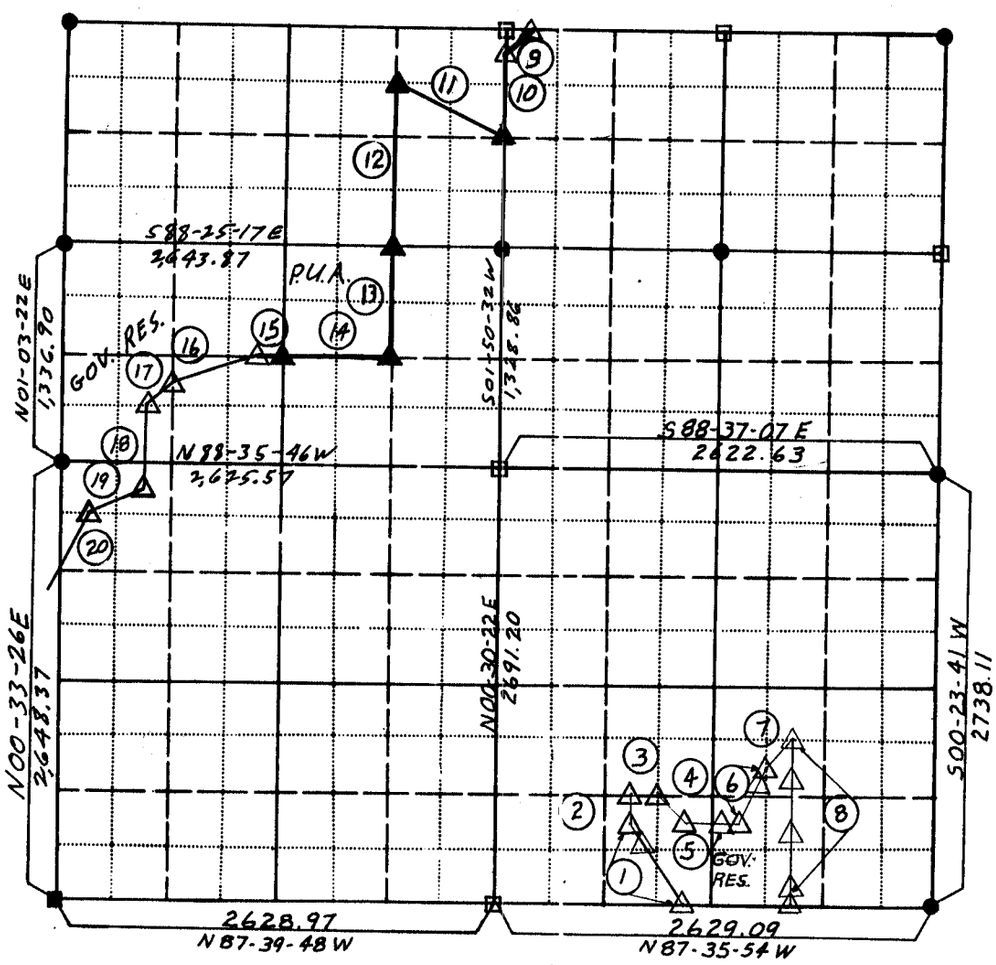


FULL SEC. APPROX. SCALE 1:12,000

| TRACT NO. | COURSE NO. | MONUMENT NO. | ANGLE / GRID BEARING | ELEVATION / DISTANCE | POSITION NORTH | POSITION EAST | REMARKS |
|---|---|---|---|---|---|---|---|
| | | 1034-1 | | 1162.58 | 729,783.51 | 1,432,789.45 | |
| | 1 | | N31-40-00W | 484.87 | | | |
| | | 1034-1A | | 1151.02 | 730,196.17 | 1,432,534.92 | |
| | 1 | | N31-40-00W | 128.84 | | | |
| | | 1034-2 | | 1134.78 | 730,305.83 | 1,432,467.28 | |
| | 2 | | N00-42-58E | 101.67 | | | |
| | | 1034-2A | | 1126.31 | 730,407.47 | 1,432,468.55 | |
| | 2 | | N00-42-58E | 67.45 | | | |

Field Book No. Transit-67B-98, Chain-67B-99, Levels-67B-100, TRANSIT-67B-97, CHAIN-67B-96, LEVEL-67B-101 Date: 6 July 67, 6 July 67, 14 July 67, JUNE 1967, JUNE 1967, JUNE 1967

**CERTIFICATE OF SURVEY**

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____
COUNTY, ARKANSAS

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 3

GN MN 01°-07'-30" 6°56'

**LEGEND**

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

# PARTIAL BOUNDARY SURVEYS
# BEAVER RESERVOIR
# WHITE RIVER, ARKANSAS

SEC. 11, T 19N, R 28W COUNTY BENTON

| TRACT NO. | COURSE NO. | MONUMENT NO. | GRID BEARING | ELEVATION / DISTANCE | POSITION NORTH | POSITION EAST | REMARKS |
|---|---|---|---|---|---|---|---|
| | | 1034-3 | | 1115.22 | 730,474.91 | 1,432,469.39 | |
| | 3 | | S87-36-31E | 164.21 | | | |
| | | 1034-4 | | 1150.17 | 730,468.06 | 1,432,633.44 | |
| | 4 | | S42-35-31E | 239.44 | | | |
| | | 1034-5 | | 1138.80 | 730,291.78 | 1,432,795.49 | |
| | 5 | | S87-31-11E | 234.49 | | | |
| | | 1034-5A | | 1164.73 | 730,281.64 | 1,433,029.73 | |
| | 5 | | S87-31-11E | 93.99 | | | 1032-5 WAS NOT SET |
| | | 1032-6 | | 1132.80 | 730,277.57 | 1,433,123.62 | |
| | 6 | | N26-48-40E | 271.87 | | | |
| | | 1032-6A | | 1133.24 | 730,520.17 | 1,433,246.23 | |
| | 6 | | N26-49-22E | 101.17 | | | |
| | | 1032-7 | | 1122.82 | 730,610.44 | 1,433,291.87 | |
| | 7 | | N45-28-12E | 233.06 | | | |
| | | 1032-8 | | 1134.70 | 730,773.85 | 1,433,457.98 | |
| | 8 | | S00-45-40W | 230.46 | | | |
| | | 1032-8A | | 1163.02 | 730,543.38 | 1,433,454.92 | |
| | 8 | | S00-45-39W | 307.64 | | | |
| | | 1032-8B | | 1171.28 | 730,235.73 | 1,433,450.84 | |
| | 8 | | S00-46-07W | 380.70 | | | |
| | | 1032-8C | | 1171.16 | 729,855.01 | 1,433,445.73 | |
| | 8 | | S00-46-07W | 107.40 | | | |
| | | 1032-9 | | 1159.19 | 729,747.61 | 1,433,444.29 | YIELDED TO FENCE |
| | | | | | | | |
| | | | | | | | |
| | | 907-7 | | 1146.78 | 735,173.95 | 1,431,886.26 | |
| | 9 | | S46-04-00W | 127.08 | | | |
| | | 907-7A | | 1138.89 | 735,085.78 | 1,431,794.75 | |
| | | | S46-04-00W | 102.13 | | | |
| | | 907-8 = 910-4 | | 1130.79 | 735,014.98 | 1,431,721.26 | |
| | 10 | | S00-33-37W | 101.84 | | | |
| | | 907-8A | | 1148.37 | 734,913.15 | 1,431,720.27 | |
| | 10 | | S00-33-37W | 280.41 | | | |
| | | 907-8B | | 1122.46 | 734,632.75 | 1,431,717.53 | |

SHEET 2 of 3

SWL FORM 136
REVISED FEB. 66

# PARTIAL BOUNDARY SURVEYS
# BEAVER RESERVOIR
# WHITE RIVER, ARKANSAS

SEC. 11, T -19-N, R -28-W COUNTY BENTON

| TRACT NO. | COURSE NO. | MONUMENT NO. | GRID BEARING | ELEVATION DISTANCE | POSITION NORTH | POSITION EAST | REMARKS |
|---|---|---|---|---|---|---|---|
| | 10 | | S00-33-37W | 119.01 | | | |
| | | 910-3 | | 1133.72 | 734,513.95 | 1,431,716.36 | CONC MON |
| | 11 | | N61-09-16W | 747.06 | | | |
| | | 910-2 | | | 734,874.37 | 1,431,061.99 | CONC MON |
| | 12 | | S01-23-13W | 931.17 | | | |
| | | 910-1 = 935-3-1 | | | 733,943.47 | 1,431,039.45 | CONC MON |
| | 13 | | S01-23-13W | 718.87 | | | |
| | | 935-3-2 | | | 733,224.81 | 1,431,022.04 | CONC MON |
| | 14 | | N88-36-47W | 660.00 | | | |
| | | 935-33 | | 1130.19 | 733,240.78 | 1,430,362.23 | CONC MON |
| | 15 | | S86-08-11W | 160.43 | | | |
| | | 911-1-2 | | 1127.53 | 733,229.98 | 1,430,202.24 | |
| | 16 | | S72-48-31W | 118.14 | | | |
| | | 911-1-2A | | 1150.24 | 733,195.06 | 1,430,089.38 | |
| | 16 | | S72-48-31W | 402.63 | | | |
| | | 911-1-3 | | 1144.61 | 733,076.11 | 1,429,704.89 | |
| | 17 | | S45-55-58W | 233.82 | | | |
| | | 911-1-4 | | 1134.12 | 732,913.48 | 1,429,536.87 | |
| | 18 | | S01-01-18W | 268.31 | | | |
| | | 911-1-4A | | 1136.28 | 732,645.21 | 1,429,532.09 | |
| | 18 | | S01-01-18W | 231.06 | | | |
| | | 911-1-5 | | 1128.78 | 732,413.86 | 1,429,527.96 | |
| | 19 | | S64-29-45W | 140.30 | | | |
| | | 911-1-5A | | 1139.51 | 732,353.45 | 1,429,401.33 | |
| | 19 | | S64-29-45W | 225.07 | | | |
| | | 911-1-6 | | 1124.79 | 732,256.56 | 1,429,198.26 | |
| | 20 | | S27-12-04W | 736.41 | | | |
| | | 911-1-7 | | 1129.08 | 731,601.38 | 1,428,861.52 | THIS POINT FALLS IN SEC. 10 |

SHEET 3 of 3

SWL FORM 136
REVISED FEB. 66

# PARTIAL BOUNDARY SURVEYS
# BEAVER RESERVOIR
# WHITE RIVER, ARKANSAS

SEC. 11, T 19N, R 28 W COUNTY BENTON

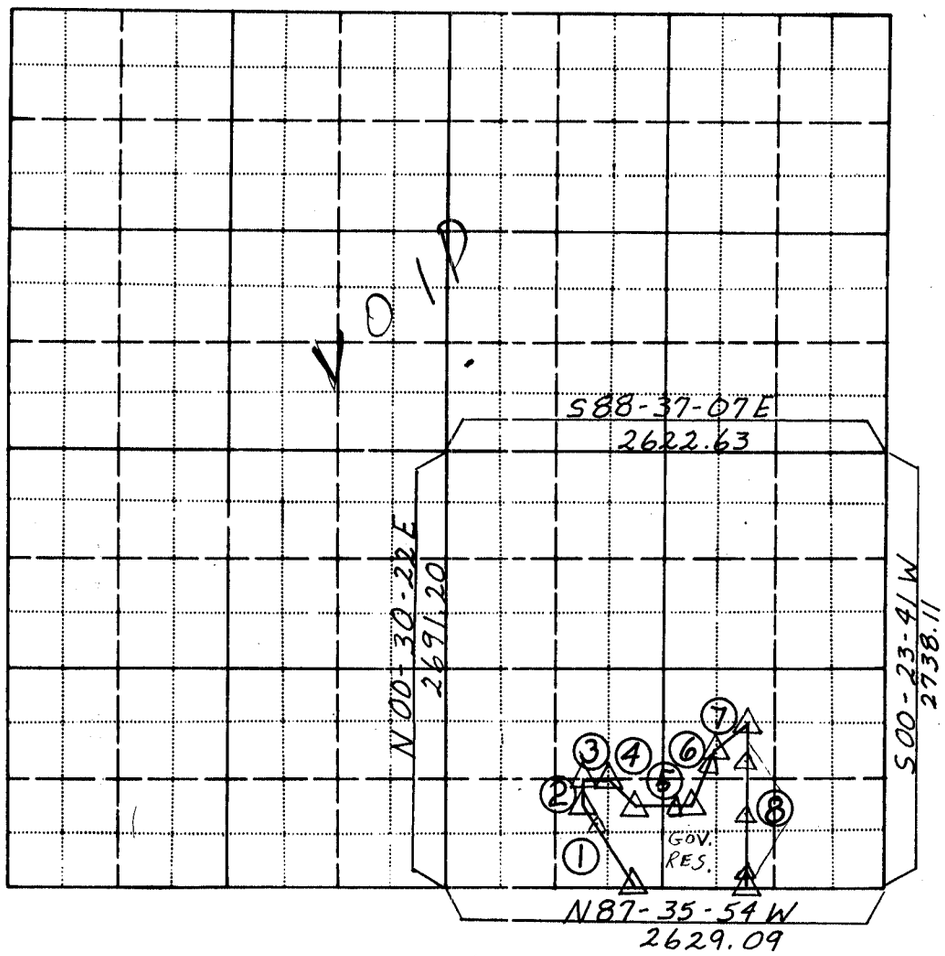


FULL SEC. APPROX. SCALE 1:12,000

| TRACT NO. | COURSE NO. | MONUMENT NO. | ANGLE / GRID BEARING | ELEVATION / DISTANCE | POSITION / NORTH | POSITION / EAST | REMARKS |
|---|---|---|---|---|---|---|---|
| | | 1034-1 | | 1162.58 | 729,783.51 | 1,432,789.45 | |
| | 1 | | N31-40-00W | 484.87 | | | |
| | | 1034-1A | | 1151.02 | 730,196.17 | 1,432,534.92 | |
| | 1 | | N31-40-00W | 128.84 | | | |
| | | 1034-2 | | 1134.78 | 730,305.83 | 1,432,467.28 | |
| | 2 | | N00-42-58E | 101.67 | | | |
| | | 1034-2A | | 1126.31 | 730,407.47 | 1,432,468.55 | |
| | 2 | | N00-42-58E | 67.45 | | | |

Field Book No. TRANSIT BK 67B-112 Date: OCTOBER 1968
CHAIN BK 67B-113
LEVEL BK 67B-114

**CERTIFICATE OF SURVEY**

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____
COUNTY, ARKANSAS

GN MN
61°07'30" 6°56'

**LEGEND**

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 2
