BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SECTION 32 ,T 20N ,R 28W COUNTY BENTON

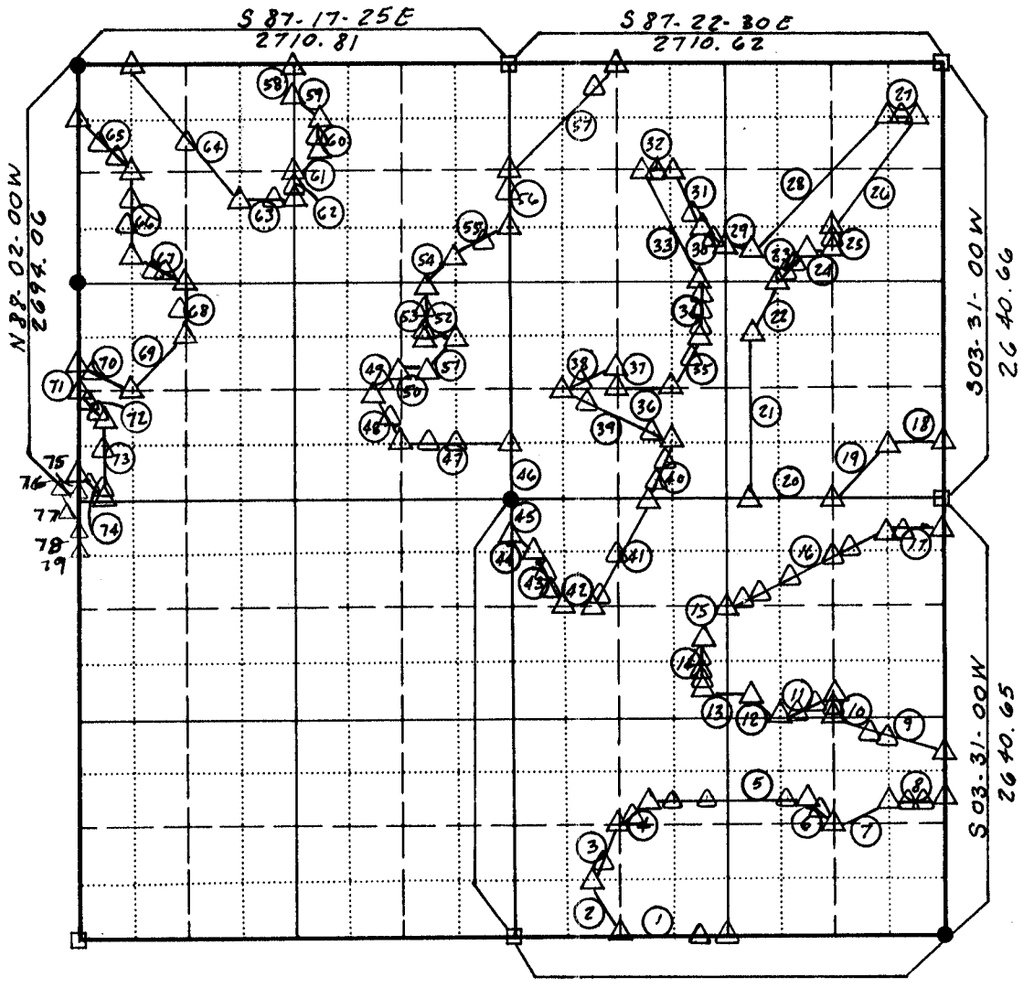

FULL SECTION APPROXIMATE SCALE 1:12,000

COURSE 75 REVISED NOV 84 BK 948-2

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	542-3		1152.98	740,698.39	1,417,086.02	Type 1
1		N 87.48-50-W	534.37			
	542-3A		1135.37	740,718.78	1,416,552.04	Type 1
1		N 87-48-50 W	138.16			
	542-4			740,724.05	1,416,413.98	Type 3
2		N 23-25-28 W	367.49			
	542-5			741,061.25	1,416,267.89	NOT SET IN FIELD IN LAKE
3		N 28-14-58 E	124.23			

Field Book No. 65 W-8 Date: MARCH 65
69 B -17 APRIL 69

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

COUNTY, ARKANSAS

SURVEYOR REG. NO.

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 OF 11

GN MN

LEGEND
- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 3
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✳ OTHER

BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SECTION 32 , T 20N , R 28W COUNTY BENTON

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	542-5A		1132.57	741,169.64	1,416,328.59	Type 3
3		N29-14-59E	250.42			
	542-6		1144.52	741,388.13	1,416,450.96	Type 3
4		N47-22-13E	146.72			
	542-6A		1173.27	741,487.50	1,416,558.90	Type 3
4		N47-21-57E	89.73			
	542-7		1181.08	741,548.27	1,416,624.92	Type 3
5		S87-50-20E	125.35			
	542-7A		1212.00	741,543.55	1,416,750.18	Type 3
5		S87-50-36E	205.09			
	542-7B		1224.58	741,535.83	1,416,955.12	Type 3
5		S87-50-53E	500.43			
	542-7C		1224.08	741,517.04	1,417,455.20	Type 3
5		S87-51-09E	157.61			
	542-8		1213.57	741,511.13	1,417,612.70	Type 3
6		S42-05-26E	108.15			
	542-8A		1230.27	741,430.87	1,417,685.20	Type 3
6		S42-05-42E	122.89			
	542-9		1219.76	741,339.68	1,417,767.58	Type 3
7		N65-42-47E	371.93			
	542-10		1199.12	741,492.66	1,418,106.59	Type 3
8		S87-52-00E	116.70			
	542-10A		1217.92	741,488.32	1,418,223.21	Type 3
8		S87-52-16E	143.47			
	542-10B		1215.58	741,482.99	1,418,366.58	Type 3
8		S87-52-33E	69.32			
	542-11 = 541-2-1		1201.13	741,480.42	1,418,435.85	Type 3
		N 00-12-56 E	432.99			
	541-2-6 = 542-12			741,913.41	1,418,437.48	IN LAKE Not Set
9		N73-41-00W	380.22			
	542-12A			742,020.23	1,418,072.57	IN LAKE Not Set
9		N73-41-17W	79.90			
	542-12B			742,042.67	1,417,995.89	IN LAKE Not Set
9		N73-41-33W	58.03			
	542-13			742,058.96	1,417,940.19	IN LAKE Not Set
10		N03-16-55E	50.84			
	542-13A			742,109.72	1,417,943.11	IN LAKE Not Set
10		N03-16-39E	114.73			
	542-14			742,224.26	1,417,949.66	IN LAKE Not Set

SHEET 2 OF 7

SWL FORM 136
REVISED OCT. 1971

BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SECTION 32 , T 20N , R 28W COUNTY BENTON

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
11		S 65-45-08W	109.75			IN LAKE
	542-14A			742,179.19	1,417,849.59	Not Set
11		S 65-44-51W	203.40			IN LAKE
	542-14B			742,095.64	1,417,664.15	Not Set
11		S 65-44-35W	58.77			IN LAKE
	542-15			742,071.50	1,417,610.57	Not Set
12		N 78-11-57W	167.20			IN LAKE
	542-16			742,185.74	1,417,322.49	NOT SET IN FIELD
13		N 85-57-25W	330.01			IN LAKE
	542-17			742,199.42	1,416,992.76	NOT SET IN FIELD
14		N 3-18-19 E	ABOUT 69.73			
	542-17A		1131.43	742,269.03	1,416,996.78	Type 3
14		N 03-18-57E	103.43			
	542-17B		1161.80	742,372.29	1,417,002.77	Type 3
14		N 03-19-11E	95.66			
	542-17C		1155.81	742,467.79	1,417,008.31	Type 3
14		N 03-19-25E	63.66			
	542-18			742,531.34	1,417,012.00	Not Set
15						
	542-19		1160.76	742,689.93	1,417,186.77	Type 3
16		N66-11-05E	98.36			
	542-19A		1189.78	742,729.65	1,417,276.77	Type 3
16		N66-11-19E	112.75			
	542-19B		1195.92	742,775.17	1,417,379.91	Type 3
16		N66-11-33E	221.45			
	542-19C		1189.90	742,864.56	1,417,582.51	Type 3
16		N66-11-47E				
	542-19D		1151.33	743,053.73	1,418,011.34	Type 3
16		N66-12-02E	93.53			
	542-19E		1149.47	743,091.47	1,418,096.92	Type 3
16		N66-12-16E	120.96			
	542-20		1129.44	743,140.28	1,418,207.60	Type 3
17		S87-16-45E	70.80			
	542-20A		1165.38	743,136.92	1,418,278.32	Type 3
18		S 87-16-31E	260.01			
	542-21 = 541-3-1		1228.28	743,124.56	1,418,538.04	Type 3
	540-1-7 = 543-2-1			743,620.43	1,418,567.67	NOT SET IN FIELD

SHEET 3 OF 11

SWL FORM 136
REVISED OCT. 1971

BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SECTION 32 , T 20N , R 28W COUNTY BENTON

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
19						
	543-2-2			743,636.01	1,418,236.11	NOT SET IN FIELD
20						
	543-2-3= 542-22			743,322.16	1,417,886.27	NOT SET IN FIELD
21						
	542-23= 543-1-1			743,345.54	1,417,390.41	NOT SET IN FIELD
22						
	543-1-1B		1154.56	743,501.11	1,417,398.40	Type 1
22		N02-54-02E	184.50			
	543-1-1C		1155.51	743,685.46	1,417,407.68	Type 1
22		N02-54-02E	355.46			
	543-1-1D		1165.31	744,040.46	1,417,425.60	Type 3
22		N02-54-02E	160.72			
	543-1-1E		1148.19	744,200.98	1,417,433.79	Type 3
22						
	543-1-2			744,333.83	1,417,440.79	NOT SET IN FIELD
23						
	543-1-2A		1156.25	744,441.30	1,417,501.99	Type 3
23		N29-46-02E	107.29			
	543-1-2B		1154.89	744,534.44	1,417,555.25	Type 3
23		N29-46-02E	139.51			
	543-1-3		1148.56	744,655.54	1,417,624.62	Type 3
24		N 48-17-02E	235.92			
	543-1-4		1160.59	744,812.53	1,417,800.62	Type 3
25		N87-22-13E	93.08			
	543-1-4A		1192.22	744,808.26	1,417,893.60	Type 3
25		N87-22-13E	74.61			
	543-1-5		1205.75	744,804.84	1,417,968.14	Type 3
26		N03-08-47E	164.97			
	543-1-6		1142.69	744,969.56	1,417,977.19	Type 3
27		N 40-27-32E	490.34			
	543-1-6A		1168.46	745,342.64	1,418,295.37	Type 3
27		N 40-27-32E	345.47			
	543-1-7		1151.06	745,605.50	1,418,519.55	Type 3
28		N 87-22-28W	168.92			
	543-1-8		1190.74	745,613.24	1,418,350.81	Type 3
29		S 48-26-32W	219.32			
	543-1-8A		1155.95	745,467.75	1,418,186.69	Type 3
29		S 48-26-32W	175.24			

SHEET 4 OF 11

SWL FORM 136
REVISED OCT. 1971

BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SECTION 32 , T 20N , R 28W COUNTY BENTON

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	543-1-8B		1180.70	745,351.50	1,418,055.56	Type 3
29		S 48-26-32W	258.89			
	543-1-8C		1171.34	745,179.76	1,417,861.84	Type 3
29		S 48-26-32W	144.35			
	543-1-8D		1177.08	745,084.00	1,417,753.82	Type 3
29		S 48-26-32W	225.82			
	543-1-8E		1162.82	744,934.20	1,417,584.85	Type 3
29		S 48-26-32W	159.72			
	543-1-9		1139.62	744,828.24	1,417,465.33	Type 3
30		N61-08-43W	81.56			
	543-1-9A		1155.62	744,867.60	1,417,393.90	Type 3
30		N 61-08-43W	105.04			
	543-1-10		1141.04	744,918.29	1,417,301.90	Type 3
31		N 61-11-13W	35.60			
	543-1-10A		1136.71	744,935.45	1,417,270.71	Type 3
31						
	543-1-11			745,008.230	1,417,138.86	NOT SET IN FIELD
32						
	543-1-11A		1136.17	745,169.00	1,417,065.49	Type 1
32		N 64-20-43W	193.71			
	543-1-12		1140.34	745,345.49	1,416,985.63	Type 1
33		N87-21-43W	168.43			
	543-1-13		1190.91	745,353.24	1,416,817.38	Type 3
34		S 24-19-58E	154.57			
	543-1-13A		1196.96	745,212.40	1,416,881.07	Type 3
34		S 24-19-58E	313.63			
	543-1-13B		1175.74	744,926.63	1,417,010.29	Type 3
34		S 24-19-58E	126.77			
	543-1-13C		1194.03	744,811.13	1,417,062.53	Type 3
34		S 24-19-58E	145.12			
	543-1-14		1194.76	744,678.90	1,417,122.32	Type 3
35		S02-44-47W	111.35			
	543-1-14A		1192.99	744,567.68	1,417,116.99	Type 3
35		S02-44-47W	218.45			
	543-1-15		1156.62	744,349.48	1,417,106.52	Type 3
36	15 A 15 B	S 29-30-47W	370.00			
	543-1-16		1148.08	744,027.81	1,416,923.68	Type 3
37		N 87-19-34W	116.14			
	543-1-16A			744,033.16	1,416,809.17	Type 3

Book 71 B-9 Page 40 & 41 SHEET 5 OF 17

SWL FORM 136
REVISED OCT. 1971

BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SECTION 32 , T 20N , R 28W COUNTY BENTON

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
37		N 87-19.39W	157.99			
	543-1-16B		1132.68	744,040.53	1,416,651.35	Type 3
37		N 87-19-39 W	58.69			
	543-1-17		1125.72	744,043.27	1,416,592.72	Type 3
38		N 02-30-31 E	74.61			
	543-1-17A		1150.44	744,117.17	1,416,595.83	Type 3
38		N 02.28.23E	90.90			
	543-1-18		1174.50	744,207.99	1,416,599.75	Type 3
38		S 66-17.18 W	209.88			
	543-1-18A		1151.98	744,123.59	1,416,407.59	Type 3
38		S 66-17-14W	161.11			
	543-1-19		1190.71	744,058.80	1,416,260.08	Type 3
39		S 60.59.06E	186.33			
	543-1.19A		1192.35	743,968.42	1,416,423.03	Type 3
39		S 60-59.10E	479.67			
	543-1.19B		1188.32	743,735.77	1,416,842.50	Type 3
39		S 60.59.15E	77.11			
	543-1-20		1172.46	743,698.37	1,416,909.93	Type 3
40		S 29.17.18W	133.13			
	543-1-20A		1193.44	743,582.26	1,416,844.80	Type 3
40		S 29.17.14W	139.83			
	543-1-20B		1195.90	743,460.30	1,416,776.40	Type 3
40		S 29.17.09 W	95.90			
	543.1.21= 542-24		1180.47	743,376.66	1,416,729.49	Type 3
41		S 29-27.50W	365.64			
	542-24A		1182.30	743,058.31	1,416,549.64	Type 3
41		S29.27.45W	319.65			
	542-24B		1146.65	742,779.99	1,416,392.42	Type 3
41		S 29.27.40W	62.00			
	542-25		1128.36	742,726.02	1,416,361.92	Type 3
42						
	542-26			742,733.55	1,416,196.27	NOT SET IN FIELD
43						
	542-26A		1147.74	742,884.26	1,416,131.79	Type 3
43		N23.18-55W	118.04			
	542-26B		1153.79	742,992.66	1,416,085.08	Type 3
43		N23-19-00W	88.47			
	542-27		1145.33	743,073.91	1,416,050.06	Type 3
44		N 41-42.35W	240.61			

SHEET 6 OF 11

WL FORM 136
EVISED OCT. 1971

BOUNDARY SURVEYS
BEAVER LAKE
WHITE RIVER, ARKANSAS

SECTION 32 , T 20N , R 28W COUNTY BENTON

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	542-28		1161.66	743,253.53	1,415,889.97	Type 1 Set 1965
45		N03-08-28E	167.17			
	542-29 = 544-3-1A			743,415.71	1,415,902.83	Type 3
46		N02-46-59E	330.00			Type 1
	544-3-2			743,745.32	1,415,918.85	Type 1
47		N87-13-01W	337.72			
	544-3-2A			743,761.72	1,415,581.52	STAMPED 544-3-3B
47		N87-13-01W	172.24			
	544-3-2B			743,770.08	1,415,409.49	STAMPED 544-3-3A
47		N87-13-01W	171.91			
	544-3-3		1133.73	743,778.43	1,415,237.78	Type 1
48		N25-01-16W	135.09			
	544-3-3A		1150.69	743,900.79	1,415,180.69	Treated Hub
48		N25-01-16W	226.21			

SHEET 7 OF 11

SWL FORM 136
REVISED OCT. 1971

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 32, T -20-N, R -28-W COUNTY Benton

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		544-3-4		1149.86	744,105.65	1,415,085.03	Type 3
	49		N47-38-14E	113.75			
		544-3-4A		1164.99	744,182.32	1,415,169.10	"
	49		N47-38-14E	122.23			
		544-3-5		1153.56	744,264.70	1,415,259.44	"
	50		S87-49-46E	168.70			
		544-3-6		1161.80	744,258.30	1,415,428.12	"
	51		N47-43-52E	235.83			
		544-3-7		1141.82	744,416.96	1,415,602.67	"
	52		N87-47-46E	168.77			
		544-3-8		1128.49	744,423.45	1,415,434.13	"
	53		N02-02-14E	66.58			
		544-3-8A		1150.72	744,489.97	1,415,436.50	"
	53		N02-02-14E	100.67			
		544-3-8B		1167.26	744,590.55	1,415,440.07	"
	53		N02-02-14E	163.19			
		544-3-9= 547-1		1146.25	744,753.59	1,415,445.87	"
	54		N47-50-06E	235.69			
		547-2		1150.98	744,911.84	1,415,620.61	"
	55		N66-17-36E	196.77			
		547-2A		1165.13	744,990.98	1,415,800.85	"
	55		N66-17-36E	178.58			
		547-3		1143.74	745,062.81	1,415,964.43	"
	56		N02-08-49E	210.44			
		547-3A		1162.64	745,272.97	1,415,972.31	"
	56		N02-08-49E	119.17			
		547-4= 544-1-1		1148.88	745,392.06	1,415,976.77	"
	57		N48-11-10E	740.45			
		544-1-1A		1202.26	745,885.52	1,416,528.43	Type I
	57		N48-11-10E	201.01			
		544-1-2= 545-1-1		1201.77	746,019.49	1,416,678.18	Type I

SHEET 8 of 11

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 32, T-20-N, R-28-W COUNTY Benton

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		546-3-4= 547-5		1124.79	746,112.47	1,414,650.63	Type 3
	58		S02-02-14W	163.91			
		547-6		1162.14	745,948.76	1,414,644.80	"
	59		S43-14-36E	238.39			
		547-7		1141.07	745,774.96	1,414,808.25	"
	60		S02-01-40W	100.88			
		547-7A		1158.00	745,674.20	1,414,804.69	"
	60		S02-01-40W	64.88			
		547-8		1156.90	745,609.40	1,414,802.39	"
	61		S47-52-04W	235.74			
		547-9		1153.80	745,451.51	1,414,627.84	"
	62		S02-58-18W	83.17			
		547-9A		1156.67	745,368.43	1,414,624.94	"
	62		S02-58-18W	82.83			
		547-10= 642-2-1		1146.99	745,285.85	1,414,619.24	"
	63		N87-31-45W	93.15			
		642-2-1A		1155.53	745,289.83	1,414,526.24	Type 1
	63		N87-31-45W	245.04			
		642-2-2		1167.15	745,300.39	1,414,281.55	"
	64		N36-58-07W	465.38			
		642-2-2A		1186.29	745,672.26	1,414,001.64	Type 3
	64		N36-58-07W	614.05			
		642-2-3= 546-4-1		1170.66	746,162.93	1,413,632.31	"
		642-2-7		1163.09	745,845.63	1,413,283.56	"
	65		S43-11-46E	166.70			
		642-2-7A		1175.63	745,724.11	1,413,397.66	"
	65		S43-11-46E	155.42			
		642-2-7B		1164.49	745,610.81	1,413,504.03	"
	65		S43-11-46E	156.34			
		642-2-8		1134.29	745,496.85	1,413,611.04	"
	66		S01-50-06W	165.84			

SHEET 9 of 11

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 32, T -20-N, R-28-W COUNTY Benton

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		642-2-8A		1176.92	745,331.19	1,413,605.74	Type 3
	66		S01-50-06W	116.45			
		642-2-8B		1181.70	745,214.86	1,413,602.01	"
	66		S01-50-06W	217.91			
		642-2-9		1170.55	744,997.19	1,413,595.04	"
	67		S61-22-34E	144.68			
		642-2-9A		1170.67	744,928.09	1,413,722.18	"
	67		S61-22-34E	97.57			
		642-2-9B		1155.92	744,881.48	1,413,807.92	"
	67		S61-22-34E	135.99			
		642-2-10= 548-1-1		1122.31	744,815.96	1,413,927.11	"
	68		S01-53-48W	207.79			
		548-1-1A		1157.42	744,608.30	1,413,920.25	"
	68		S01-53-48W	125.12			
		548-1-2		1154.71	744,483.25	1,413,916.11	"
	69		S47-23-39W	472.77			
		548-1-3		1153.66	744,163.16	1,413,568.09	"
	70		N61-34-57W	264.23			
		548-1-3A		1158.25	744,288.94	1,413,335.66	"
	70		N61-34-57W	113.08			
		548-1-4		1154.75	744,342.76	1,413,236.19	"
	71		S01-46-19W	167.01			
		548-1-5		1148.84	744,175.83	1,413,231.03	"
	72		S43-19-50E	117.91			
		548-1-5A		1142.78	744,090.07	1,413,311.92	"
	72		S43-19-50E	99.61			
		548-1-5B		1125.56	744,017.61	1,413,380.27	NOT SET- FALLS IN LAKE
	72		S43-19-50E	20.40			
		548-1-6		—	744,002.78	1,413,394.27	Not Set - Falls in Lake
	73		S01-47-50W	157.18			
		548-1-6A		1142.29	743,845.67	1,413,389.34	Type 3
	73		S01-47-50W	262.30			
		548-1-6B		1147.28	743,583.50	1,413,381.11	"
	73		S01-47-50W	81.13			

SHEET 10 of 11

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 32, T -20-N, R -28-W COUNTY Benton

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		548-1-7= 548-2-1		1131.77	743,502.41	1,413,378.57	Conc. Mon.
	74		N43-22-26W	108.47			
		548-2-1A		1147.37	743,581.26	1,413,304.07	Conc. Mon.
	74		N43-22-26W	129.05			
		548-2-2		1143.89	743,675.08	1,413,215.43	Type 3
	75		S01-45-42W	167.01			
		548-2-3= 549-1		—	743,508.15	1,413,210.30	Not Set in Field
	75		S01-45-42W	334.31			
		549-2= 642-1-1		1132.77	743,174.00	1,413,200.02	
	COURSE 75 REVISED TO SHOW TRACT 653 ADDED IN FEE BK 848-2						
		548-2-2		1143.89	743,675.08	1,413,215.43	SET 1969
	75		S01-48-25W	75.61			
		653-1			743,599.51	1,413,213.05	T-3 SET 11-27-84
	76		N37-01-19W	70.20			
		653-2			743,655.56	1,413,170.78	T-3 SET 11-27-84 IN SEC 31, 20N, R28W
	77		S08-47-41W	227.30			
		653-3			743,430.93	1,413,136.02	T-3 SET 1984 IN SEC 31
	78		S20-15-19E	191.70			
		653-4			743,251.08	1,413,202.39	T-3 SET 1984 ON SEC 4NE
	79		S01-45-42W	77.12			
		549-2= 642-1-1		1132.77	743,174.00	1,413,200.02	SET 1969

SHEET 11 of 11

SWL FORM 136
REVISED FEB. 66
