PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 24, T -20-N, R -29-W COUNTY Benton

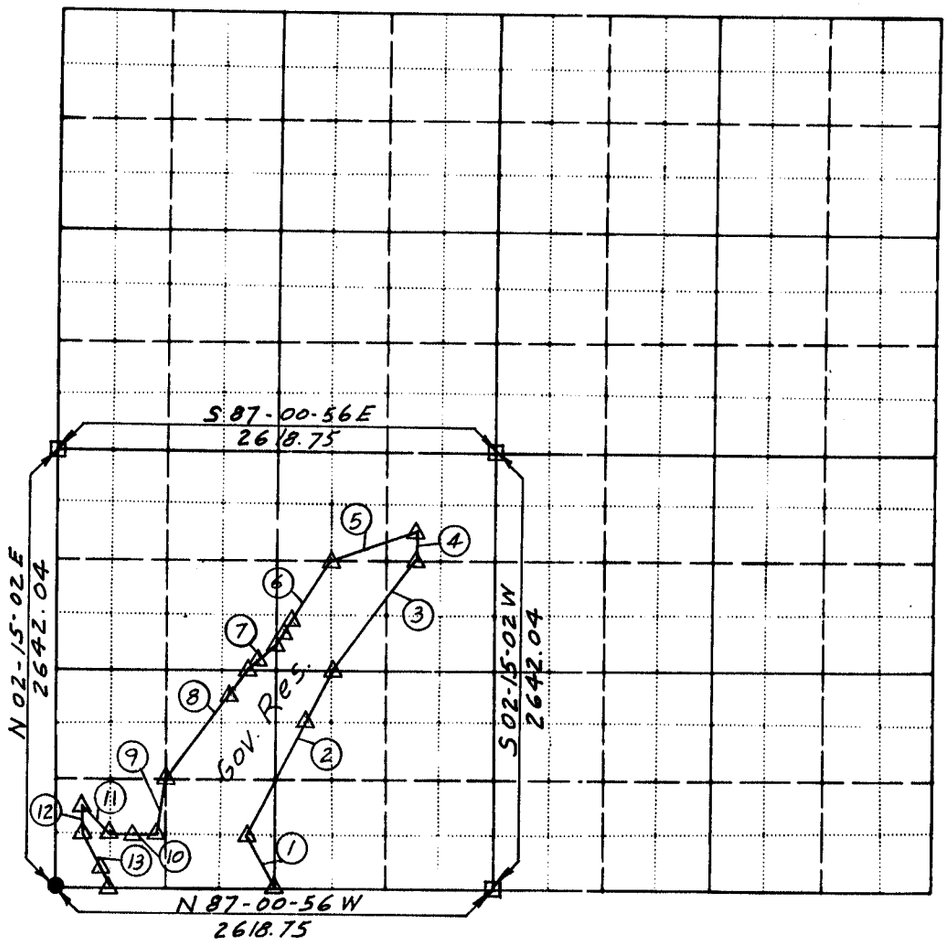

FULL SEC APPROX SCALE 1:12,000

TRACT NO	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		602-1 = 603-9		1176.34	751,769.13	1,404,934.17	18" ROD + CAP TYPE 3
	1		N23-59-03 W	370.46			
		602-2		1127.73	752,107.74	1,404,783.52	30" ROD + CAP TYPE 3
	2		N28-43-36 E	806.86			
		602-2A		1126.81	752,817.05	1,405,171.32	" " "
	2		N28-43-29 E	293.26			
		602-3		1128.68	753,072.60	1,405,312.33	" " "
	3		N39-06-00 E	817.95			

Angle 69-B-12, Chaining 69-B-13 Levels 69B-11

Field Book No. _____ Date: 1969

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____

COUNTY, ARKANSAS

_____

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 2



LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

PARTIAL BOUNDARY SURVEYS
BEAVER RESERVOIR
WHITE RIVER, ARKANSAS

SEC. 24, T -20-N, R -29-W COUNTY Benton

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		602-4		1130.50	753,707.40	1,405,828.22	
	4		N02-13-38 E	165.13			
		602-5		1131.65	753,872.47	1,405,834.64	
	5		S74-17-47 W	516.03			
		602-6		1178.53	753,732.76	1,405,337.78	18" ROD & CAP TYPE 3
	6		S35-53-55W	455.97			
		602-6A		1196.81	753,363.40	1,405,070.42	" " "
	6		S35-53-48W	64.05			
		602-6B		1193.98	753,311.52	1,405,032.85	" " "
	6		S35-53-41W	70.24			
		602-7 = 600-1		1180.13	753,254.65	1,404,991.71	18" ROD & CAP TYPE 3
	7		S47-19-43W	183.57			
		600-1A		1192.23	753,130.23	1,404,856.74	18" ROD & CAP TYPE 3
	7		S47-19-36W	47.43			
		600-2 = 602-8		1180.73	753,098.08	1,404,821.87	" " "
	8		S39-06-37W	159.95			
		602-8A		1196.61	752,974.00	1,404,720.98	" " "
	8		S39-06-31W	582.01			
		602-9		1187.65	752,522.39	1,404,353.87	℄ of road
	9		S09-45-12W	393.92			
		601-1		1143.46	752,134.29	1,404,287.06	18" ROD & CAP TYPE 3
	10		N87-05-07W	131.86			
		601-1A		1155.45	752,141.00	1,404,155.37	18" ROD & CAP TYPE 3
	10		N87-05-07W	188.96			
		601-2		1129.59	752,150.60	1,403,966.65	18" ROD & CAP TYPE 3
	11		N42-11-19W	233.98			
		601-3		1131.37	752,324.03	1,403,809.45	" " "
	12		S02-11-56W	165.13			
		601-4		1131.62	752,159.08	1,403,803.11	" " "
	13		S24-00-41 E	232.19			
		601-4A		1157.35	751,946.48	1,403,897.41	" " "
	13		S23-52-54E	138.88			
		601-5 = 603-10		1152.02	751,820.13	1,403,953.76	" " "

SHEET 2 of 2

SWL FORM 136
REVISED FEB. 66
