BOUNDARY SURVEYS
LAKE DARDANELLE
ARKANSAS RIVER, ARKANSAS

SECTION 2, T 7N, R 21W COUNTY POPE

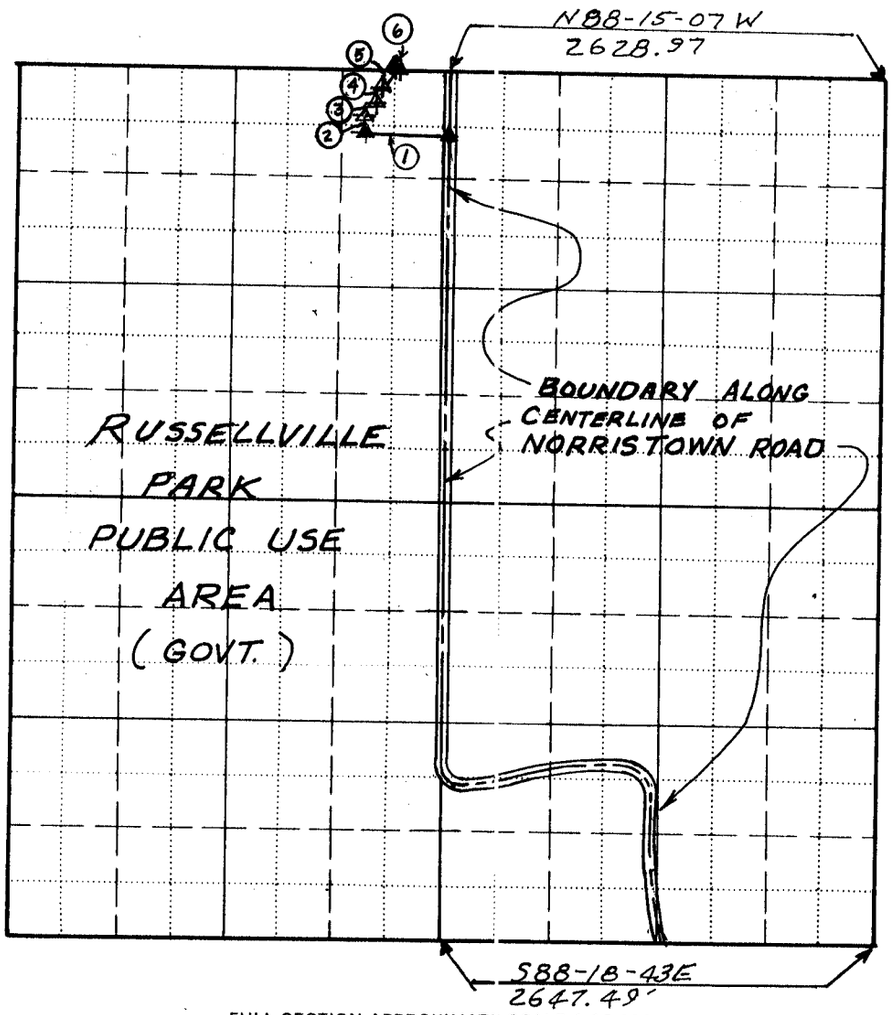

FULL SECTION APPROXIMATE SCALE 1:12,000

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	316-6		358.15	351,537.85	1641,518.94	BOAT SPIKE
1		N88-26-09W	129.72			
	316-5A		349.24	351,541.39	1,641,389.27	T-3
1		N88-26-09W	370.28			
	316-5		343.26	351,551.50	1,641,019.13	CONC. MON.
2		N01-26-02E	105.89			
	385-1-1	*	341.21	351,657.36	1,641,021.78	T-3 *
3		N42-02-51E	95.60			

Field Book No. 65A-60 Date: 1979

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

* Reset by Hale-Martin Associates, 1980. New elevations by same.

COUNTY, ARKANSAS

SURVEYOR REG. NO.

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 OF 2

GN MN

LEGEND
- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 2
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✳ OTHER

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 2, T 7 N., R 21W COUNTY POPE

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION / NORTH	POSITION / EAST	REMARKS
		385-1-2	*	342.06	351,728.35	1,641,085.80	T-3 *
	4		N18-23-51E	100.00'			
		385-1-3= 385-2-1	*	341.58	351,823.24	1,641,117.36	T-3 *
	5		N36-53-51E	154.20'			
		385-2-2		341.05	351,946.55	1,641,209.94	T-3
	6		S89-05-52W	10.16			
		316-1	*	340.84	351,946.39	1,641,199.78	CONC. MON. *

* Reset by Hale-Martin Associates, 1980
New elevations by same.

SHEET 2 of 2

SWL FORM 136
REVISED FEB. 66
