PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 13, T 7N, R 21W COUNTY YELL

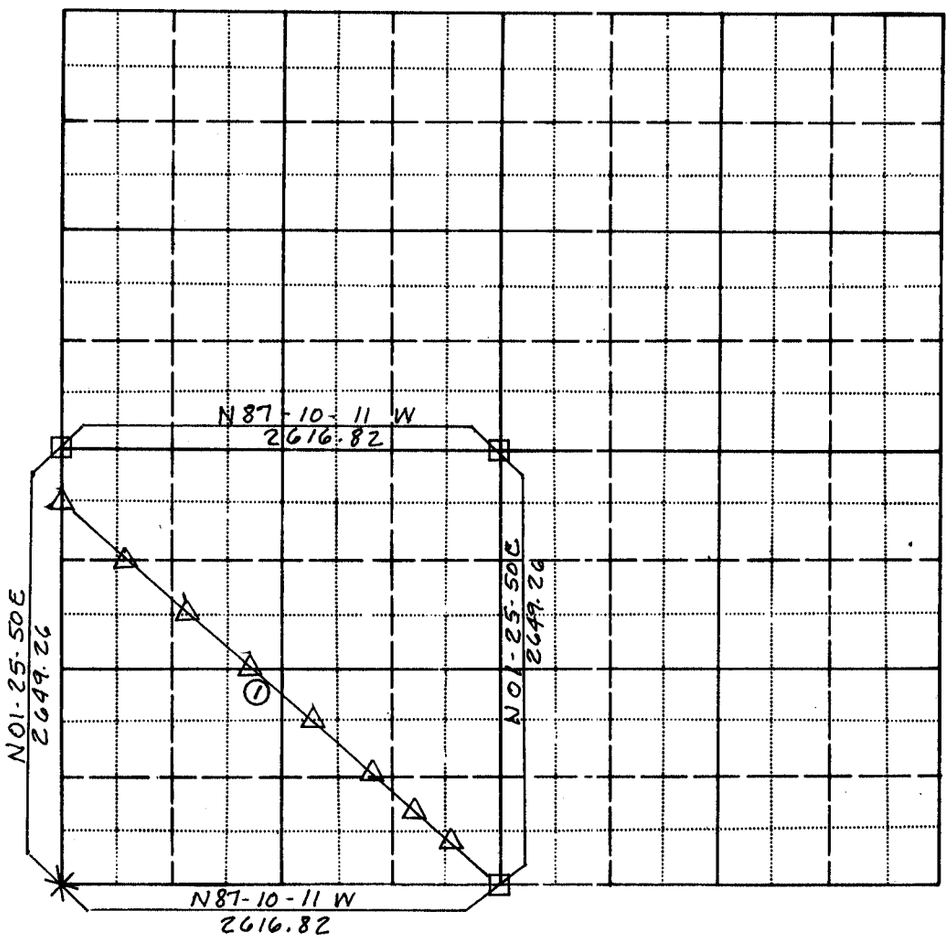

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		123-1		341.50	337,120.14	1,647,423.07	TYPE III
	1		N 47-05-42W	415.83			
		123-1A		360.88	337,403.23	1,647,118.48	TYPE III
	1		N 47-05-42W	300.47			
		123-1B		357.01	337,607.79	1,646,898.39	TYPE III
	1		N 47-05-42W	354.98			
		123-1C		363.24	337,849.45	1,646,638.37	TYPE III
	1		N 47-05-42W	461.95			

Field Book No. 72D-178 18 Date: FEB. 1973

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____

COUNTY, ARKANSAS

_____

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

GN MN

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

SHEET 1 of 2

BOUNDARY SURVEYS
LAKE DARDANELLE
ARKANSAS RIVER, ARKANSAS

SECTION 13 , T 7N , R 21W COUNTY YELL

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	123-1D		385.67	338,163.94	1,646,300.00	TYPE III
1		N 47-05-42 W	458.57			
	123-1E		376.61	338,476.13	1,645,964.11	TYPE III
1		N 47-05-42 W	600.05			
	123-1F		351.20	338,884.63	1,645,524.58	TYPE III
1		N 47-05-42 W	489.13			
	123-1G		345.24	339,217.62	1,645,166.30	TYPE III
1		N 47-05-42 W	470.28			
	123-2		343.06	339,537.78	1,644,821.83	TYPE III

SHEET 2 OF 2

SWL FORM 136
REVISED OCT. 1971

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

FRAC. SEC. 13, T 7-N, R 21-W COUNTY POPE

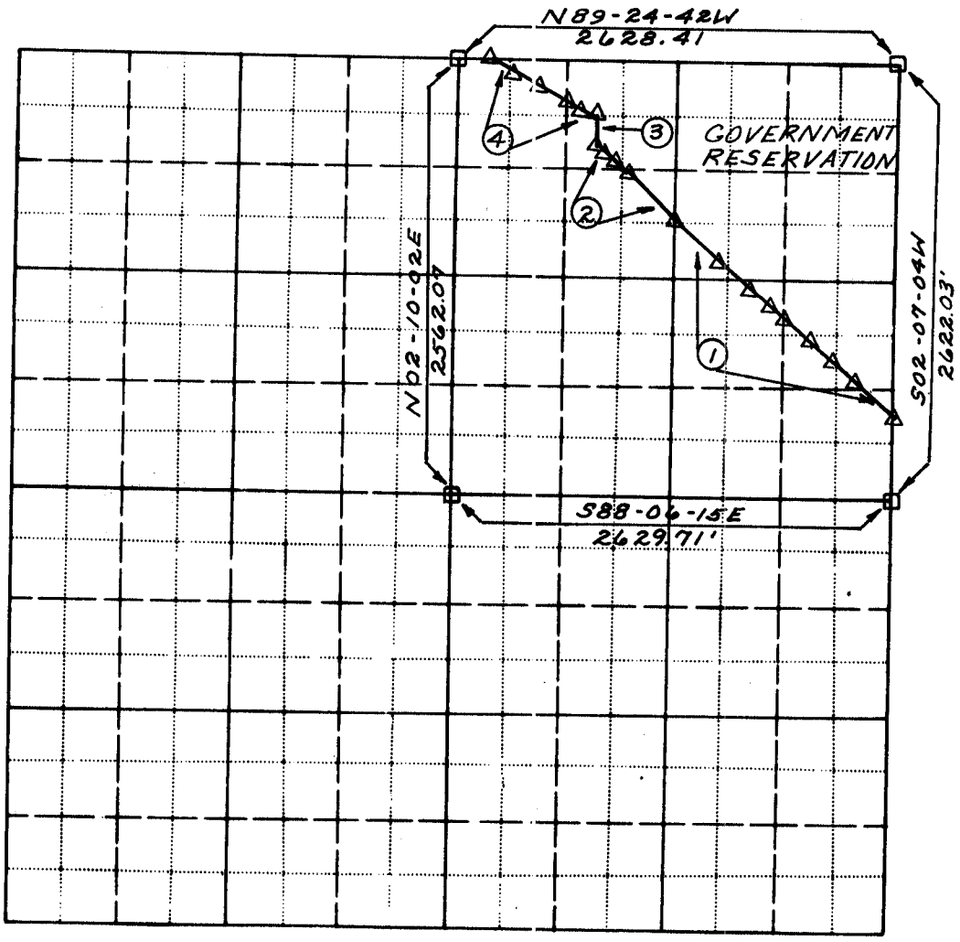

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		100-3=126-1		405.96	339,000.29	1,649,022.28	
	1		N42-35-53W	274.05'			
		126-1A		403.84	339,202.07	1,648,836.79	
	1		N42-35-53W	148.28'			
		126-1B		440.37	339,311.23	1,648,736.42	
	1		N42-35-53W	235.11'			
		126-1C		462.05	339,484.30	1,648,577.29	
	1		N42-35-53W	171.26'			

Field Book No. 67D-13&14 Date: Nov. 67

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____

COUNTY, ARKANSAS

_____

GN MN 0°43'-04" 6°05E

LEGEND

- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 3
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✱ OTHER

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 2

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

FRAC. SEC. 13, T 7 N, R 21 W COUNTY POPE

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		126-1D		456.91	339,610.36	1,648,461.37	
	1		N42-35-53W	45.92'			
		126-1E		464.10	339,644.17	1,648,430.30	
	1		N42-35-53W	135.48'			
		126-1F		451.82	339,743.90	1,648,338.60	
	1		N42-35-53W	306.45'			
		126-1G		417.69	339,969.48	1,648,131.18	
	1		N42-35-53W	231.08'			
		126-2=128-1		397.41	340,139.53	1,647,974.77	
	2		N42-59-38W	415.40'			
		128-1A		430.47	340,443.42	1,647,691.50	
	2		N42-59-38W	261.87'			
		128-1B		415.18	340,634.96	1,647,512.93	
	2		N42-59-38W	21.40'			
		128-2		404.25	340,650.56	1,647,498.33	
	3		N02-07-07E	165.00'			
		128-3		413.80	340,815.45	1,647,504.43	
	4		N61-29-42W	151.32'			
		128-3A		444.45	340,887.72	1,647,371.46	
	4		N61-29-42W	103.16'			
		128-3B		453.43	340,936.95	1,647,280.80	
	4		N61-29-42W	49.52'			
		128-3C		448.18	340,960.58	1,647,237.29	
	4		N61-29-42W	248.68'			
		128-3D		417.89	341,079.26	1,647,018.75	
	4		N61-29-42W	184.08'			
		128-4		394.16	341,167.06	1,646,856.98	

SHEET 2 of 2

SWL FORM 136
REVISED FEB. 66
