PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 2, T 7-N, R 23-W COUNTY LOGAN

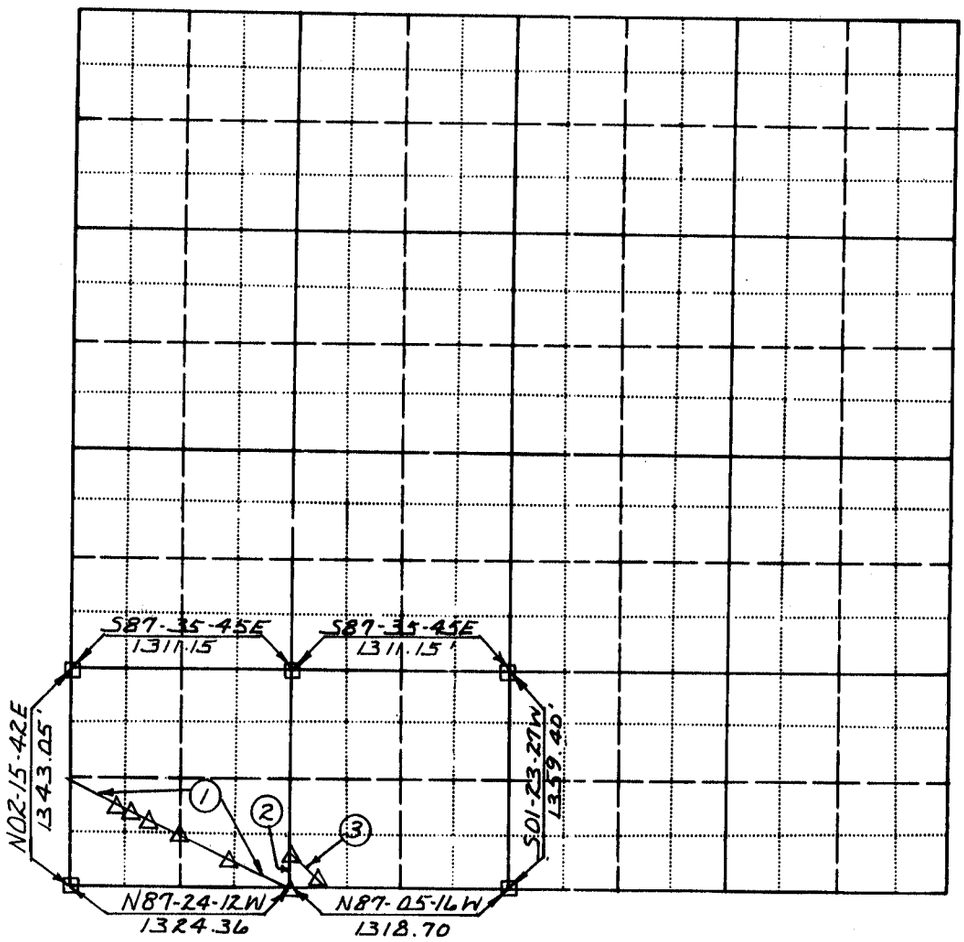

FULL SEC. APPROX. SCALE 1:12,000

Note: Course No. 1 is along old RIR bed.

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1155-8: 1153-1		348.99	350,922.92	1,576,283.53	In Sec. 3
	1		S58-45-13E	362.45'			
		1152-1A		345.72	350,734.89	1,576,593.44	
	1		S58-45-13E	36.30'			
		1152-1B		—	350,716.06	1,576,624.48	In Road Not Set
	1		S58-05-34E	102.60'			
		1152-1C		345.12	350,661.82	1,576,711.58	
	1		S58-05-34E	218.24'			

Field Book No. 68D-16, 69D-2, 69D-1 Date: Jan. 69, Jan. 69

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____
COUNTY, ARKANSAS

GN MN
0°34'21" 6°37'

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 2

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 2, T 7-N, R 23-W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1152-1D		345.12	350,546.46	1,576,896.86	
	1		S63-20-36E	357.26'			
		1152-1E		346.90	350,386.14	1,577,216.22	
	1		S67-07-54E	465.55'			
		1152-2		349.94	350,205.17	1,577,645.30	In Sec. 11
	2		N01-39-18E	160.00'			
		1152-3		342.32	350,365.36	1,577,649.93	
	3		S42-39-30E	216.74'			
		1152-3A		369.31	350,205.90	1,577,796.87	
	3		S42-39-30E	146.18'			
		1152-3B		351.71	350,098.35	1,577,895.97	In Sec. 11

SHEET 2 of 2

SWL FORM 136
REVISED FEB 66
