PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 9, T 7-N, R 23-W COUNTY LOGAN

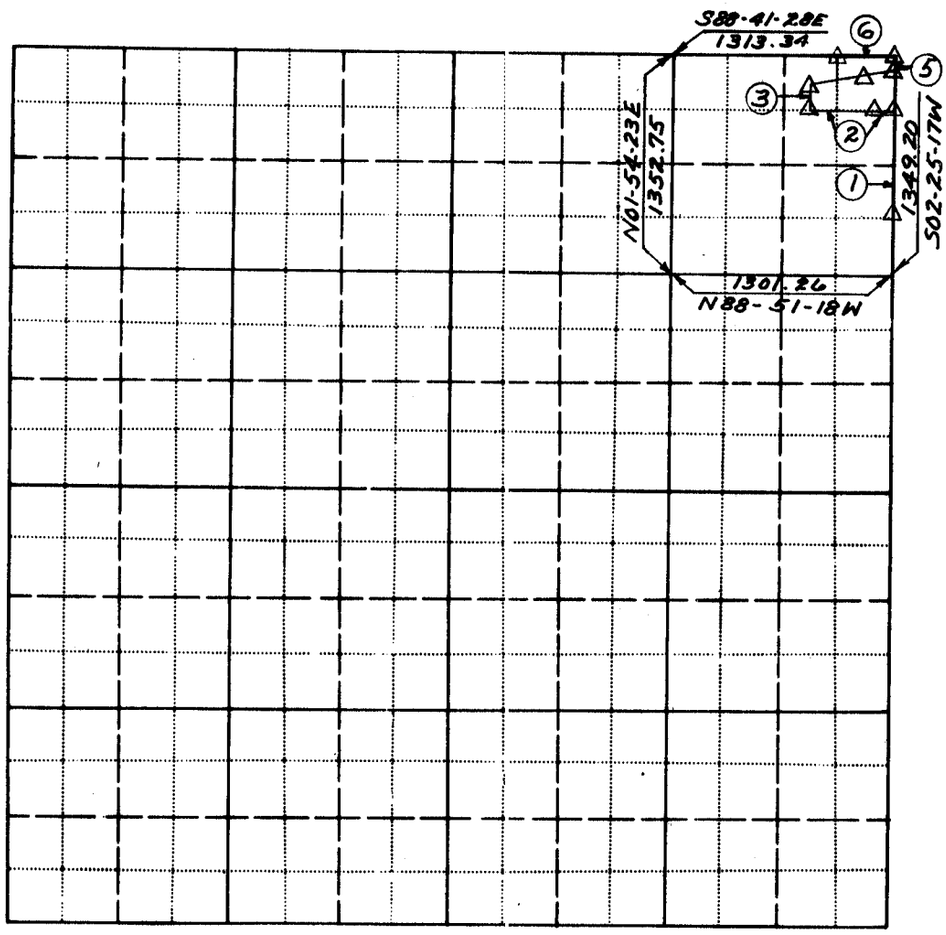

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE	ELEVATION	POSITION		REMARKS
			GRID BEARING	DISTANCE	NORTH	EAST	
		1137-1-4		351.59	349,494.06	1,571,129.44	
	1		N02-33-55E	674.60'			
		1137-1-5= 1136-1		345.33	350,168.00	1,571,159.66	
	2		N88-35-05W	16.30'			
		1136-1A		346.64	350,168.40	1,571,143.36	
	2		N88-35-05W	475.07			
		1136-2		347.87	350,180.13	1,570,668.43	
	3		N02-22-55W	168.81'			

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____

COUNTY, ARKANSAS

Field Book No. 68D-18E19 Date: June 1968

Level Books 69D-15 Feb. 69

68D-17 Jan. 69

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 2

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 9, T -7-N, R -23-W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1136-3		348.87	350,348.80	1,570,675.42	
	4		N83-00-25E	331.27'			
		1136-3A		345.72	350,389.13	1,571,004.23	
	4		N83-00-25E	167.51'			
		1136-4 = 1137-1-6		349.25	350,409.73	1,571,170.49	Nail in Hwy.
	5		N02-33-55E	95.34'			
		1137-1-7 = 1132-2-1		343.76	350,505.04	1,571,175.00	Tie Point
	6		N88-41-28W N89-16-59W	328.34 325.91			COMP. BEAR. & DIST. FIELD BEAR. & DIST.
		1132-2-2		349.24	350,509.12	1,570,849.06	

SHEET 2 of 2

SWL FORM 136
REVISED FEB. 66
