PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 17, T 8-N, R 20-W COUNTY POPE

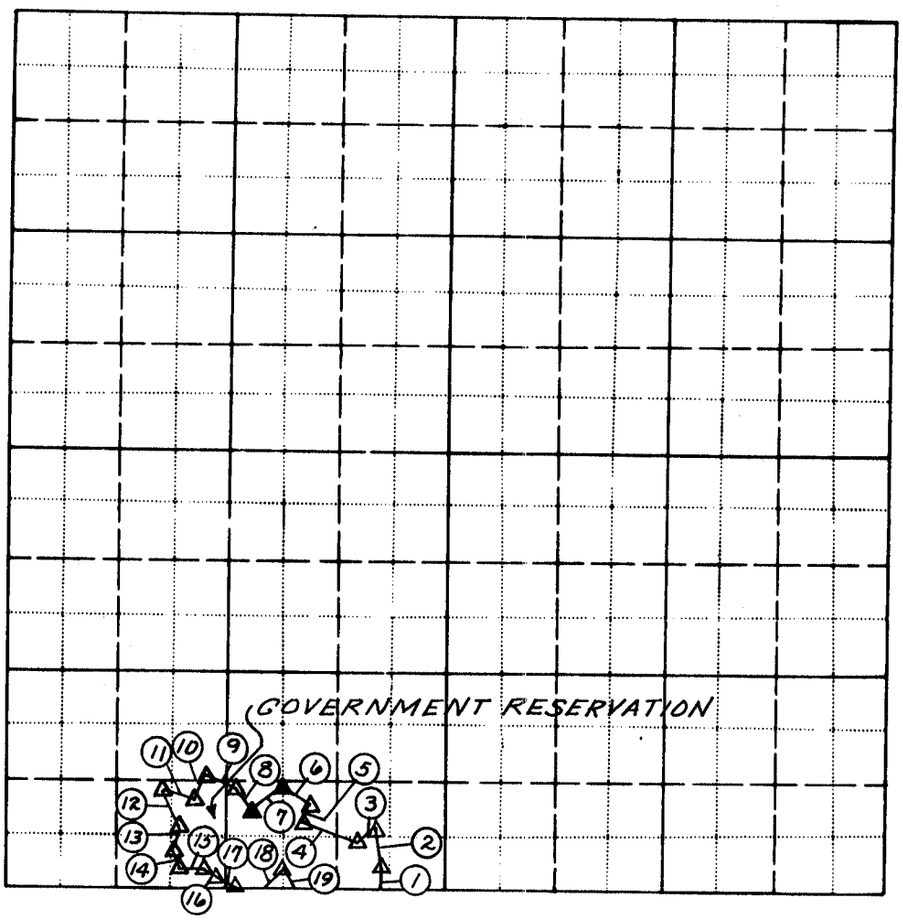

FULL SEC APPROX SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION / NORTH	POSITION / EAST	REMARKS
		TH-D			367,094.74	1,657,932.81	This point in Sec. 20
	1		N01-16-08W	287.89'			
		TH-C			367,382.56	1,657,926.44	
	2		N15-23-50W	191.08'			
		TH-B			367,566.78	1,657,875.70	
	3		S86-13-18W	40.00			
		TH-A			367,564.15	1,657,835.79	
	4		N69-34-42W	379.95			

Field Book No. MA-24 Date: Sept. 1965

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____

COUNTY, ARKANSAS

_____

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 2



LEGEND

- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 3
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✱ OTHER

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 17, T -8-N, R -20-W COUNTY POPE

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		TH-AA			367,696.72	1,657479.72	
	5		N17-42-01E	99.87'			
		245-1			367,791.86	1,657,510.08	
	6		N77-44-27W	136.29'			
		245-2		349.43	367,820.80	1,657,376.90	
	7		S24-30-55W	173.45'			
		245-3		346.21	367,662.99	1,657,304.93	
	8		N09-48-43W	96.97'			
		245-4		344.37	367,758.54	1,657,288.41	
	9		N61-07-35W	51.59'			
		245-5		344.27	367,783.45	1,657,243.23	
	10		S06-04-55W	65.80'			
		245-6		344.22	367,718.02	1,657,236.26	
	11		N63-05-20W	98.89'			
		245-7		344.22	367,762.78	1,657,148.08	
	12		S35-18-58E	164.44'			
		245-8		344.16	367,628.60	1,657,243.14	
	13		S28-37-40W	55.47'			
		245-9		344.47	367,579.92	1,657,216.56	
	14		S08-58-20E	110.26'			
		245-10		347.93	367,471.00	1,657,233.76	
	15		S53-15-12E	43.02'			
		245-11		348.29	367,445.27	1,657,268.23	
	16		S36-20-20E	86.88			
		245-12		348.71	367,375.28	1,657,319.71	
	17		S08-34-42E	40.81'			
		245-13		350.14	367,334.93	1,657,325.80	
		245-15		349.55	367,278.41	1,657,440.11	This Point in Sec. 20
	18		N38-09-33E	84.11'			
		245-16		349.95	367,344.54	1,657,492.08	
	19		S33-17-27E	123.74			
		245-17		350.03	367,241.11	1,657,560.00	This point in Sec. 20

SHEET 2 of 2

SWL FORM 136
REVISED FEB. 66
