PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 16, T -8-N, R -23-W COUNTY LOGAN

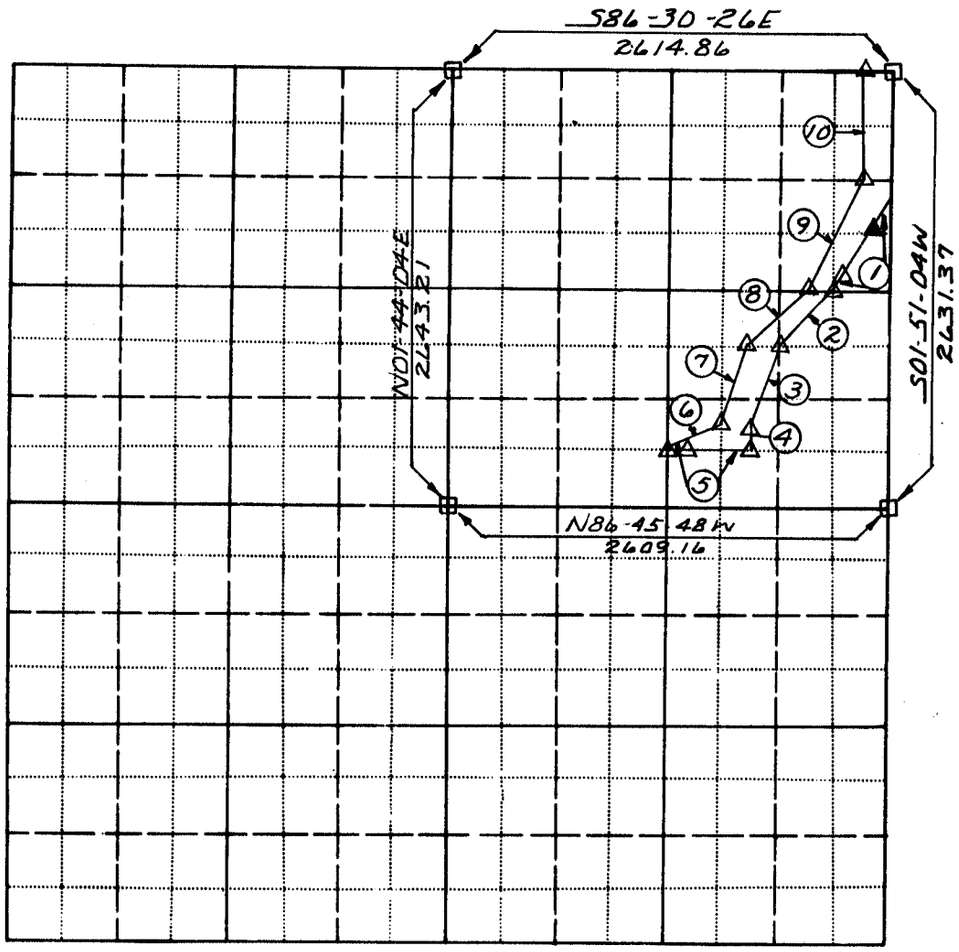

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1502-2-3		346.26	376,487.48	1,571,960.39	This Point in Section 15
	1		S33-14-23W	483.63'			
		1502-2-3A		346.81	376,082.98	1,571,695.29	
	1		S33-14-23W	459.45'			
		1502-2-3B		—	375,698.70	1,571,443.44	Boat Spike & Road
	1		S33-14-23W	3.44'			
		1502-2-4		—	375,695.83	1,571,441.59	Boat Spike in Road
	2		S47-22-06W	457.43'			

Field Book No. 68D-1&2 Date: April 1968
Level Book No 68D-3&4

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____
COUNTY, ARKANSAS

_____

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 2

GN MN
6°34'21" 6°37

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 16, T 8N, R 23W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1502-2-5		348.47	375.386.00	1.571.105.02	
	3		S20-15-55W	516.21'			
		1502-2-6		347.87	374.901.80	1.570.926.25	
	4		S01-49-59W	164.69'			
		1502-2-7		350.06	374.737.23	1.570.920.98	
	5		N86-42-56W	416.56'			
		1502-2-7A		346.88	374,761.11	1.570.504.97	
	5		N86-42-56W	72.80'			
		1502-2-8		349.93	374.765.27	1.570.432.27	
	6		N66-11-57E	361.70'			
		1502-2-9		349.16	374.911.22	1.570.763.15	
	7		N20-15-01E	516.32'			
		1502-2-10		348.57	375,395.68	1.570.941.87	
	8		N47-24-20E	457.47'			Field Bearing & Dist.
		1502-2-11		——	375,705.27	1.571.278.62	
	9		N28-21-05E	722.81'			
		1502-2-12		345.52	376.341.42	1571.622.20	
	10		N01-53-17E	658.03'			
		1502-2-13-1503-2-1		346.67	376.999.46	1.571.643.89	

SHEET 2 of 2

SWL FORM 136
REVISED FEB. 66
