PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 26, T-8-N, R-23W COUNTY LOGAN

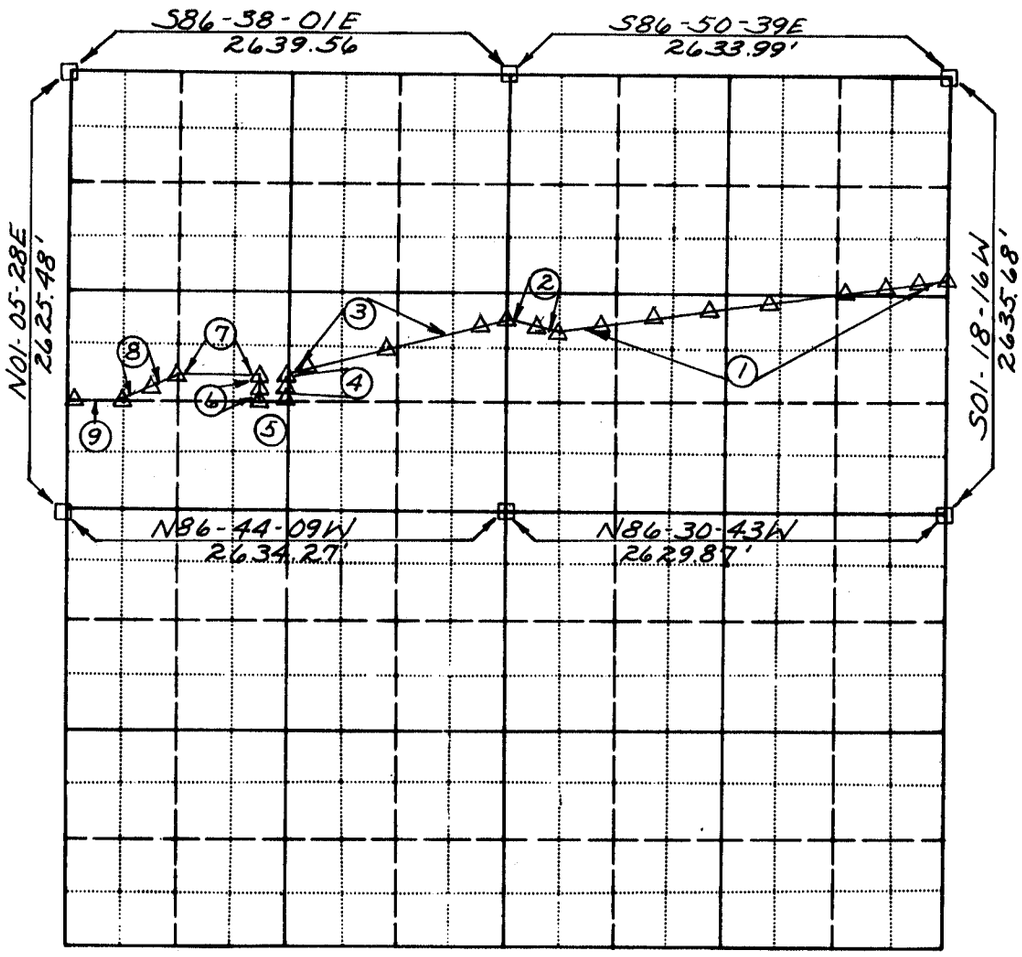

FULL SEC. APPROX. SCALE 1:12,000

NEW BLAINE QUAD

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1308-7		385.50	364,667.53	1,582,053.46	
	1		S83-17-37W	174.49'			
		1308-7A		385.44	364,647.16	1,581,880.17	
	1		S83-17-37W	201.72'			
		1308-7B		401.54	364,623.60	1,581,679.84	
	1		S83-17-37W	238.02'			
		1308-7C		401.12	364,595.81	1,581,443.46	
	1		S83-17-37W	451.04'			

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____

COUNTY, ARKANSAS

_____

Field Book No. 68D-16 & 69D2 Date: March 1969
Level Book No. 69-1 March 1969

GN MN
0°34'21" 6°37'

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 3

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 26, T 8 N, R 23 W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1308-7D		419.64	364,543.14	1,580,995.52	
	1		S83-17-37W	389.14'			
		1308-7E		400.34	364,497.70	1,580,609.06	
	1		S83-17-37W	328.18'			
		1308-7F		403.59	364,459.38	1,580,283.13	
	1		S83-17-37W	308.61'			
		1308-7G		385.53	364,423.34	1,579,976.65	
	1		S83-17-37W	231.50'			
		1308-8		355.11	364,396.31	1,579,746.74	
	2		N72-36-06W	112.83'			
		1308-8A		351.35	364,430.04	1,579,639.10	
	2		N72-36-06W	230.74'			
		1308-9- 1309-1		339.13	364,499.02	1,579,418.95	
	3		S79-06-54W	161.33'			
		1309-1A		344.61	364,468.56	1,579,260.53	
	3		S79-06-54W	594.97'			
		1309-1B		339.90	364,356.21	1,578,676.27	IN LAKE
	3		S79-06-54W	490.77'			
		1309-1C		338.34	364,263.54	1,578,194.34	IN LAKE
	3		S79-06-54W	100.00'			
		1309-2		——	364,244.65	1,578,096.14	In Lake
	4		S01-10-40W	100.00'			
		1309-2A		344.29	364,144.66	1,578,094.07	
	4		S01-10-40W	65.00'			
		1309-3		346.76	364,079.65	1,578,092.74	
	5		N86-42-50W	165.08'			
		1309-4		358.18	364,089.11	1,577,927.95	
	6		N01-09-10E	83.69'			
		1309-4A		345.39	364,172.75	1,577,929.63	
	6		N01-09-10E	81.31'			
		1309-5		——	364,254.04	1,577,931.27	In Lake
	7		N86-43-19W	495.30			
		1309-6		——	364,282.36	1,577,436.80	In Lake
	8		S66-06-11W	162.03'			

SHEET 2 of 3

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 26, T 8-N, R 23-W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1309-6A		338.54	364,216.71	1,577,288.67	
	8		S66-06-11W	198.95'			
		1309-7		341.41	364,136.11	1,577,106.77	
	9		N86-58-04W	305.41'			
		1309-7A		348.45	364,152.26	1,576,801.81	
	9		N86-58-04W	352.84'			
		1309-8		338.93	364,170.92	1,576,449.50	In Sec. 27

SHEET 3 of 3

SWL FORM 136
REVISED FEB 66
