PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 33, T -8-N, R -23-W COUNTY LOGAN

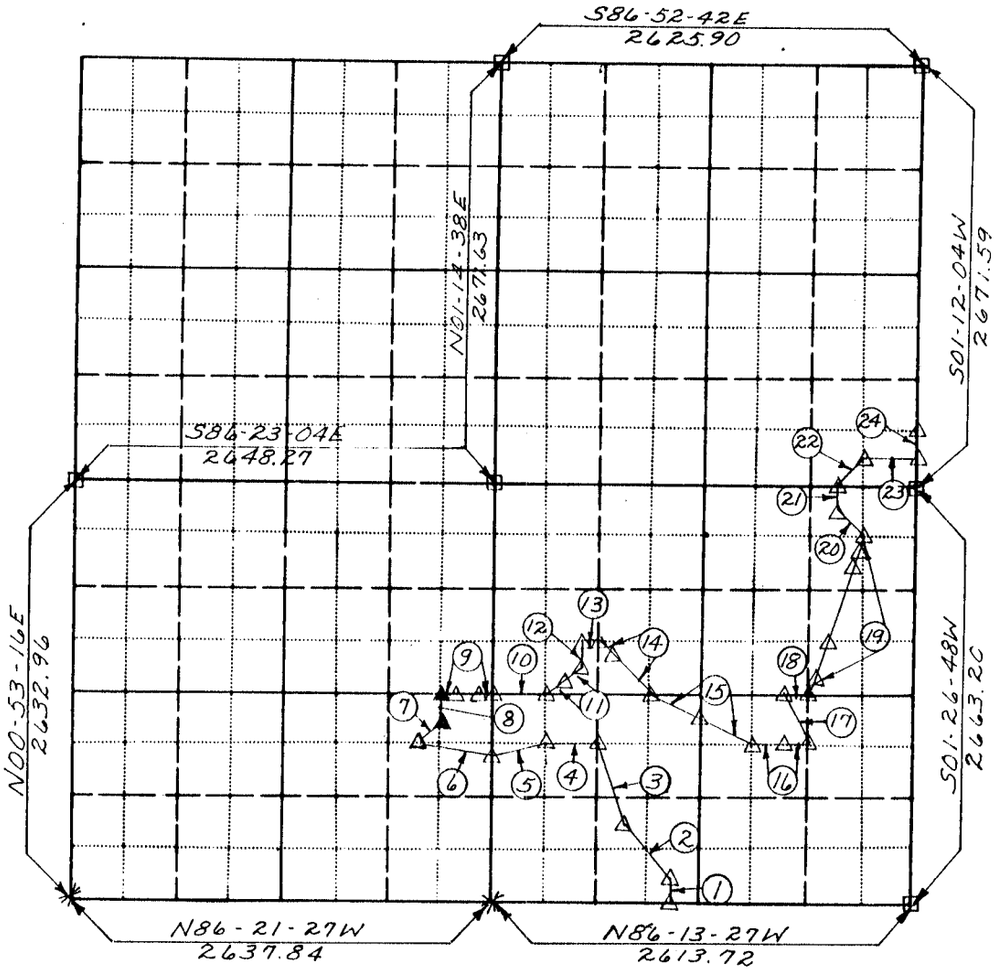

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1114-1= 1112-2-2		355.38	355,998.37	1,569,855.01	
	1		N01-20-28E	165.41'			
		1114-2		340.95	356,163.67	1,569,858.88	
	2		N42-09-12E	474.80'			
		1114-3		348.15	356,515.58	1,569,540.31	
	3		N16-44-51W	528.10'			
		1114-4		350.62	357,021.11	1,569,388.19	
	4		N86-24-00W	327.38'			

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____

COUNTY, ARKANSAS

_____

Field Book No. 68D-17 & 18 Date: June 1968
Level Book No. 68 D-19

GN MN
0°34'21" 6°37'

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 3

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 33, T 8 N, R 23 W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1114-5		356.76	357,041.66	1,569,061.46	
	5		S79-21-43W	334.18			
		1114-6= 1113-1		363.13	356,979.97	1,568,733.00	
	6		N76-55-56W	505.67'			
		1113-2		348.60	357,094.29	1,568,240.46	
	7		N47-31-40E	227.90'			
		1113-3		348.60	357,248.14	1,568,408.52	
	8		N01-09-39E	164.61'			
		1113-4		351.51	357,412.66	1,568,411.85	
	9		S86-18-09E	92.17'			
		1113-4A		355.51	357,406.71	1,568,503.83	
	9		S86-18-09E	124.03'			
		1113-4B		363.59	357,398.71	1,568,627.60	
	9		S86-18-09E	93.39			
		1113-4C		360.34	357,392.69	1,568,720.80	
	9		S86-18-09E	20.79			
		1113-5= 1115-1		——	357,391.35	1,568,741.55	Not Set In Road
	10		S86-29-36E	36.45'			
		1115-1A		357.32	357,389.12	1,568,777.93	
	10		S86-29-36E	291.15'			
		1115-2		346.50	357,371.31	1,569,068.54	
	11		N58-55-15E	143.65'			
		1115-2A		356.48	357,445.46	1,569,191.54	
	11		N58-55-15E	146.86'			
		1115-3		346.11	357,521.26	1,569,317.30	
	12		N01-13-57E	165.02'			
		1115-4		347.88	357,686.18	1,569,320.84	
	13		S86-35-12E	81.95'			
		1115-5= 1119-2-1		351.78	357,681.30	1,569,402.65	
	14		S42-25-21E	112.16'			
		1115-5A		359.82	357,598.48	1,569,478.33	
	14		S42-25-21E	361.97'			
		1119-2-2= 1115-6		352.66	357,331.22	1,569,722.59	
	15		S59-26-11E	352.44'			

SHEET 2 of 3

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 33, T -8-N, R -23-W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1115-6A		346.03	357,152.01	1,570,026.06	
	15		S59-26-11E	397.34'			
		1115-7		346.42	356,949.96	1,570,368.20	
	16		S86-25-39E	196.19'			
		1115-7A		354.70	356,937.74	1,570,564.01	
	16		S86-25-39E	131.16'			
		1115-8		350.89	356,929.56	1,570,694.95	
	17		N23-44-30W	384.22'			
		1115-9		363.83	357,281.26	1,570,540.26	
	18		S86-31-05E	163.80'			
		1115-10= 1119-1-1		349.74	357,271.32	1,570,703.76	
	19		N19-55-00E	81.47'			
		1119-1-1A		356.70	357,347.92	1,570,731.51	
	19		N19-55-00E	276.65'			
		1119-1-1B		344.23	357,608.02	1,570,825.75	
	19		N19-55-00E	490.42'			
		1119-1-1C		352.34	358,069.11	1,570,992.81	
	19		N19-55-00E	119.92'			
		1119-1-1D		348.69	358,181.86	1,571,033.66	
	19		N19-55-00E	70.49'			
		1119-1-2		339.67	358,248.16	1,571,057.64	
	20		N42-42-52W	238.48'			
		1119-1-3		341.04	358,423.38	1,570,895.87	
	21		N01-24-05E	166.10'			
		1119-1-4= 1116-1		349.68	358,589.37	1,570,899.93	
	22		N46-41-56E	230.28'			
		1116-2		357.77	358,747.27	1,571,067.47	
	23		S86-51-13E	328.47'			
		1116-3= 1117-1		345.94	358,729.24	1,571,395.45	
	24		N01-13-37E	166.98'			
		1117-2		351.29	358,896.12	1,571,399.02	

SHEET 3 of 3

SWL FORM 136
REVISED FEB. 66
