BOUNDARY SURVEYS
LAKE DARDANELLE
ARKANSAS RIVER, ARKANSAS

SECTION 1, T 8 N, R 26 W COUNTY FRANKLIN

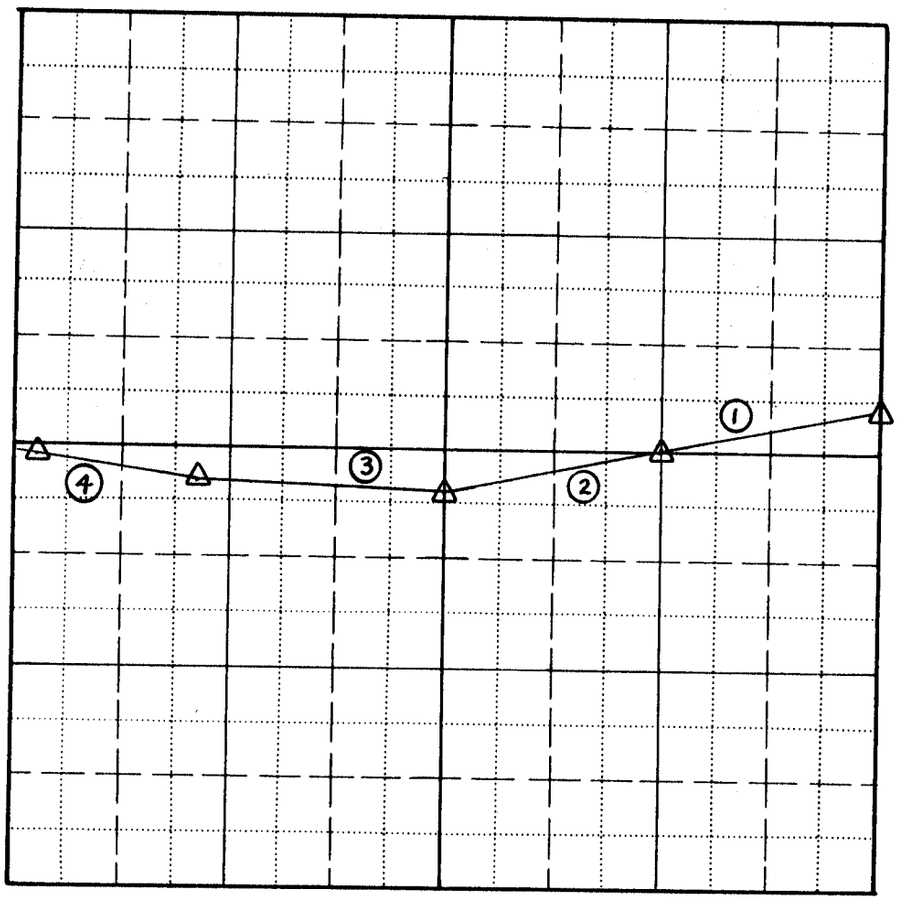

FULL SECTION APPROXIMATE SCALE 1:12,000

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	2821-5 = 2820-1			387,088.00	1,490,404.43	△
1		S 84-00-28 W	1331.68			
	2814-1 = 2820-2			386,949.01	1,489,080.30	△
2		S 81-21-21 W	1349.34			
	2819-2 = 3004-1			386,746.21	1,487,746.29	△
3		N 85-51-47 W	1579.60			
	3004-2			386,860.16	1,486,170.81	△
4		N 80-11-06 W	1063.63			

Field Book No. 70 D-1, 70 D-2 Date: _____

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____
COUNTY, ARKANSAS

_____ _____
SURVEYOR REG. NO.

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS
SHEET 1 OF 2

GN MN

LEGEND
- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 3
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✳ OTHER

BOUNDARY SURVEYS
LAKE DARDANELLE
ARKANSAS RIVER, ARKANSAS

SECTION 1 , T 8 N , R 26 W COUNTY JOHNSON

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	3004-2A			387,041.51	1,485,122.64	△
4		N 80-11-06 W	1028.47			
	3019-2			387,216.84	1,484,109.11	△ IN SEC.2

SHEET 2 OF 2

SWL FORM 136
REVISED OCT. 1971
