BOUNDARY SURVEYS
LAKE DARDANELLE
ARKANSAS RIVER, ARKANSAS

SECTION 3, T 8 N, R 26 W COUNTY FRANKLIN

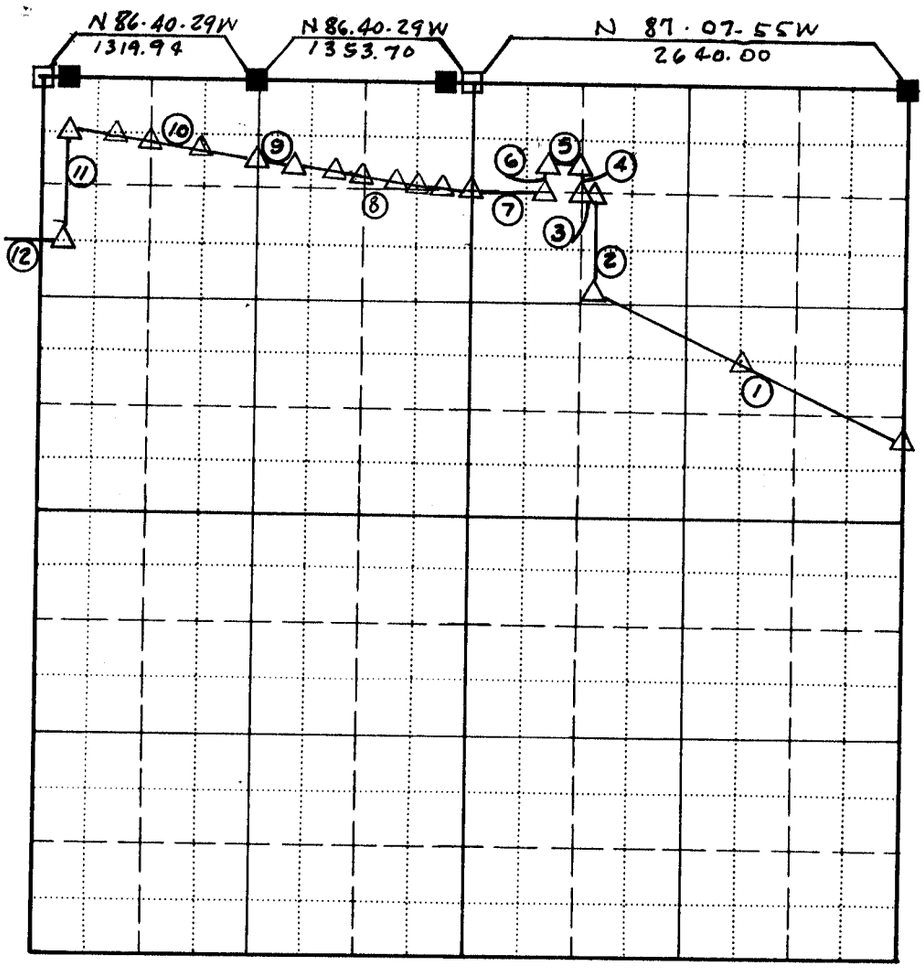

FULL SECTION APPROXIMATE SCALE 1:12,000

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	3019-5: 3018-1			387,901.67	1,479,844.93	TYPE III
1		N 64-41-21 W	1050.03			
	3018-1A			388,350.79	1,478,895.33	TYPE III
1		N 64-41-21 W	1051.65			
	3018-2			388,800.56	1,477,944.25	TYPE III
2		N 01-19-40 W	637.48			
	3018-3			389,438.58	1,477,929.46	TYPE III
3		S 88-40-13 W	75.00			

Field Book No. 70D-1 70D-2 73D-10-14 Date: MAY 1973

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

COUNTY, ARKANSAS

SURVEYOR REG. NO.

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS
SHEET 1 OF 2

GN MN

LEGEND

- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 2
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✳ OTHER

BOUNDARY SURVEYS
LAKE DARDANELLE
ARKANSAS RIVER, ARKANSAS

SECTION 3 , T 8N , R 26W COUNTY FRANKLIN

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	3018-4			389,436.84	1,477,854.49	TYPE III
4		N01-19-55W	120.00			
	3018-5			389,556.94	1,477,851.70	TYPE III
5		S88-39-58W	100.00			
	3018-6			389,554.62	1,477,751.74	TYPE III
6		S01-20-10E	114.69			
	3018-7			389,440.08	1,477,754.41	TYPE III
7		N86-41-08W	468.51			
	3018-8		367.19	389,467.66	1,477,286.90	TYPE III
8		N79-11-31W	257.45			
	3018-8A		370.97	389,516.21	1,477,034.14	TYPE III
8		N79-11-31W	293.22			
	3018-8B		373.67	389,571.50	1,476,746.25	TYPE III
8		N79-11-31W	228.37			
	3018-8C		380.64	389,614.58	1,476,522.04	TYPE III
8		N79-11-31W	117.90			
	3018-8D		380.48	389,638.81	1,476,406.69	TYPE III
8		N79-11-31W	117.90			
	3018-8E		386.33	389,659.00	1,476,290.56	TYPE III
8		N79-11-31W	181.56			
	3018-9 = 3015-1		379.34	389,693.18	1,476,112.30	TYPE III
9		N87-08-22W	169.21			
	3015-2		374.01	389,701.80	1,475,943.37	TYPE III
10		N79-05-45W	442.86			
	3015-2A		368.55	389,786.04	1,475,508.72	TYPE III
10		N79-05-45W	138.54			
	3015-2B		372.73	389,812.39	1,475,372.73	TYPE III
10		N79-05-45W	457.00			
	3015-2C		371.17	389,899.36	1,474,923.68	TYPE III
10		N79-05-45W	200.22			
	3015-3		365.72	389,937.44	1,474,727.17	" "
11		S02-17-54W	610.63			
	3014-1 = 3015-4			389,327.30	1,474,702.68	NOT SET IN FIELD
12		N86-58-07W	1420.23			
	3014-2		356.06	389,402.40	1,473,284.44	IN SEC. 4

SHEET 2 OF 2

SWL FORM 136
REVISED OCT. 1971
