PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 23, T -8-N, R -26-W COUNTY LOGAN

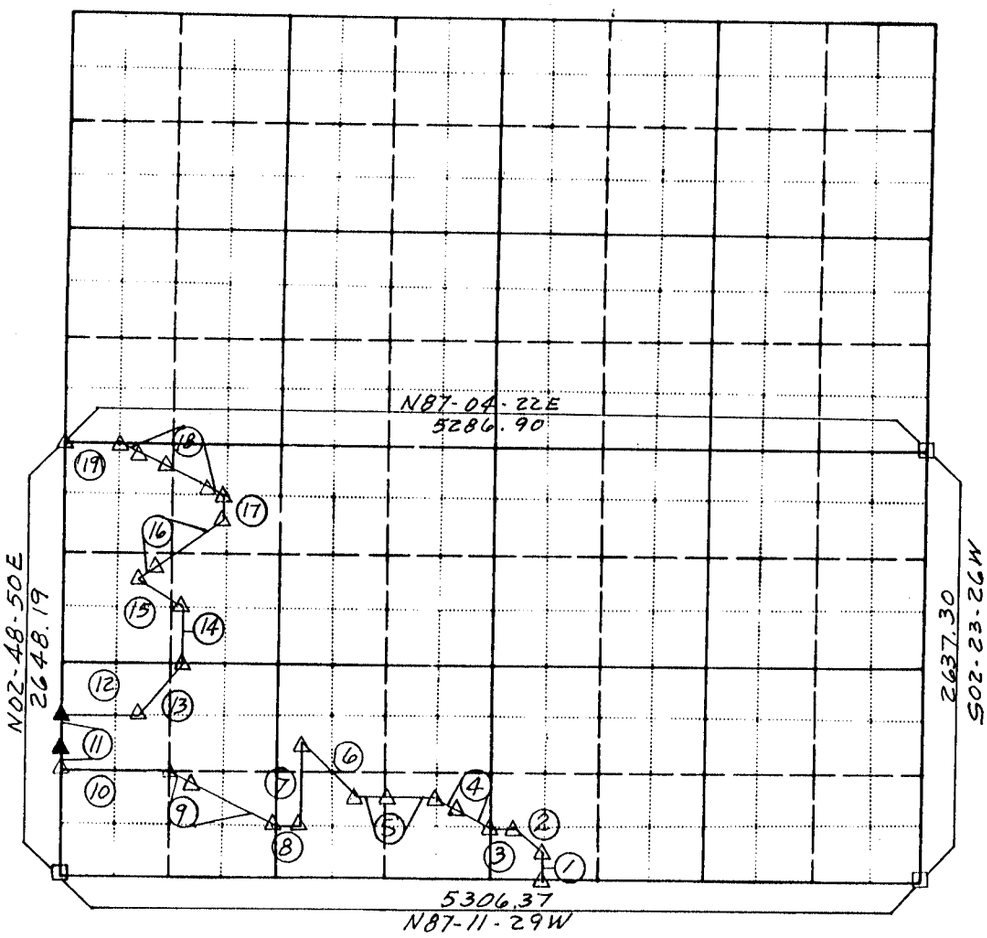

FULL SEC APPROX SCALE 1:12,000

TRACT NO	COURSE NO	MONUMENT NO	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		3234-5= 3231-1		374.72	370,772.83	1,484,759.14	
	1		N02-36-00E	165.13			
		3231-2		372.15	370,937.78	1,484,766.63	
	2		N42-23-04W	234.47			
		3231-3		415.40	371,110.94	1,484,608.61	
	3		N87-09-08W	165.75			
		3231-4= 3233-1		417.66	371,119.17	1,484,443.10	
	4		N60-42-14W	304.02			

Field Book No. 71D-13, 14 Date: 1971
Level Book No. 71D-15

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION 23, T -8-N, R -26-W.

COUNTY, ARKANSAS

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 3



LEGEND

- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 3
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✱ OTHER

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 23, T - 8-N, R - 26-W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		3233-1A		412.31	371,267.91	1,484,178.03	
	4		N60-42-14W	66.87			
		3233-2		397.38	371,300.62	1,484,119.72	
	5		N87-09-21W	297.11			
		3233-2A		385.85	371,315.36	1,483,823.05	
	5		N87-09-21W	200.02			
		3233-3		379.17	371,325.28	1,483,623.33	
	6		N42-17-27W	468.70			
		3233-4		369.11	371,671.93	1,483,308.00	
	7		S02-42-29W	495.96			
		3233-5		362.56	371,176.52	1,483,284.57	
	8		N87-09-35W	165.75			
		3233-6 = 3141-1		368.66	371,184.73	1,483,119.07	
	9		N60-38-41W	580.42			
		3141-1A		384.97	371,469.20	1,482,613.30	
	9		N60-38-41W	160.86			
		3141-2		384.49	371,548.04	1,482,473.12	
	10		N87-08-47W	662.68			
		3141-3		391.24	371,581.02	1,481,811.43	
	11		N02-50-07E	131.01			
		3141-3A		364.05	371,711.87	1,481,817.91	
	11		N02-50-07E	200.01			
		3141-4		361.22	371,911.63	1,481,827.81	
	12		S87-07-59E	496.79			
		3141-5		357.34	371,886.78	1,482,324.10	
	13		N39-41-58E	413.36			
		3141-6		358.08	372,204.86	1,482,588.17	
	14		N02-45-54E	330.83			
		3141-7		359.28	372,535.30	1,482,604.13	
	15		N53-27-10W	298.52			
		3141-8		360.66	372,713.03	1,482,364.36	
	16		N59-09-44E	50.00			
		3141-8A		—	372,738.66	1,482,407.30	
	16		N59-09-44E	545.61			

SHEET 2 of 3

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 23, T -8-N, R -26-W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		3141-9		357.71	373,018.41	1,482,875.87	
	17		N02-44-38E	165.38			
		3141-10		364.79	373,183.60	1,482,883.78	
	18		N60-30-32W	124.44			
		3141-10A		372.45	373,244.85	1,482,775.50	
	18		N60-30-32W	305.29			
		3141-10B		356.00	373,395.11	1,482,509.82	
	18		N60-30-32W	208.75			
		3141-10C		374.44	373,497.85	1,482,328.16	
	18		N60-30-32W	101.53			
		3141-11		369.80	373,547.82	1,482,239.80	
	19		N87-03-42W	330.43			
		3141-12		375.68	373,564.75	1,481,909.89	

SHEET 3 of 3

SWL FORM 136
REVISED FEB. 66
