PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 36, T -8-N, R -26-W COUNTY LOGAN

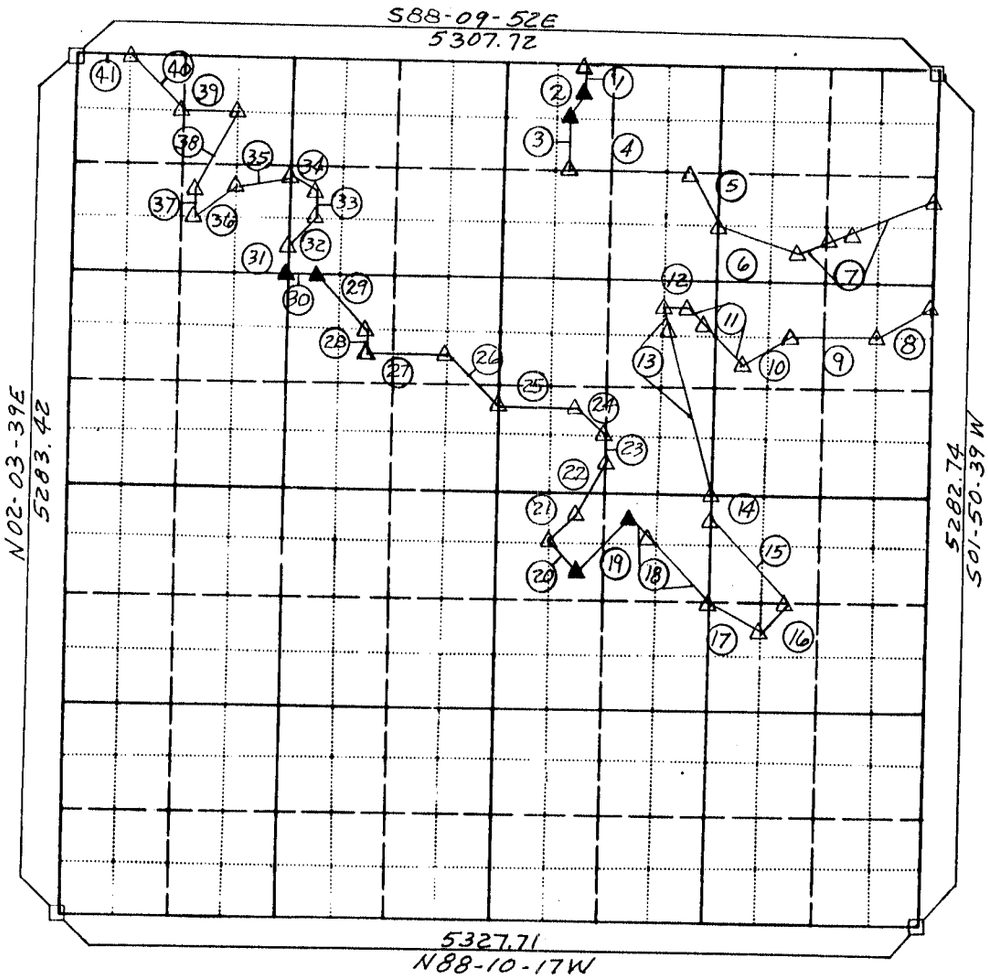

FULL SEC. APPROX SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		3213-4 = 3212-1		—	365,309.75	1,490,035.43	Not Set
	1		S01-56-33W	165.10			
		3212-2		357.35	365,144.34	1,490,029.84	
	2		S28-35-36W	184.89			
		3212-3		358.57	364,982.00	1,489,941.36	
	3		S01-56-38W	330.19			
		3212-4		356.08	364,652.06	1,489,930.16	
	4		S88-09-19E	746.75			

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION 36, T-8-N, R-26-W.

COUNTY, ARKANSAS

Field Book No. 71D-20, 21 Date: 1971
Level Book No. 71D-22

GN MN
0° 57'38" 06°46'04"

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 4

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 36, T-8-N, R-26-W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		3212-5		359.52	364,628.03	1,490,676.36	
	5		S24-47-16E	369.37			
		3212-6 = 3207-1		354.12	364292.77	1,490,831.18	
	6		S69-48-14E	524.48			
		3207-2		360.99	364,111.75	1,491,323.29	
	7		N69-46-52E	241.19			
		3207-2A		371.04	364,195.10	1,491,549.58	
	7		N69-46-52E	100.92			
		3207-2B		357.72	364,229.97	1,491,644.27	
	7		N69-46-52E	554.09			
		3207-3 = 3206-1		365.76	364,421.44	1,492,164.15	
		3219-3 = 3208-1		365.71	363,728.02	1,492,140.58	
	8		S69-12-56W S69-45-41W	358.94 360.30			Computed Bearing & Dist. Field Bearing & Dist.
		3208-2		355.60	363,603.43	1,491,802.61	Tie Point
	9		N88-15-09W	498.18			
		3208-3		352.25	363,618.62	1,491,304.83	
	10		S65-20-02W	371.04			
		3208-4		360.28	363,463.82	1,490,967.76	
	11		N43-22-42W	382.18			
		3208-4A		367.42	363,741.54	1,490,705.32	
	11		N43-22-42W	85.87			
		3208-5		359.05	363,803.94	1,490,646.36	
	12		N88-14-27W	166.05			
		3208-6		350.30	363,809.04	1,490,480.44	
	13		S14-12-11E	94.15			
		3208-6A		360.70	363,717.77	1,490,503.54	
	13		S14-12-11E	1,107.89			
		3208-7 = 3209-1		356.88	362,643.70	1,490,775.35	
	14		S01-50-05W	165.09			
		3209-2		356.11	362,478.71	1,490,770.07	
	15		S43-23-44E	702.49			
		3209-3		359.93	361,968.16	1,491,252.79	

SHEET 2 of 4

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 36, T -8-N, R - 26-W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	16		S 47-00-26W	234.40			
		3209-4		357.59	361,808.36	1,491,081.39	
	17		N61-48-23W	371.09			
		3209-5 = 3211-1		355.17	361,983.64	1,490,754.42	
	18		N43-22-07W	586.02			
		3211-1A		360.93	362,409.55	1,490,352.08	
	18		N43-22-07W	116.35			
		3211-2		356.76	362,494.12	1,490,272.20	
	19		S47-02-09W	468.93			
		3211-3		358.49	362,174.61	1,489,929.14	
	20		N43-20-41W	234.07			
		3211-4		361.66	362,344.81	1,489,768.51	
	21		N47-02-30E	234.49			
		3211-5		357.17	362,504.65	1,489,940.17	
	22		N28-35-40E	369.90			
		3208-9		355.12	362,829.50	1,490,117.25	
	23		N01-54-21E	165.09			
		3208-10		353.89	362,994.51	1,490,122.74	
	24		N43-19-28W	234.01			
		3208-11		359.33	363,164.71	1,489,962.21	
	25		N88-11-18W	498.35			
		3208-12 = 3214-1		358.45	363,180.46	1,489,464.28	
	26		N43-18-07W	467.88			
		3214-2		356.51	363,520.89	1,489,143.44	
	27		N88-10-57W	498.24			
		3214-3		362.07	363,536.69	1,488,645.63	
	28		N01-58-14E	165.10			
		3214-4		358.96	363,701.70	1,488,651.30	
	29		N43-15-36W	467.66			
		3214-5		360.25	364,042.21	1,488,330.87	
	30		N88-10-25W	166.02			
		3214-6 = 3212-7		362.23	364,047.50	1,488,164.99	
	31		N02-00-23E N02-00-55E	165.10 163.34			Computed Bearing & Dist. Field Bearing & Dist.
		3212-8		359.79	364,210.80	1,488,170.74	Tie Point

SHEET 3 of 4

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 36, T -8-N, R-26-W COUNTY LOGAN

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	32		N47-05-55E	234.47			
		3212-9		357.66	364,370.43	1,488,342.51	
	33		N02-01-54E	165.10			
		3212 10		358.37	364,535.49	1,488,348.37	
	34		N61-39-06W	185.14			
		3212-11		355.90	364,623.42	1,488,185.38	
	35		S82-13-23W	336.86			
		3212-12= 3221-1		358.60	364,577.84	1,487,851.58	
	36		S54-24-23W	314.41			
		3221-2		362.68	364,394.85	1,487,595.93	
	37		N02-03-22E	153.21			
		3221-3= 3222-2-1		360.43	364,548.02	1,487,601.43	
	38		N28-08-37E	565.77			
		3222-2-2= 3222-1-1		359.12	365,047.01	1,487,868.36	
	39		N88-08-39W	331.81			
		3222-1-2		357.56	365,057.76	1,487,536.67	
	40		N43-10-40W	487.25			
		3222-1-3		360.60	365,413.21	1,487,203.14	
	41		N88-03-11W	628.04			
		3222-1-3A		363.17	365,434.55	1,486,575.35	In Sec. 26
	41		N88-03-11W	200.03			
		3222-1-3B		362.54	365,441.34	1,486,375.40	In Sec. 26
	41		N88-03-11W	156.04			
		3251-1		362.81	365,446.65	1,486,219.43	In Sec. 26

SHEET 4 of 4

SWL FORM 136
REVISED FEB. 66
