PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 14, T 9N, R 22W COUNTY JOHNSON

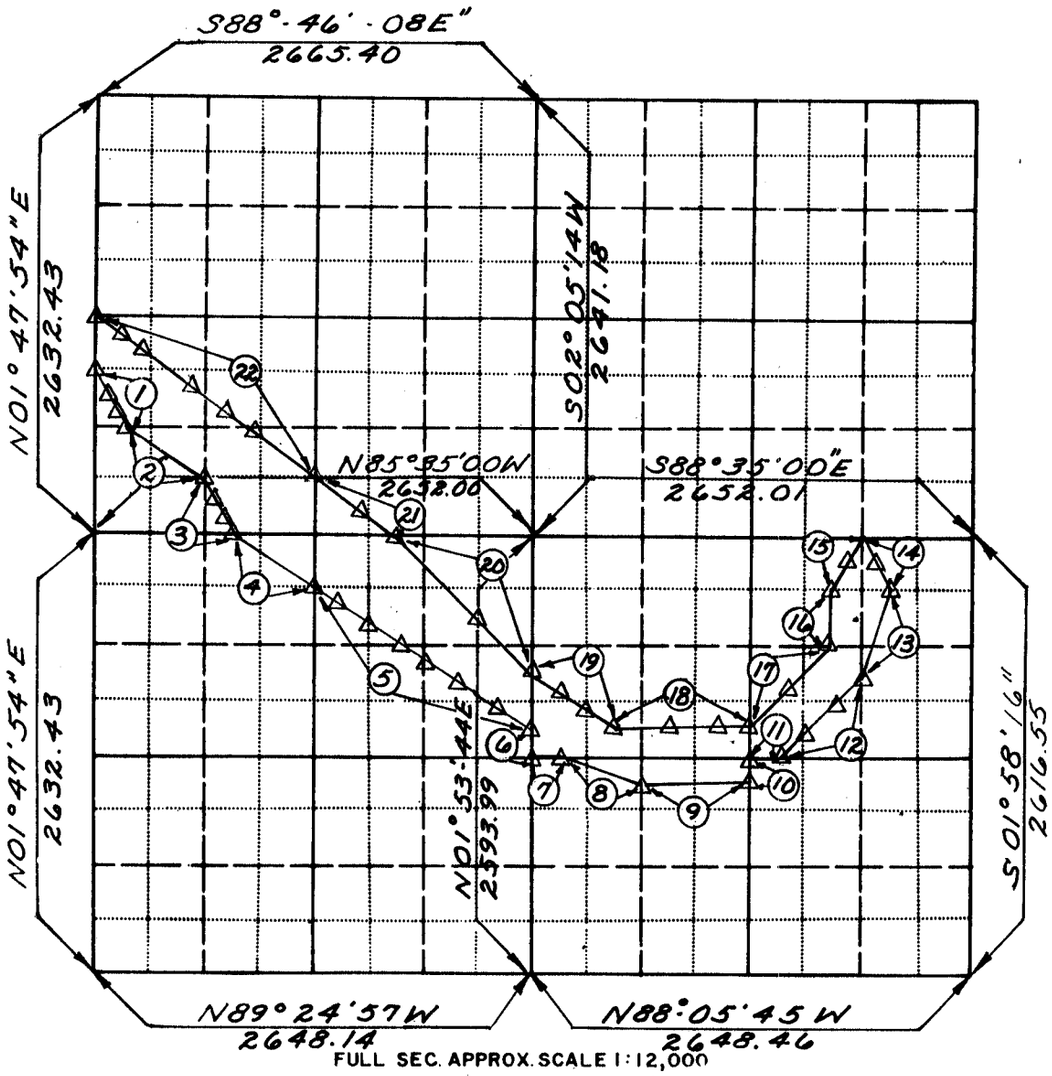

FULL SEC. APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1012-2			404.072.79	1.608.493.58	In Lake
	1		S25-03-14E	202.01			
		1012-2A		338.06	403.889.79	1.608.579.13	
	1		S25-03-14E	120.37			
		1012-2B		354.04	403.780.75	1.608.630.10	
	1		S25-03-14E	45.04			
		1012-3		352.40	403.739.95	1.608.649.17	
	2		S54-59-34E	594.48			

Field Book No. 69D-5 Date: June 1969
69D-6
69D-8 (Levels)

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

_____
COUNTY, ARKANSAS

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 4

GN MN

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 14, T 9N, R 22W COUNTY JOHNSON

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1012-4		351.68	403,399.08	1,609,135.88	
	3		S24-56-20E	203.54			
		1012-4A		352.72	403,214.67	1,609,221.62	
	3		S24-56-20E	49.89			
		1012-4B		355.40	403,169.43	1,609,242.66	
	3		S24-56-20E	114.00			
		1012-5		368.11	403,066.15	1,609,290.69	
	4		S55-09-55E	205.86			
		1012-5A		384.55	402,948.58	1,609,459.58	
	4		S55-09-55E	199.87			
		1012-5B		385.37	402,834.40	1,609,623.63	
	4		S55-09-55E	187.05			
		1012-6 = 1013-1		387.22	402,727.59	1,609,777.10	
	5		S57-06-10E	138.44			
		1013-1A		391.86	402,652.41	1,609,893.30	
	5		S57-06-10E	178.66			
		1013-1B		395.18	402,555.40	1,610,043.26	
	5		S57-06-10E	319.68			
		1013-1C		412.78	402,381.82	1,610,311.58	
	5		S57-06-10E	189.05			
		1013-1D		392.78	402,279.17	1,610,470.26	
	5		S57-06-10E	245.03			
		1013-1E		367.72	402,146.13	1,610,675.93	
	5		S57-06-10E	230.78			
		1013-1F		363.33	402,020.84	1,610,869.65	
	5		S57-06-10E	245.23			
		1013-2 = 1014-1-1		357.05	401,887.71	1,611,075.50	
	6		S01-36-44W	163.48			
		1014-1-2			401,724.29	1,611,070.90	In Steep Bluff
	7		S88-20-22E	165.64			
		1014-1-3 = 1016-1			401,719.49	1,611,236.47	In Steep Bluff
	8		S70-12-30E	522.12			
		1016-2			401,542.70	1,611,727.75	In Steep Bluff
	9		N85°15'30E	666.20			

SHEET 2 of 4

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 14, T -9-N, R -22W COUNTY JOHNSON

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1016-3		412.40	401,597.77	1,612,391.67	
	10		N02-01-21E	81.43'			
		1016-4= 1015-1		357.89	401,679.23	1,612,394.55	
	11		S88-16-14E	165.64'			
		1015-2		387.10	401,674.23	1,612,560.15	
	12		N47-17-22E	326.04'			
		1015-2A		351.29'	401,895.58	1,612,799.95	
	12		N47-17-22E	257.46'			
		1015-2B		370.07	402,070.37	1,612,989.29	
	12		N47-17-22E	115.84'			
		1015-3		365.85	402,149.02	1,613,074.49	
	13		N20-39-36E	86.86'			
		1015-3A		363.38	402,230.38	1,613,105.17	
	13		N20-39-36E	431.26'			
		1015-4		399.34	402,634.34	1,613,257.49	
	14		N25-00-31W	137.25'			
		1015-4A		363.01	402,758.83	1,613,199.42	
	14		N24-34-42W	233.74'			
		1015-5			402,971.39	1,613,102.20	In Lake
	15		S28-20-51W	233.65'			
		1015-5A		353.44	402,765.76	1,612,991.26	
	15		S28-49-33W	137.25'			
		1015-6		359.28	402,645.64	1,612,925.15	
	16		S01-59-28W	326.19'			
		1015-7		353.20	402,319.99	1,612,913.84	
	17		S47-16-19W	386.13'			
		1015-7A		357.41	402,058.24	1,612,630.44	
	17		S47-16-19W	313.19'			
		1015-1-8 =1014-1-5		345.84	401,845.92	1,612,400.59	
	18		N88-19-37W	99.39'			
		1014-1-5A		349.18	401,848.83	1,612,301.27	
	18		N88-19-37W	323.14'			
		1014-1-5B		349.60	401,858.26	1,611,978.35	
	18		N88-19-37W	405.73'			

SHEET 3 of 4

SWL FORM 136
REVISED FEB. 66

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 14, T 9N, R 22W COUNTY JOHNSON

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1014-1-6		348.10	401,870.08	1,611,572.90	
	19		N55-07-53W	147.72'			
		1014-1-6A		345.09	401,954.57	1,611,451.65	
	19		N55-07-53W	161.96'			
		1014-1-6B		352.09	402,047.16	1,611,318.77	
	19		N55-07-53W	282.27'			
		1014-1-7= 1013-3		355.27	402,208.57	1,611,087.08	
	20		N43-57-44W	478.20'			
		1013-3A		357.40	402,552.98	1,610,754.95	
	20		N43-57-44W	676.23			
		1013-4= 1014-2-1		383.45	403,039.99	1,610,285.25	
	21		N54-52-08W	287.47			
		1014-2-1A		None	403,205.48	1,610,050.06	
	21		N54-52-08W	306.56			
		1014-2-2 =1012-7		380.16	403,381.95	1,609,799.25	
	22		N51-48-32W	424.91			
		1012-7A		368.12	403,644.80	1,609,465.17	
	22		N51-48-32W	229.21			
		1012-7B		364.68	403,786.59	1,609,284.95	
	22		N51-48-32W	369.02			
		1012-7C		None	404,015.90	1,608,995.54	
	22		N51-48-32W	371.71			
		1012-7D		356.45	404,245.71	1,608,703.38	
	22		N51-48-32W	66.64			
		1012-7E		351.31	404,286.93	1,608,650.98	
	22		N51-48-32W	186.80			
		1012-8= 1011-4		359.15	404,402.46	1,608,504.10	

SHEET 4 of 4

SWL FORM 136
REVISED FEB. 66
