PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

PERFORMED UNDER CONTRACT NO. DA-03-050-CIVENG-66-50

SEC. 6, T-9-N, R-23-W COUNTY JOHNSON

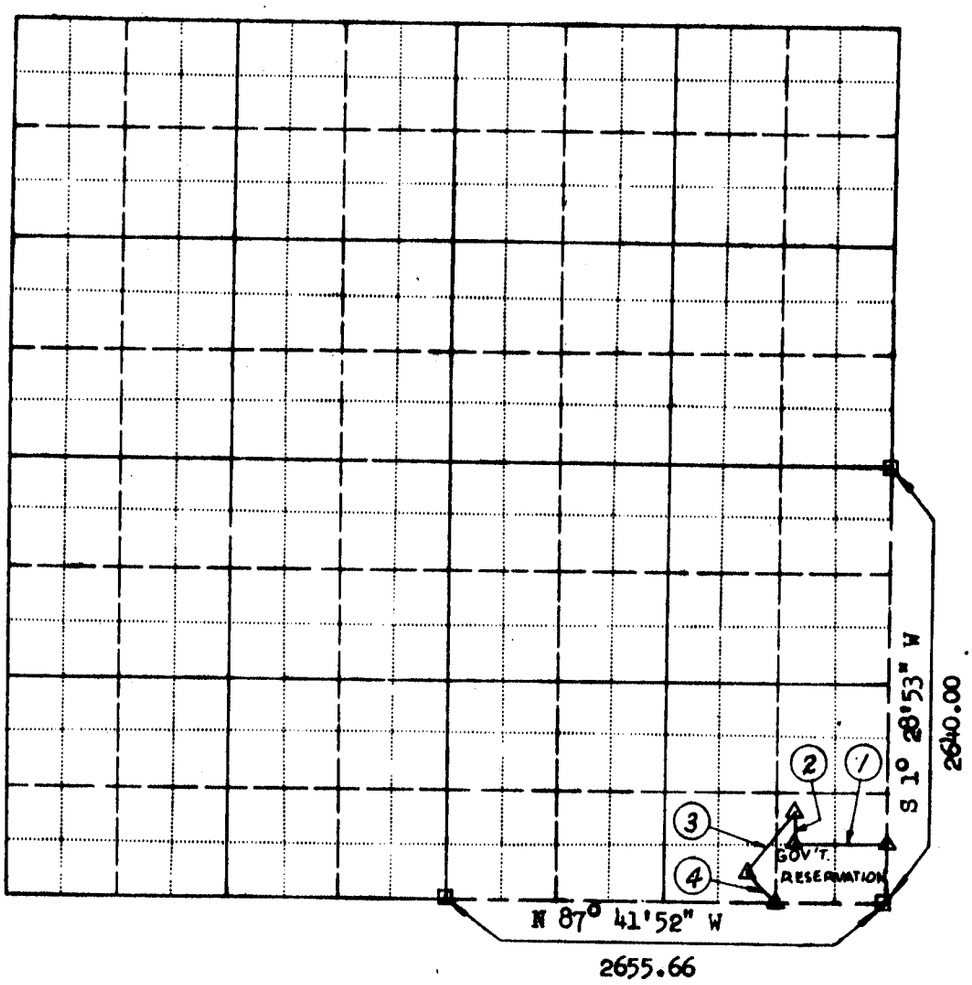

Rev. June 1968

APPROX. SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		1819-3		349.69	412,842.17	1,561,005.04	
	1		N87-41-56W	497.89			
		1819-4		349.17	412,862.16	1,560,507.55	
	2		N01-25-03E	165.00			
		1819-5		349.79	413,027.11	1,560,511.64	
	3		S47-02-40W	464.55			
		1819-6		350.26	412,710.55	1,560,171.64	
	4		S43-19-24E	235.90			

Field Book No. 65 D-7 Date: 5/12/66

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION 6, T-9-N, R-23-W.

JOHNSON COUNTY, ARKANSAS

Chester R. Phillips

PHILLIPS ENGINEERS INC.

Under the Supervision of

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 2

GN MN 0°-51'-47" 6°-47'

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED COR.
- # - OTHER

PARTIAL BOUNDARY SURVEYS
DARDANELLE RESERVOIR
ARKANSAS RIVER, ARKANSAS

SEC. 6, T -9-N, R -23-W COUNTY Johnson

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE	ELEVATION	POSITION		REMARKS
			GRID BEARING	DISTANCE	NORTH	EAST	
		1819-7 1818-1		352.41	412,538.93	1,560,333.49	

SHEET 2 of 2

SWL FORM 136
REVISED FEB. 66
