BOUNDARY SURVEYS
LAKE DARDANELLE
ARKANSAS RIVER, ARKANSAS

SECTION 18, T 9N, R 24W COUNTY JOHNSON

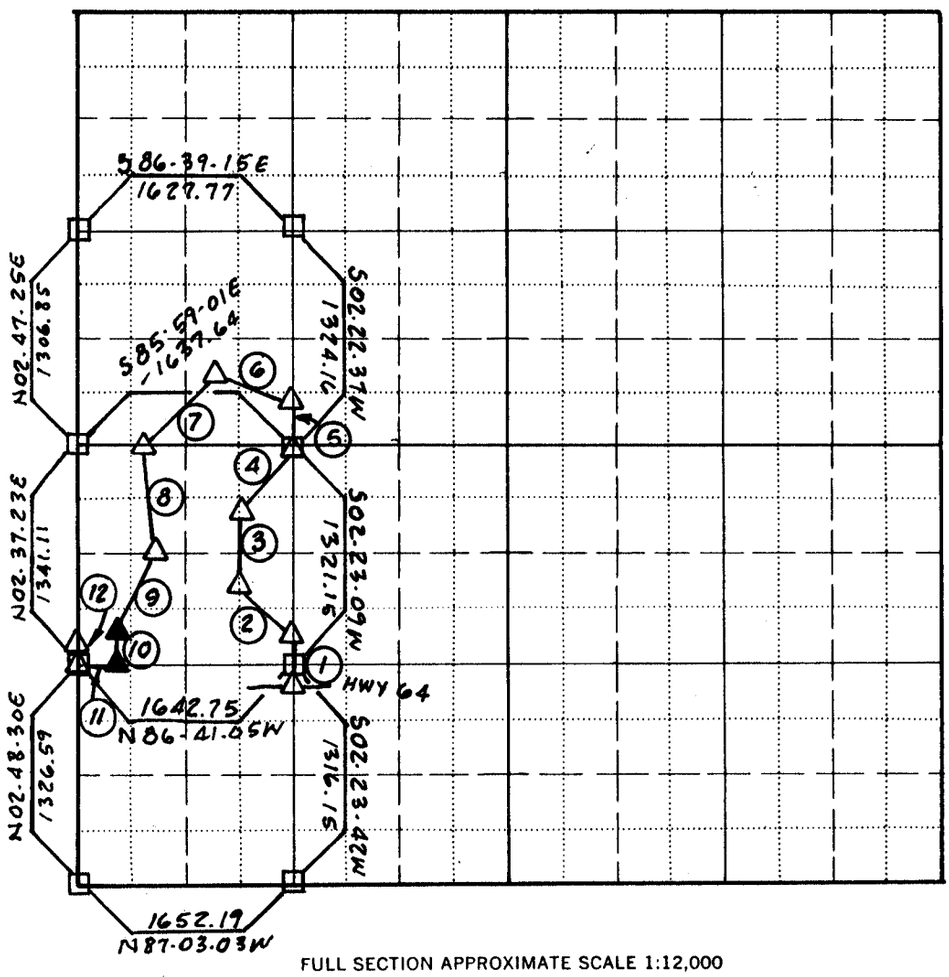

FULL SECTION APPROXIMATE SCALE 1:12,000

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	2510-1			—	—	℄ HWY NO MON. SET
1		N02-23-52E	—			
	2510-1A			404,803.16	1,524,513.84	TYP ■ ▥ MON. ON HWY R-O-W
1		N02-23-52E	196.79			
	2510-1B			404,999.74	1,524,522.17	TYPE ▥ MON.
1		N02-23-52E	117.31			
	2510-2			405,116.92	1,524,527.13	(")
2		N39-05-41W	249.29			

Field Book No. 70D-4&5 Date: 1970

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION _____, T _____, R _____.

COUNTY, ARKANSAS

SURVEYOR REG. NO.

U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 OF 2

GN MN

LEGEND

- ▲ MONUMENT TYPE 1
- △ MONUMENT TYPE 2
- ● FOUND I. P.
- ○ SET I. P.
- ■ FOUND STONE
- □ COMPUTED CORNER
- ✳ OTHER

BOUNDARY SURVEYS
LAKE DARDANELLE
ARKANSAS RIVER, ARKANSAS

SECTION 18 , T 9N , R 24W COUNTY JOHNSON

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	2510.2A			405,310.35	1,524,370.05	TYPE III MON.
2		N39.05.41W	203.44			
	2510.3			405,468.20	1,524,241.86	(")
3		N02.23.16W	242.67			
	2510.3A			405,710.60	1,524,252.09	(")
3		N02.23.16W	179.97			
	2510.4			405,890.38	1,524,259.68	(")
4		N38.17.17E	488.17			
	2510.5= 2513.1			406,273.55	1,524,562.16	(")
5		N02.27.51E	299.80			
	2513.2			406,573.07	1,524,575.05	(")
6		N74.08.33W	92.08			
	2513.2A			406,597.09	1,524,486.22	(")
6		N74.51.37W	104.28			
	2513.2B			406,624.33	1,524,385.56	NO MON. SET
6		N74.51.37W	104.28			
	2513.2C			406,651.56	1,524,284.90	TYPE III MON.
6		N71.51.05W	197.23			
	2513.3			406,703.06	1,524,094.62	(")
7		S56.51.22W	660.92			
	2513.4= 2510.6			406,341.57	1,523,541.55	(")
8		S06.48.10E	607.29			
	2510.7			405,738.43	1,523,613.77	(")
9		S27.51.56W	582.80			
	2510.8			405,223.21	1,523,341.37	TYPE I MON.
10		S02.30.56W	200.03			
	2510.9= 2509.1			405,023.37	1,523,332.59	(")
11		N86.35.16W	451.77			
	2509.2			405,050.26	1,522,881.62	TYPE III MON.
12		N06.50.24E	47.68			
	2509.3			405,097.59	1,522,887.32	(")

SHEET 2 OF 2

SWL FORM 136
REVISED OCT. 1971
