PARTIAL BOUNDARY SURVEY
TABLE ROCK LAKE
WHITE RIVER, ARK. AND MO.

SEC. 30, T 23N., R 23W COUNTY STONE

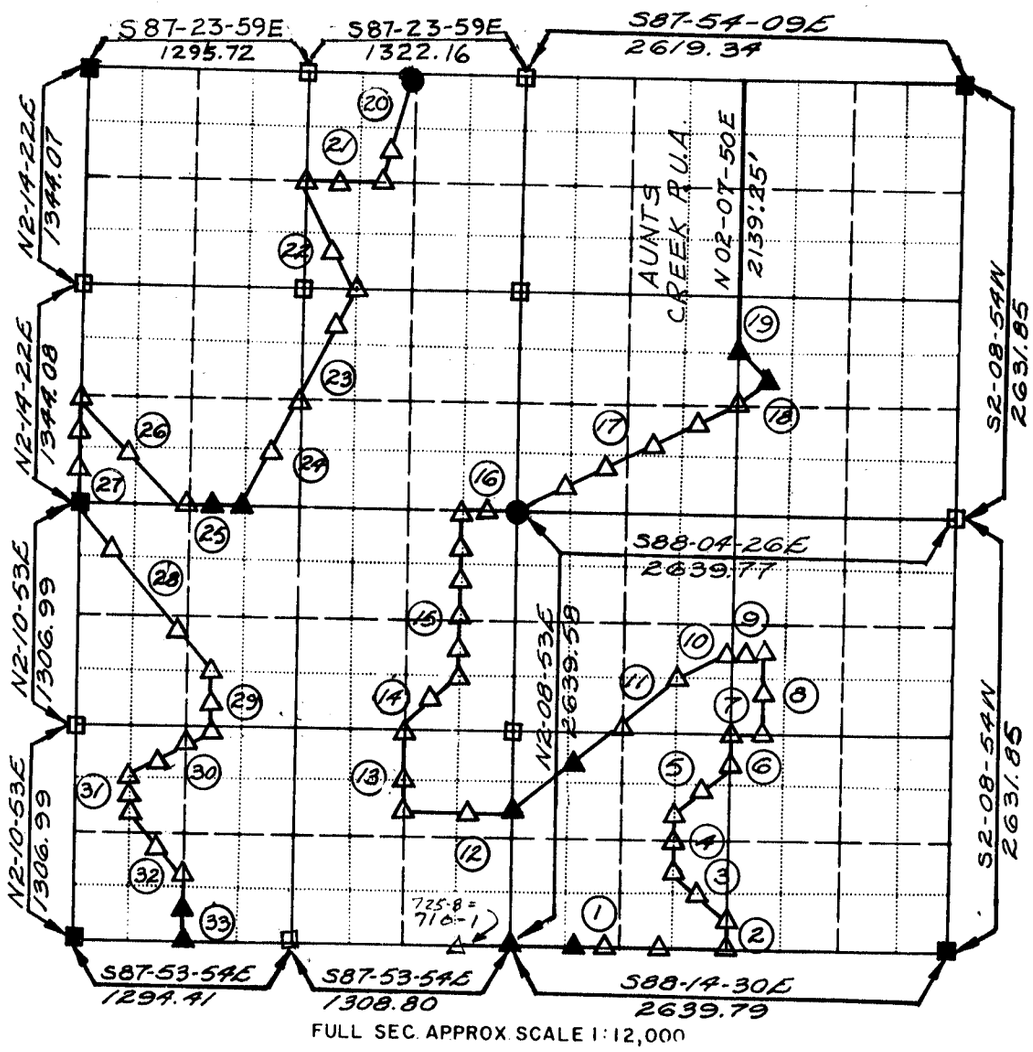

FULL SEC. APPROX. SCALE 1:12,000

MO. CENTRAL ZONE

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		711-3-1=	710-2	960.49	302,784.78	217,589.60	EXIST ¼ COR. STONE T-1
	*1		S88-11-51E	444.00			
		711-3-1A		988.08	302,770.81	218,033.38	T-1
	1		S88-11-51E	122.18			
		711-3-1B		983.98	302,766.97	218,155.50	T-3
	1		S88-11-51E	367.20			
		711-3-1C		954.17	302,755.42	218,522.52	T3
	1		S88-11-51E	387.18			

Field Book No. 72-TR20 / 72-TR11 ~~71~~ / 72-TR15 Date: JULY 1972

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION 30, T 23N., R 23W.

STONE COUNTY, MISSOURI

Bruce R. Slack

BRUCE R. SLACK L.S. 1466.

TOWILL, INC.
UNDER THE SUPERVISION OF
U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 1 of 8

GN MN 0°35'18" 7°30'E

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER

PARTIAL BOUNDARY SURVEYS
TABLE ROCK LAKE
WHITE RIVER, ARK. AND MO.

SEC. 30, T 23N., R 23W COUNTY STONE

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION / NORTH	POSITION / EAST	REMARKS
		711-3-2		926.07	302,743.24	218,909.51	YIELD 1/2" BAR T-3
	*2		N2-14-32E	164.54			
		711-3-3		935.90	302,907.65	218,915.95	YIELD 1/2" BAR T-3
	*3		N42-57-11W	303.67			
		711-3-3A		940.13	303,129.91	218,709.03	T-3
	3		N42-57-11W	162.15			
		711-3-4		932.42	303,248.59	218,598.54	YIELD 1/2" BAR T-3
	*4		N2-14-19E	144.89			
		711-3-4A		940.89	303,393.37	218,604.20	T-3
	4		N2-14-19E	184.86			
		711-3-5		937.19	303,578.09	218,611.42	YIELD 1/2" BAR T-3
	*5		N47-07-39E	243.38			
		711-3-5A		945.54	303,743.68	218,789.78	T-3
	5		N47-07-39E	223.86			
		711-3-6		939.96	303,895.99	218,953.85	YIELD 1/2" BAR T-3
	*6		N2-11-42E	164.89			
		712-1-1		922.31	304,060.76	218,960.16	RESET MAP NB7 T-3
	*7		S87-58-43E	164.99			
		712-1-2		939.26	304,054.94	219,125.05	YIELD 1/2" BAR T-3
	*8		N2-10-21E	170.43			
		712-1-2A		924.30	304,225.25	219,131.51	T-3
	8		N2-10-21E	323.37			
		712-1-3		927.35	304,548.38	219,143.77	YIELD 1/2" BAR T-3
	*9		N88-03-06W	78.93			
		712-1-3A		946.92	304,551.07	219,064.88	T-3
	9		N88-03-06W	86.07			
		711-3-8		957.78	304,553.99	218,978.86	YIELD 1/2" BAR T-3
	*10		S65-29-10W	369.59			
		711-3-9		956.16	304,400.64	218,642.59	YIELD 1/2" BAR T-3
	*11		S52-17-54W	635.43			
		711-3-9A		951.85	304,012.04	218,139.83	T-3
	11		S52-17-54W	275.64			
		711-3-9B		954.38	303,843.48	217,921.74	T-1
	11		S52-17-54W	379.16			

* DENOTES DEVIATION FROM SECTIONAL BREAKDOWN LINE SEE SHEET 6 OF 7

PARTIAL BOUNDARY SURVEYS
TABLE ROCK LAKE
WHITE RIVER, ARK. AND MO.

SEC. 30, T 23N., R 23W COUNTY STONE

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION / NORTH	POSITION / EAST	REMARKS
		710-1		937.52	303,611.60	217,621.75	YIELD 1/2" BAR T-1
	12		N88-06-37W	295.37			
		710-1A		949.07	303,621.34	217,326.54	T-3
	12		N88-06-37W	366.64			
		710-2		924.77	303,633.43	216,960.10	YIELD 3/8" BAR T-3
	*13		N2-11-48E	207.69			
		710-2A		935.61	303,840.97	216,968.06	YIELD 3/8" BAR T-3
	13		N2-11-48E	285.43			
		710-3		926.29	304,126.19	216,979.00	REF. MAPS T-3
	14		N46-56-35E	186.62			
		710-3A		934.93	304,253.59	217,115.37	T-3
	14		N46-56-35E	281.62			
		710-4		935.72	304,445.84	217,321.16	MAP T-3 N-40, N-55
	*15		N2-11-48E	236.75			
		710-4A		937.80	304,682.42	217,330.23	T-3
	15		N2-11-48E	218.52			
		710-4B		954.35	304,900.77	217,338.61	T-3
	15		N2-11-48E	201.23			
		710-4C		956.96	305,101.86	217,346.32	T-3
	15		N2-11-48E	182.63			
		710-4D		950.80	305,284.35	217,353.32	T-3
	15		N2-11-48E	150.53			
		710-5		936.80	305,434.77	217,359.08	YIELD 5/8" BAR T-3
	*16		S87-52-00E	173.76			
		710-5A		950.95	305,428.30	217,532.72	T-3
	16		S87-52-00E	155.92			
		711-2-1		959.54	305,422.50	217,688.53	YIELD 1/2" BAR
	*17		N65-29-23E	294.41			
		711-2-1A		950.41	305,544.64	217,956.41	T-3
	17		N65-29-23E	395.33			
		711-2-1B		935.84	305,708.64	218,316.12	T-3
	17		N65-29-23E	163.95			
		711-2-1C		926.81	305,776.66	218,465.29	T-3
	17		N65-29-23E	324.28			

* DENOTES DEVIATION FROM SECTIONAL BREAKDOWN LINE. SEE SHEET #6 OF 7

PARTIAL BOUNDARY SURVEYS
TABLE ROCK LAKE
WHITE RIVER, ARK. AND MO.

SEC. 30, T 23N., R 23W COUNTY STONE

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		711-2-10		927.08	305,911.19	218,760.35	T-3
	17		N65-29-23E	300.29			
		712-2-1		935.23	306,035.76	219,033.58	YIELD 5/8" BAR T-3
	*18		N47-04-16E	233.40			
		712-2-2		929.49	306,194.73	219,204.48	YIELD 5/8" BAR T-1
	*19		N42-56-51W	232.73			
		712-2-3		950.87	306,365.08	219,045.91	CORPS MON. T-1
		710-7		936.08	308,084.04	217,151.87	EXIST 1/2" BAR
	*20		S16-31-57W	600.40			
		710-7A		934.45	307,508.46	216,981.02	T-3
	20		S16-31-57W	81.38			
		710-8		930.83	307,430.44	216,957.86	HELD BREAKDOWN T-3
	*21		N87-54-00W	196.39			
		710-8A		942.45	307,437.64	216,761.60	T-3
	21		N87-54-00W	296.05			
		710-9		934.90	307,448.49	216,465.75	T-3
	22		S24-00-49E	484.40			
		710-9A		938.32	307,006.02	216,662.88	T-3
	22		S24-00-49E	251.12			
		710-10		931.70	306,776.63	216,765.07	T-3
	23		S28-35-57W	222.61			
		710-10A		937.76	306,581.18	216,658.51	T-3
	23		S28-35-57W	521.79			
		737-1		943.86	306,123.06	216,408.75	T-3
	24		S28-10-19W	368.09			
		737-1A		945.68	305,798.58	216,234.97	T-3
	24		S28-10-19W	376.92			
		737-2		931.47	305,466.30	216,057.01	T-1
	25		N88-27-44W	173.61			
		737-2A		935.72	305,470.96	215,883.46	T-1
	25		N88-27-44W	149.62			

* DENOTES DEVIATION FROM SECTIONAL BREAKDOWN LINE. SEE SHEET #7 OF 7

PARTIAL BOUNDARY SURVEYS
TABLE ROCK LAKE
WHITE RIVER, ARK. AND MO.

SEC. 30, T 23N., R 23W COUNTY STONE

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE GRID BEARING	ELEVATION DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		737-3		927.11	305,474.98	215,733.90	HOLD BREAKDOWN T-3
	26		N41-59-12W	543.15			
		737-3A		937.48	305,878.70	215,370.56	T-3
	26		N41-59-12W	383.63			
		737-4		935.29	306,163.85	215,113.92	T-3
	27		S2-14-22W	454.39			
		737-4A		954.89	305,709.81	215,096.16	T-3
	27		S2-14-22W	151.20			
		737-4B		954.16	305,558.72	215,090.25	T-3
	27		S2-14-22W	66.45			
		737-5		945.91	305,492.33	215,087.66	EXIST STONE
	28		S37-30-22E	298.28			
		737-5A		960.42	305,255.71	215,269.27	T-3
	28		S37-30-22E	731.82			
		737-5B		951.87	304,675.16	215,714.83	T-3
	28		S37-30-22E	235.78			
		737-6		936.23	304,488.12	215,858.38	HOLD BREAKDOWN T-3
	29		S2-09-38W	177.57			
		737-6A		941.39	304,310.68	215,851.69	T-3
	29		S2-09-38W	150.17			
		737-7		936.53	304,160.61	215,846.03	T-3
	30		S57-56-14W	222.76			
		737-7A		946.76	304,042.36	215,657.25	T-3
	30		S57-56-14W	182.02			
		737-7B		942.46	303,945.74	215,502.99	T-3
	30		S57-56-14W	182.01			
		737-8		935.61	303,849.12	215,348.74	T-3
	31		S2-10-23W	77.02			
		737-8A		924.48	303,772.15	215,345.82	T-3
	31		S2-10-23W	86.55			
		737-9		938.53	303,685.66	215,342.54	T-3
	32		S42-35-46E	302.85			
		737-9A		945.36	303,462.73	215,547.52	T-3
	32		S42-35-46E	156.55			

PARTIAL BOUNDARY SURVEYS
TABLE ROCK LAKE
WHITE RIVER, ARK. AND MO.

SEC. 30, T 23N., R 23W COUNTY STONE

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
		737-10		942.92	303,347.48	215,653.47	HELD BREAKDOWN T-3
	33		S0-29-42W	169.59			
		737-10A		955.75	303,177.90	215,652.00	T-1
	33		S0-29-42W	330.42			
		724-3-1		965.09	302,847.49	215,649.15	
	*						
		SECTIONAL BREAKDOWN LINE					
		711-3-1			302,784.78	217,589.60	
	1		S88-14-30E	1319.90			
		711-3-2			302,744.28	218,908.88	
	2		N2-08-53E	164.73			
		711-3-3			302,908.90	218,915.05	
	3		N43-04-32W	464.83			
		711-3-4			303,248.43	218,597.59	
	4		N2-08-53E	329.58			
		711-3-5			303,577.79	218,609.94	
	5		N47-01-24E	467.67			
		711-3-6			303,896.59	218,952.10	
	6		N2-08-53E	164.73			
		712-1-1			304,061.21	218,958.27	
	7		S88-09-28E	164.99			
		712-1-2			304,055.91	219,123.17	
	8		N2-08-53E	494.11			
		712-1-3			304,549.66	219,141.69	
	9		N88-07-35W	164.99			
		711-3-8			304,555.06	218,976.80	
	10		S65-23-25W	369.54			
		711-3-9			304,401.17	218,640.82	
	11		S52-10-35W	291.69			
		710-1			303,609.07	217,620.52	
	12		N88-04-27W	654.40			

PARTIAL BOUNDARY SURVEYS
TABLE ROCK LAKE
WHITE RIVER, ARK. AND MO.

SEC. 30, T 23N., R 23W COUNTY STONE

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION / NORTH	POSITION / EAST	REMARKS
		710-2			303,631.05	216,966.48	
	13		N2-08-53E	493.71			
		710-3			304,124.41	216,984.98	
	14		N46-46-50E	465.72			
		710-4			304,443.34	217,324.37	
	15		N2-08-53E	988.64			
		710-5			305,431.28	217,361.43	
	16		S88-27-43E	327.22			
		711-2-1			305,422.50	217,688.53	
	17		N65-29-03E	1479.80			
		712-2-1			306,036.53	219,034.92	
	18		N47-08-54E	233.66			
		712-2-2			306,195.45	219,206.22	
	19		N42-47-54W	232.07			
		712-2-3			306,365.73	219,048.55	
		710-7			308,084.07	217,151.01	
	20		S16-27-46W	681.57			
		710-8			307,430.44	216,957.86	HELD BREAKDOWN
		737-10			303,347.48	215,653.47	HELD BREAKDOWN
	33		S2-09-53W	491.31			
		724-3-1			302,856.52	215,634.91	

PARTIAL BOUNDARY SURVEY
TABLE ROCK LAKE
WHITE RIVER, ARK. AND MO.

SEC. 30, T 23N., R 23W COUNTY STONE

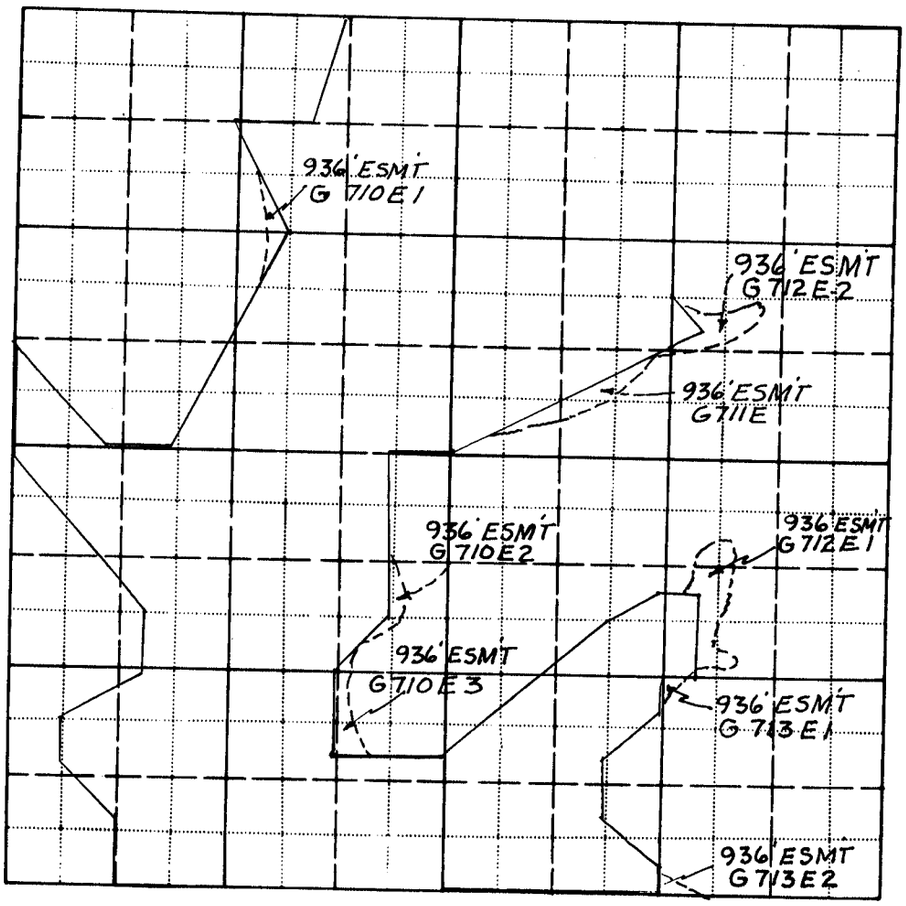

FULL SEC. APPROX SCALE 1:12,000

TRACT NO.	COURSE NO.	MONUMENT NO.	ANGLE / GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS

Field Book No. 72 TR 23 Date: AUG. 72

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION 30, T 23 N., R 23W.

STONE COUNTY, MISSOURI

Bruce R. Slack

BRUCE R. SLACK L.S. 1466.

TOWILL, INC.
UNDER THE SUPERVISION OF
U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK
CORPS OF ENGINEERS

SHEET 8 of 8

GN MN
0°35'18" 7°30'E

LEGEND

- ▲ - MONUMENT TYPE 1
- △ - MONUMENT TYPE 3
- ● - FOUND I. P.
- ○ - SET I. P.
- ■ - FOUND STONE
- □ - COMPUTED CORNER
- ✱ - OTHER
