BOUNDARY SURVEYS
TABLE ROCK LAKE
WHITE RIVER, ARKANSAS & MISSOURI

CONTRACT NO. DACW 03 - 72-C-0133

SECTION 10, T 24 N., R 24 W. COUNTY STONE

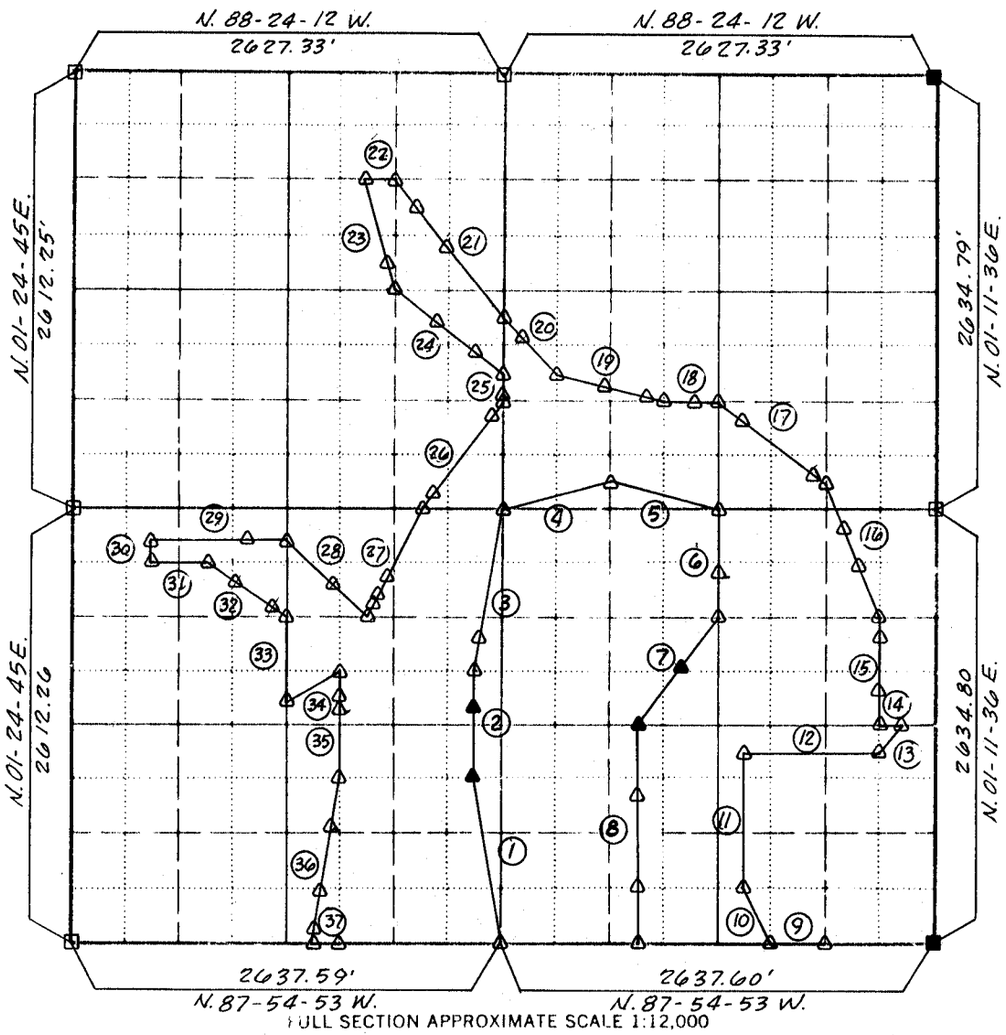

FULL SECTION APPROXIMATE SCALE 1:12,000

MO. CENTRAL ZONE

COURSE NO	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	Y2504-7		919.76	350,769.49	203,476.44	Monument type 3
1		N.08-11-00 W.	999.47			
	Y2504-8		924.49	351,758.78	203,334.17	Monument type 1
2		N.01-18-40 E.	417.05			
	Y2504-8A		933.22	352,175.72	203,343.71	Monument type 1
2		N.01-18-40 E.	238.65			
	Y2504-9		930.22	352,414.31	203,349.17	Monument type 3
3		N.10-49-20 E.	207.87			

CERTIFICATE OF SURVEY

I HEREBY CERTIFY THAT THE ABOVE PLAT IS A TRUE AND CORRECT REPRESENTATION OF THE SURVEY MADE IN SECTION 10, 24 N. & 24 W

Field Book No. 72-TR-88 Date: MARCH 1974
72-TR-82 OCT. 1973
72-TR-84 JAN 1974

GHQ, INC.
CONSULTING ENGINEERS & LAND SURVEYORS
UNDER THE SUPERVISION OF
U. S. ARMY ENGINEER DISTRICT, LITTLE ROCK

GN MN

LEGEND
▲ MONUMENT TYPE 1
△ MONUMENT TYPE 3
● FOUND I.P.
○ SET I.P.

BOUNDARY SURVEYS
TABLE ROCK LAKE
WHITE RIVER, ARKANSAS & MISSOURI

SECTION 10 , T 24 N. , R 24 W. COUNTY STONE

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	Y2504-9A		932.93	352,618.49	203,388.20	Monument type 3
3		N.10-49-20E.	787.84			
	Y2504-10		925.62	353,392.32	203,536.13	Monument type 3
4		N. 77-48-22 E.	676.71			
	Y2504-11		928.61	353,535.25	204,197.57	Monument type 3
5		S.74-11-06 E.	679.85			
	Y 2504-12		925.16	353,349.97	204,851.69	Monument type 3
6		S.01-15-10 W.	361.34			
	Y2504-12A		943.61	352,988.71	204,843.79	Monument type 3
6		S.01-15-10 W.	295.95			
	Y2504-13		942.72	352,692.84	204,837.32	Monument type 3
7		S.38-26-39W.	400.00			
	Y2504-13A		939.30	352,379.56	204,588.62	Monument type 1
7		S.38-26-39 W.	417.32			
	Y2504-14		938.06	352,052.71	204,329.15	Monument type 1
8		S.01-16-23 W.	424.48			
	Y2504-14A		926.56	351,628.33	204,319.72	Monument type 3
8		S.01-16-23 W.	518.27			
	Y2504-14B		933.79	351,110.19	204,308.20	Monument type 3
8		S.01-16-23 W.	206.69			
	Y2504-14C		958.94	350,903.55	204,303.61	Monument type 3
8		S.01-16-23 W.	164.08			
	Y2504-15		963.12	350,739.51	204,299.97	Monument type 3
	Y2505-7		925.49	350,697.22	205,453.56	RE-SET 7/9/81 Monument type 3
9		N.87-52-50W.	329.70			
	Y2505-8		929.00	350,709.41	205,124.05	RE-SET 7/9/81 Monument type 3
10		N.25-12-03W	369.97			
	Y2505-9		929.56	351,044.20	204,966.51	RE-SET JULY 81 Monument type 3
11		N.01-15-15E.	821.96			
	Y2505-10		928.56	351,866.03	204,984.50	RE-SET JULY 81 Monument type 3
12		S.88-01-16E.	823.54			
	Y2505-11		936.66	351,837.59	205,807.47	RE-SET JULY 81 Monument type 3
13		N.46-34-48E.	231.32			
	Y2502-1		929.25	351,996.59	205,975.49	RE-SET JULY 81 Monument type 3
14		N.88-02-07W.	164.69			
	Y2502-2		928.23	352,002.23	205,810.88	RE-SET JULY 81 Monument type 3
15		N.01-00-56E.	175.69			
	Y2502-3A		[illegible]	[illegible]	[illegible]	RE-SET JULY 81

BOUNDARY SURVEYS
TABLE ROCK LAKE
WHITE RIVER, ARKANSAS & MISSOURI

SECTION 10 , T 24 N. , R 24 W. COUNTY STONE

COURSE NO	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
15		N.01-00-56 E.	304.31			
	Y2502-2B			352,482.16	205,819.39	RE-SET JULY 81 Monument type 3
15		N.01-00-56 E.	176.27			
	Y2502-3		1025.64	352,658.41	205,822.51	Monument type 3
16		N.20-29-38 W.	344.05			
	Y2502-3A		999.49	352,983.44	205,703.89	Monument type 3
16		N.20-29-38 W.	250.04			
	Y2502-3B		1024.33	353,217.65	205,616.35	Monument type 3
16		N.20-29-38 W.	295.60			
	Y2502-4		1076.61	353,494.54	205,512.86	Monument type 3
17		N.51-35-05 W.	100.01			
	Y2502-4A		1076.50	353,556.68	205,434.50	Monument type 3
17		N.51-35-05 W.	536.23			
	Y2502-4B		1042.33	353,889.87	205,014.35	Monument type 3
17		N.51-35-05 W.	190.02			
	Y2501-1		1084.02	354,007.94	204,865.46	Monument type 3
18		N.88-15-34 W.	133.28			
	Y2501-1A		1088.62	354,011.99	204,732.25	Monument type 3
18		N.88-15-34 W.	195.62			
	Y2501-2		1047.82	354,017.93	204,536.72	Monument type 3
19		N.74-17-05 W.	79.11			
	Y2501-2A		1041.56	354,039.36	204,460.56	Monument type 3
19		N.74-17-05 W.	288.73			
	Y2501-2B		963.45	354,117.57	204,182.63	Monument type 3
19		N.74-17-05 W.	311.48			
	Y2501-3		940.55	354,201.93	203,882.79	Monument type 3
20		N.43-35-12 W.	319.97			
	Y2501-3A		950.81	354,433.70	203,662.18	Monument type 3
20		N.43-35-12 W.	146.38			
	Y2500-1-1		954.31	354,539.72	203,561.26	Monument type 3
21		N.37-18-55 W.	545.30			
	Y2500-1-1A		966.91	354,973.41	203,230.70	Monument type 3
21		N.37-18-55 W.	328.70			
	Y2500-1-1B		987.22	355,234.83	203,031.44	Monument type 3
21		N.37-18-55 W.	180.01			
	Y2500-1-2		980.13	355,377.99	202,922.32	Monument type 3
22		N.88-22-54 W.	164.29			
	Y2500-1-3		930.64	355,382.63	202,758.10	Monument type 3
22		N.12-46-54 E.	[illegible]			

BOUNDARY SURVEYS
TABLE ROCK LAKE
WHITE RIVER, ARKANSAS & MISSOURI

SECTION 10 , T 24 N. , R 24 W. COUNTY STONE

COURSE NO.	MONUMENT NO.	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
	Y2500-1-3A		982.29	354,895.40	202,868.60	Monument type 3
23		S.12-46-44 E.	176.66			
	Y2500-1-4		1032.03	354,723.11	202,907.68	Monument type 3
24		S. 51-41-05 E.	336.67			
	Y2500-1-4A		996.35	354,514.37	203,171.83	Monument type 3
24		S.51-41-05 E.	299.97			
	Y2500-1-4B		965.84	354,328.39	203,407.19	Monument type 3
24		S.51-41-05 E.	187.26			
	Y2500-1-5		963.08	354,212.28	203,554.12	Monument type 3
25		S.01-15-14 W.	128.73			
	Y2500-1-5A		1006.71	354,083.59	203,551.30	Monument type 3
25		S01-15-14 W.	35.22			
	Y2500-2-1		1008.21	354,048.38	203,550.53	Monument type 3
26		S.38-25-03 W.	44.96			
	Y2500-2-1A		1024.35	354,013.15	203,522.59	Monument type 3
26		S.38-25-03 W.	772.08			
	Y2503-1		946.97	353,408.23	203,042.83	Monument type 3
27		S.28-06-48 W.	468.78			
	Y2503-1A		980.54	352,994.76	202,821.93	Monument type 3
27		S.28-06-48 W.	75.68			
	Y2503-1B		997.87	352,928.01	202,786.27	Monument type 3
27		S.28-06-48 W.	67.66			
	Y2503-1C		991.87	352,868.33	202,754.39	Monument type 3
27		S.28-06-48 W.	118.29			
	Y2503-2		935.06	352,764.00	202,698.65	Monument type 3
28		N.43-32-15 W.	279.63			
	Y2503-2A		968.82	352,966.70	202,506.03	Monument type 3
28		N.43-32-15 W.	419.94			
	Y2503-3		981.45	353,271.13	202,216.76	Monument type 3
29		N.88-08-28 W.	253.81			
	Y2503-3A		941.43	353,279.36	201,963.09	Monument type 3
29		N.88-08-28 W.	568.9			
	Y2503-4		926.87	353,297.82	201,394.47	Monument type 3
30		S.01-23-38 W.	163.40			
	Y2503-5		984.24	353,134.47	201,390.50	Monument type 3
31		S.88-07-28 E.	329.14			
	Y2503-6		965.43	353,123.69	201,719.46	Monument type 3
32		S.54-44-40 E.	216.93			

BOUNDARY SURVEYS
TABLE ROCK LAKE
WHITE RIVER, ARKANSAS & MISSOURI

SECTION 10 , T 24 N. , R 24 W. COUNTY STONE

COURSE NO	MONUMENT NO	GRID BEARING	ELEVATION / DISTANCE	POSITION NORTH	POSITION EAST	REMARKS
32		S.54-44-40 E.	280.4			
	Y2503-6B		983.42	352,836.61	202125.59	Monument type 3
32		S.54-44-40 E.	97.40			
	Y2503-7		969.50	352,780.38	202,205.13	Monument type 3
33		S.01-21-38 W.	490.85			
	Y2503-8		997.56	352,289.67	202,193.47	Monument type 3
34		N.65-24-14 E.	366.24			
	Y2503-9		960.36	352,442.11	202,526.48	Monument type 3
35		S.01-20-48 W.	142.25			
	Y2503-9A		987.98	352,299.90	202,523.14	Monument type 3
35		S.01-20-48 W.	72.10			
	Y2503-9B		991.67	352,227.81	202,521.44	Monument type 3
35		S.01-20-48 W.	155.00			
	Y2503-9C		981.17	352,072.85	202,517.80	Monument type 3
35		S.01-20-48 W.	285.47			
	Y2503-10		932.73	351,787.47	202,511.09	Monument type 3
36		S.10-53-48 W.	281.03			
	Y2503-10A		943.49	351,511.50	202,457.96	Monument type 3
36		S.10-53-48 W.	401.46			
	Y2503-10B		1002.71	351,117.28	202,382.07	Monument type 3
36		S.10-53-48 W.	239.81			
	Y2503-10C		989.11	350,881.80	202,336.74	Monument type 3
36		S.10-53-48 W.	71.57			
	Y2503-11		1025.75	350,811.52	202,323.21	Monument type 3
37		S.87-54-28 E.	164.85			
	Y2504-21		924.71	350,805.50	202,487.95	Monument type 3
